



SIPL/Engg/23-24/004

To,

Ms. Prachi Gangwar, IFS (Adl. Charge)
Deputy Director General of Forests (C),
Ministry of Env., Forest and Climate Change,
Integrated Regional Office, Jaipur, A-209&218,
Aranya Bhawan, Mahatma Gandhi Road,
Jhalana Institutional Area, Jaipur – 304002, Rajasthan

Subject: Six Monthly Compliance report (October 2022 to March 2023) of Select CITYWALK-Commercial Complex at A-3 & P1B, District Centre, Saket, New Delhi.

Dear Sir

Kindly find attached the six monthly Compliance report (October 2022 to March 2022) of Select CITYWALK — Commercial Complex at A-3 & P1B, District Centre, Saket, New Delhi with all necessary information regarding the same.

This is for your kind information and record please.

Thanking you,

Yours truly,

For Select Infrastructure Pvt. Ltd.

Pawan Sachdeva Company Secretary

#### Annexure:

- 1. Consent to Establish 2013
- Consent to Operate 2022
- 3. Consent to Establish 2019

Select Infrastructure Private Limited

(Regd.Office) Seawoods Grand Central Mall, Management Office, Lower Ground Floor, Plot No. R-1, Sector 40, Node Nerul, Navi Mumbai, Thane Darave, Thane Maharashtra-400706 India
(Mall Office) 4th Floor, Select CITYWALK, A-3, District Centre, Saket, New Delhi – 110017 India
T +91 11 3050 3000 F +91 11 4211 4222 E contact@selectcitywalk.com W www.selectcitywalk.com
CIN No. U74999MH1979PTC404545



- 4. Fire NOC
- 5. Environment Clearance 2007
- 6. AAI Permission
- 7. DDA approval letter for expansion
- 8. Environment Clearance for Expansion 2019
- 9. Monitoring Reports
- 10. Adequacy of Rain Water Harvesting
- 11. MOU with M/s Chintan
- 12. Traffic Management Plan
- 13. Green Belt Development Plan
- 14. Structural Stability Certificate
- 15. Certificate from Electrical Inspector
- 16. Electricity Bill
- 17. Diesel Storage License
- 18. MOU for e-waste and hazardous waste
- 19. ECBC Report
- 20. Water Consumption details
- 21. Adequacy of STP
- 22. Energy Conservation Measures
- 23. Form -4 DPCC
- 24. Company Policy
- 25. EMP Expenditure
- 26. Advertisement in News Paper
- 27. Extension for Consent to establish
- Form and Challan of fees paid for Renewal of Consent to Operate and Consent to operate for new Area.
- 29. Installation certificate of retrofit pollution control device Chakra Shield in DG sets.



- 30. Test report of Chakra Shield as approved by CPCB approved laboratory
- 31. Occupancy- cum-completion certificate issued by Delhi development authority
- 32. CER expense (Apr22-Sep22) with details.
- 33. Form V for FY 2021-22.
- 34. Work completion certificate of Solar power system (102 KW).

Cc: Member Secretary - DPCC

## SIX MONTHLY COMPLIANCE REPORT OF

"Commercial Complex SELECT CITYWALK (Shopping Mall)", at A-3 & P1-B, District Centre, Saket, New Delhi by M/s. Select Infrastructure Private Limited.

Compliance Status (For the period October 2022- March 2023)

EC Clearance letter No - F. No. 21-672/2006-IA-III, dated 14/02/2007

EC Clearance letter No. - F. No. 21-45/2019-IA-III, dated 1/11/2019 (For Project Expansion)

S. No.	Description	
Α	Specific Conditions:	
(i)	Consent to Establish/Operate for the project shall be obtained from the State Pollution Control Board as required under the Air (Prevention and Control of Pollution) Act, 1981 and the Water {Prevention and Control of Pollution) Act, 1974	Consent to establish and Operate for the project have been obtained from the Delhi Pollution Control Board, and are attached as Annexure 1 and Annexure 2 respectively.  - Consent to establish for the expansion project has also been obtained from the Delhi Pollution Control Board, and is attached as Annexure 3.
		-Extension for Consent to establish has also been obtained from the Delh Pollution Control Board and is attached as Annexure 27
	Lolev 4	Renewal of Consent to Operate and Consent to operate for new Area applied through online application to DPCC or 3/11/22, application form



		and fees submission challan attached as Annexure 28
(ii)	The project proponent shall provide for adequate fire safety measures and equipment as per National Building Code/required by Fire Service Act of the State and instructions issued by the local Authority/Directorate of fire, from time to time. Further, the project proponent shall take necessary permission/NOC regarding fire safety from Competent Authority as required	The project proponent has adopted adequate fire safety measures and equipment as per National Building Code/required by Fire Service Act of the State and instructions issued by the local Authority/Director.
		NOC regarding fire safety from Competent Authority has been obtained and is attached as Annexure 4
(iii)	The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws	Environment Clearance has been obtained from MOEF&CC and is attached as Annexure 5. And approval from Airport authority of India has also been obtained for building height permission and is attached as Annexure -6.
		All necessary clearances/ permissions for expansion project from all relevant agencies including Town Planning Authority has been obtained. Form B-1 is attached as Annexure 7. Environment Clearance has also been obtained for expansion project from MOEF&CC and is attached as Annexure 8.
		Expansion Project is completed and Occupancy-cum-completion certificate issued by Delhi development authority has been attached as Annexure - 31
(iv)	As proposed, fresh water requirement from Saket Place Developers Association shall not exceed 240 KLD Ecopsent to Operate	240 KLD (Annual per day

	(CTO)/Occupancy Certificate shall be issued only after getting necessary permission for required water supply from DJB/concerned authority	supply from Saket Place Developer's Association, which has DJB and DDA approved water supply scheme for District Centre, Saket, New Delhi.
(v)	Sewage shall be treated in the STP based on Extended Aeration Technology with tertiary treatment i.e. Ultra Filtration. The treated effluent from STP shall be recycled/re-used for flushing & HVAC Cooling. As proposed, no excess treated water shall be discharge to Municipal drain	Noted & Complied. Total waste water generated is treated through in-house Sewage Treatment Plant. And treated water is reused in flushing , Cooling process and horticulture . Hence, no treated water is discharge outside the project.
(vi)	The project proponents would devise a monitoring plan to the satisfaction of the State Pollution Control Board so as to continuously monitor the treated waste water being used for flushing in terms of faecal coliforms and other pathogenic bacteria	Noted & Complied. The monitoring report of treated waste water is attached as Annexure 9
(vii)	The project proponents would commission a third party study on the implementation of conditions related to quality and quantity of recycle and reuse of treated water, efficiency of treatment systems, quality of treated water being supplied for flushing (specially the bacterial counts), comparative bacteriological studies from toilet seats using recycled treated waters and fresh waters for flushing, and quality of water being supplied through spray faucets attached to toilet seats	Green Circle Inc. authorized / approved by MoEF & CC & NABL is hired as third party agency for monitoring of Water, Noise, Air, Stack & STP. Reports attached as annexure 9
(viii)	The local bye-law provisions on rain water harvesting should be followed. If local bye- law provision is not available, adequate provision for storage and recharge should be followed as per the Ministry of Urban Development Model Building Byelaws, 2016. As proposed, 17 no. of rain water harvesting recharge pits shall be provided for rain water harvesting after filtration as per CGWB guidelines	Noted. Rooftop rainwater of buildings is collected in 17 (which includes 2 new Rain water harvesting pit) RWH tanks for harvesting after filtration. Adequacy for Rain Water Harvesting System is attached as Annexure 10
(ix)	Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. Wet garbage shall be composted in Organic Waste Converter. As proposed 50 sqm area shall be provided for solid waste management within the premises which Origin Include area for segregation, composting. The fact waste from	Noted & Complied. Generated garbage is segregated. Biodegradable waste is treated in Organic waste converter and non biodegradable recyclable waste including pastic waste is handed over to

	project will be sent to dumping site	waste collector (M/s Chintan Enviro Research Group). MOU with M/s Chintan Enviro Research Group is attached at Annexure -11 Adequate area is provided for solid waste management.
implemented in letter and detailed traffic management decongestion plan shall be of that the current level of se within a 05 kms radius maintained and improved implementation of the project be based on cumulative development and increased carried out or proposed to be project or other agencies in of the site in different scena time. Traffic management provalidated and certified by Development department competent authority for road shall also have their implementation of component	decongestion plan shall be drawn up to ensure that the current level of service of the roads within a 05 kms radius of the project is maintained and improved upon after the implementation of the project. This plan should be based on cumulative impact of all development and increased habitation being carried out or proposed to be carried out by the project or other agencies in this 05 Kms radius of the site in different scenarios of space and time. Traffic management plan shall be duly validated and certified by the State Urban Development department and the P.W.D./ competent authority for road augmentation and	Noted, Traffic management Plan is attached as Annexure 12.
(xi)	No tree cutting/transplantation of existing trees has been proposed in the instant project. A minimum of 1 tree for every 80 sqm of land should be planted and maintained. The landscape planning should include plantation of native species. The plantation species should be carefully chosen to avoid bird nesting and to improve pollution control and noise control measures. Water intensive and/or invasive species should not be used for landscaping. As proposed 8,290.16 sqm (34.30% of total area) area shall be provided for green area development	No tree cutting/transplantation of existing trees has been done. Greenbelt has been developed in the premises.  Greenbelt Development Details is attached as Annexure 13.
(xii)	The company shall draw up and implement corporate social Responsibility plan as per the Company's Act of 2013. As per the Ministry's Office Memorandum F.No. 22- 65/2017-IA. III dated 1 May, 2018, and proposed by the project proponent, an amount of Rs. 0.32 Crore (@ 1.00% of project Cost) shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as drinking water supply, plantation and horticulture and skill development & computer education. The activities proposed under CER shall be restricted to the affected area around the project? The entire activities	As a CER activity SIPL (Select CITYWALK) has adopted 2 parks in front of Mall, Jamunwala park was adopted in 2016 and redeveloped and maintained and Gandhi wala park was adopted in 2021 and its redevelopment work was completed in September 2022 and is being maintained since then by

	proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the Regional Office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent	Rs. 35,83,269 was incurred from SIPL (Select CITYWALK) CER fund for redevelopment and maintenance of these parks in period April -22 to September 22. The detail of expense along with project details are attached as Annexure 32. The report has also been submitted to District Collector office and has been posted on our website.
B.	Standard Conditions:	
I.	Statutory compliance:  The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws.	Environment Clearance has been obtained from MOEF&CC and is attached as Annexure 5  Environment Clearance for expansion project has been obtained from MOEF&CC and is attached as Annexure 8  For Town Planning Authority, Form B-1 from Delhi Development Authority is attached as Annexure 7  Expansion Project is completed and Occupancy-cum-completion certificate issued by Delhi development authority has been attached as Annexure -31
ii.	The approval of the Competent Authority shall be obtained for structural safety of buildings due to earthquakes, adequacy of firefighting equipment etc as per National Building Code including protection measures from lightening etc	Approval for structural safety from the Competent Authority has been obtained and is attached as Annexure 14  NOC from Delhi Fire Sevice has been obtained and is attached as Annexure 4.  NOC from Office of

		Electrical Inspector is attached as Annexure 15.
III.	The project proponent shall obtain the necessary permission for drawl of ground water / surface water required for the project from the competent authority	The fresh Water supply is met by water supply from Saket Place Developer's Association, which has DJB and DDA approved water supply scheme for District Centre, Saket, New Delhi. No Ground water/ surface water is extracted for use.
iv.	A certificate of adequacy of available power from the agency supplying power to the project along with the load allowed for the project should be obtained.	The Power requirement after expansion is 5660 KW (Connected Load: 6340 kva) which is provided by BSES, Delhi. Adequacy for Power Supply is attached as Annexure 16 (BSES bill)
٧.	All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department shall be obtained, as applicable, by project proponents from the respective competent authorities.	License for Diesel Storage is obtained from Petroleum & Explosive Safety Organization (PESO) attached as Annexure 17
VI.	The provisions of the Solid Waste Management Rules, 2016, e-Waste (Management) Rules, 2016, and the Plastics Waste Management Rules, 2016, shall be followed	Generated garbage is

		18
vii.	The project proponent shall follow the ECBC/ECBC-R prescribed by Bureau of Energy Efficiency, Ministry of Power strictly	Noted & Complied. ECBC compliance report has been obtained and is attached as Annexure 19
l.	Air quality monitoring and preservation:	
i.	Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory implementation of Dust Mitigation Measures for Construction and Demolition Activities for projects requiring Environmental Clearance shall be complied with.	All dust mitigation measures was implemented during constructed phase (including submission of fortnightly self assessment on DPCC portal)
il.	A management plan shall be drawn up and implemented to contain the current exceedance in ambient air quality at the site.	During construction phase all necessary measures like operation of anti smog gun, dry construction, covering of building materials during transportation and storage, online monitoring of ambient air with a link being provided of the same to DPCC and video fencing and a link of the same being provided to DPCC for online monitoring was implemented.  In addition to it SIPL (Select CITYWALK) for its common area has installed multiple advance filters to maintain AQI inside mall.
iii.	The project proponent shall install system to carryout Ambient Air Quality monitoring for common/criterion parameters relevant to the main pollutants released (e.g. PM10 and PM2.5) covering upwind and downwind directions during the construction period.	Noted & Complied.  During the construction phase air monitoring sensors were provided and air quality was regularly online monitored also a link of online monitoring of the same was provided to DPCC.
iv.	Diesel power generating sets proposed as source of backup power should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The height of stack of DG sets should be equal to the height needed for the combined capacity of all proposed DG sets FUSE of low sulphur diesel. The location of the DG sets may be decided with	Noted & Complied. Yes, all the D.G Sets installed at Select CITYWALK confirm to the Environment (Protection) Act. And have additionally been provided with retrofit pollution control device

	in consultation with State Pollution Control Board	(Chakra shield) which reduces PM emission to upto minimum of 70%. The installation certificate is attached as Annexure 29 and test report of Chakra Shield as approved by CPCB approved laboratory is attached as Annexure 30.
V.	Construction site shall be adequately barricaded before the construction begins. Dust, smoke & other air pollution prevention measures shall be provided for the building as well as the site. These measures shall include screens for the building under construction, continuous dust/ wind breaking walls all around the site (at least 3 meter height). Plastic/tarpaulin sheet covers shall be provided for vehicles bringing in sand, cement, murram and other construction materials prone to causing dust pollution at the site as well as taking out debris from the site.	Noted & Complied.  During construction phase the project area was completely barricaded and all measures are taken to control the dust, smoke & other air pollution during construction phase.
vi.	Sand, murram, loose soil, cement, stored on site shall be covered adequately so as to prevent dust pollution	Noted & Complied. Sand, murram, loose soil, cement, stored on site are covered properly to prevent dust pollution
vii.	Wet jet shall be provided for grinding and stone cutting	Noted & Complied.
viii.	Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppress dust	Noted, however there were no Unpaved surfaces and loose soil as it is existing building and only 1 floor was being constructed.
ix.	All construction and demolition debris shall be stored at the site (and not dumped on the roads or open spaces outside) before they are properly disposed. All demolition and construction waste shall be managed as per the provisions of the Construction and Demolition Waste Management Rules 2016	Noted & Complied.  During project phase all demolition and construction waste were disposed off to DPCC approved authorised C&D waste recycler and entire C&D waste was managed as per the provisions of the Construction and Demolition Waste Management Rules 2016
х.	The diesel generator sets to be used during construction phase shall be low sulphur diesel type and shall conform to rules made under the Environment (Protection) Act, 1986	Noted & Complied. No additional DG set was used during construction phase, the D.G Sets already installed at Select CITYWALK were used (when required) and which

		confirms to the Environment (Protection) Act. And have additionally been provided with retrofit pollution control device (Chakr shield) which reduces PM emission to upto minimum of 70%. The installation certificate is attached as Annexure 29 and test report of Chakra Shield as approved by CPCB approved laboratory is attached as Annexure 30.
xi.	The gaseous emissions from DG set shall be dispersed through adequate stack height as per CPCB standards. Acoustic enclosure shall be provided to the DG sets to mitigate the noise pollution. Low sulphur diesel shall be used. The location of the DG set and exhaust pipe height shall be as per the provisions of the Central Pollution Control Board (CPCB) norms	Noted & Complied.  To avoid the emissions, stack height of 6 m above roof level has been provided to reduce the air emissions, meeting all the norms prescribed by CPCB. Additionally as an air pollution control measure Emission control device – Chakra Shield 2.0 is installed in stack of all 5 DG sets. The installation certificate is attached as Annexure 29 and test report of Chakra Shield as approved by CPCB approved laboratory is attached as Annexure 30.
xii.	For indoor air quality the ventilation provisions as per National Building Code of India	Noted & Complied. In addition to provisions as per National Building Code of India , SIPL (Select CITYWALK) has installed multiple advance filters to maintain AQI inside mall.
III.	Water quality monitoring and preservation	
į.	The natural drain system should be maintained for ensuring unrestricted flow of water. No construction shall be allowed to obstruct the natural drainage through the site, on wetland and water bodies. Check dams, bio-swales, landscape, and other sustainable urban drainage systems (SUDS) are allowed for maintaining the drainage pattern and to harvest	Noted & Complied. During construction natural drainage has not been obstructed.
ii.	Buildings shall be designed to follow the natural	Noted & Complied

	topography as much as possible. Minimum cutting and filling should be done	
iii.	The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports	The quantity of fresh water usage, water recycling and rainwater harvesting is measured and recorded regularly. The records are submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports.  Record attached as Annexure 20.
iv.	A certificate shall be obtained from the local body supplying water, specifying the total annual water availability with the local authority, the quantity of water already committed, the quantity of water allotted to the project under consideration and the balance water available. This should be specified separately for ground water and surface water sources, ensuring that there is no impact on other users	Record of water Cosumption is attached as Annexure 20.
v.	At least 20% of the open spaces as required by the local building bye-laws shall be pervious. Use of Grass pavers, paver blocks with at least 50% opening, landscape etc. would be considered as pervious surface	Noted & Complied.
Vi.	Installation of dual pipe plumbing for supplying fresh water for drinking, cooking and bathing etc and other for supply of recycled water for flushing, landscape irrigation, car washing, thermal cooling, conditioning etc. shall be done	Noted & shall be complied.
VII.	Use of water saving devices/ fixtures (viz. low flow flushing systems; use of low flow faucets tap aerators etc) for water conservation shall be incorporated in the building plan	Noted & Complied.
viii.	Separation of grey and black water should be done by the use of dual plumbing system. In case of single stack system separate recirculation lines for flushing by giving dual plumbing system be done	Noted & Complied, Individual piping system has been provided for separation of grey and black water,
ix.	Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred	Noted & Complied.
*.	A rain water harvesting plan needs to be designed where the recharge bores of minimum one recharge bore per 5,000 square meters of built up area and storage capacity of minimum one day of total fresh water requirement shall be provided. In areas where ground water recharge is not feasible, the rain water should be harvested and stored for reuse. The ground water shall not be withdrawn without approval	Rooftop rainwater of buildings is collected in 17 (which includes 2 new Rain water harvesting pit) RWH tanks for harvesting after filtration. Adequacy for Rain Water Harvesting System is attached as Annexure 10

	from the Competent Authority	
xi.	All recharge should be limited to shallow aquifer	Noted & Complied.
xii.	No ground water shall be used during construction phase of the project	Ground water is not extracted, as the fresh Water supply requirement is met by water supply from Saket Place Developer's Association, which has DJB and DDA approved water supply scheme for District Centre, Saket, New Delhi, and for construction treated water was used.
xiii.	Any ground water dewatering should be properly managed and shall conform to the approvals and the guidelines of the CGWA in the matter. Formal approval shall be taken from the CGWA for any ground water abstraction or dewatering	No abstraction or dewatering is being done.
xiv.	The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports	Noted & Complied. The quantity of fresh water usage, water recycling and rainwater harvesting is measured and recorded regularly. The records are submitted to the Regiona Office, MoEF&CC along with six monthly Monitoring reports. Record attached as Annexure 20.
XV.	No sewage or untreated effluent water would be discharged through storm water drains	Noted & Complied.
xvi.	Onsite sewage treatment of capacity of treating 100% waste water to be installed. The installation of the Sewage Treatment Plant (STP) shall be certified by an independent expert and a report in this regard shall be submitted to the Ministry before the project is commissioned for operation. Treated waste water shall be reused on site for landscape, flushing, cooling tower, and other end-uses. Excess treated water shall be discharged as per statutory norms notified by Ministry of Environment, Forest and Climate Change. Natural treatment systems shall be promoted.	capacity is 300 KLD. Generated waste water is treated in-house STP and treated water is reused for flushing, irrigation & cooling purpose.  Outsourced treated water is used for irrigation & cooling
xvii.	Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from STP	Necessary measures an

XVI	ii Sludge from the	Monitoring Report attached as Annexure 9
	including septic tanks, shall be collecte conveyed and disposed as per the Ministry Urban Development, Central Public Health ar Environmental Engineering Organizatio (CPHEEO) Manual on Sewerage and Sewag Treatment Systems, 2013	nt. Generated sludge from d. STP is converted to manure and Manure in d used in gardening purpos
IV	Noise monitoring and prevention	
i.	Ambient noise levels shall conform to residentical area/commercial area/industrial area/silence zone both during day and night as per Nois Pollution (Control and Regulation) Rules, 2000 Incremental pollution loads on the ambient a and noise quality shall be closely monitored during construction phase. Adequate measure shall be made to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards by CPCB SPCB	e conform to residential e area/commercial oral area/industrial area/silence ir zone both during day and night as per Noise Pollution (Control and Regulation Rules, 2000. The Monitoring Report of Ambient Noise level is
ii.	Noise level survey shall be carried as per the prescribed guidelines and report in this regard shall be submitted to Regional Officer of the Ministry as a part of six-monthly compliance report	
ili.	Acoustic enclosures for DG sets, noise barriers for ground-run bays, ear plugs for operating personnel shall be implemented as mitigation measures for noise impact due to ground sources	Acoustic enclosures for DG sets, noise barriers for ground-run bays, ear plugs for operating personnel are implemented as mitigation measures for noise impact
	Energy Conservation measures:	due to ground sources
i.	Building Code (ECBC) of Bureau of Energy Efficiency shall be ensured. Buildings in the States which have notified their own ECBC, shall comply with the State ECBC.	Noted & Complied. ECBC compliance report has been obtained and is attached as Annexure 19
III.	Outdoor and common area lighting shall be LED	Noted & Complied.
	energy consumption in buildings by using design elements, such as building orientation, landscaping, efficient building envelope, appropriate fenestration, increased day lighting design and thermal mass etc. shall be incorporated in the building design. Wall, window, and roof u-values shall be as per ECBC specifications	Noted & Complied. ECBC compliance report has been obtained and is attached as Annexure 19
1	the building should be integral part of the project	Noted & Complied. Energy conservation measures is attached as Annexure 22.

	commissioning	
V	Solar, wind or other Renewable Energy shall be installed to meet electricity generation equivalent to 1% of the demand load or as per the state level/ local building bye-laws requirement, whichever is higher	Solar water heating system through solar panel to tap on renewable energy converting to Hot water system of capacity 3000 LPD for food outlets. Solar lights for open area is provided. Energy conservation measures is attached as Annexure 22 Also 1 % of the total additional energy demand (102 KW) has been met by installing solar power system. The Work completion certificate of Solar power system (102 KW) has been attached as Annexure 34
vi.	Solar power shall be used for lighting in the apartment to reduce the power load on grid. Separate electric meter shall be installed for solar power. Solar water heating shall be provided to meet 20% of the hot water demand of the commercial and institutional building or as per the requirement of the local building byelaws, whichever is higher. Residential buildings are also recommended to meet its hot water demand from solar water heaters, as far as possible	Noted & Complied. Solar lights for open area is provided to reduce the power load on grid and separate electric meter is installed. Solar water heating system through solar panel to tap on renewable energy converting to Hot water system of capacity 3000 LPD for food outlets is provided.
VI	Waste Management	
i.	A certificate from the competent authority handling municipal solid wastes, indicating the existing civic capacities of handling and their adequacy to cater to the M.S.W. generated from project shall be obtained	Noted & Complied. Generated garbage is segregated. Biodegradable waste is treated in Organic waste converter and non biodegradable recyclable waste including pastic waste is handed over to DPCC approved authorized waste collector (M/s Chintan Enviro Research Group). MOU with M/s Chintan Enviro Research Group is attached at Annexure -11
ii.	Disposal of muck during construction phase shall not create any adverse effect on the neighbouring communities and be disposed taking the necessary procautions for general	Noted & Complied. No muck was generated during construction phase and all C&D waste

	safety and health aspects of people, only in approved sites with the approval of competent authority	dispose off to DPCC authorised recycling plant.
HL.	Organic waste compost/ Vermiculture pit/ Organic Waste Converter within the premises with a minimum capacity of 0.3 kg /person/day must be installed	Organic Waste Converter is installed having capacity of 1.2 TPD.
ÌV.	All non-biodegradable waste shall be handed over to authorized recyclers for which a written tie up must be done with the authorized recyclers.	Non biodegradable recyclable waste including pastic waste is handed over to DPCC approved authorized waste collector (M/s Chintan Enviro Research Group). MOU with M/s Chintan Enviro Research Group is attached at Annexure -11
V.	Any hazardous waste generated during construction phase, shall be disposed off as per applicable rules and norms with necessary approvals of the State Pollution Control Board	E waste and hazardous waste (used lube oil) generated is handed over to pollution control board approved vendor (M/s Bharat Oil and waste management limited) MOU with M/s Bharat Oil and waste management limited is attached as Annexure 18.  Form 4 for FY 2021-2022 has been attached as Annexure 23.
vi.	Use of environment friendly materials in bricks, blocks and other construction materials, shall be required for at least 20% of the construction material quantity. These include Fly Ash bricks, hollow bricks, AACs, Fly Ash Lime Gypsum blocks, Compressed earth blocks, and other environment friendly materials	Noted & Complied. Environment friendly materials are being used in construction.
vii.	Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27th August, 2003 and 25th January, 2016. Ready mixed concrete must be used in building construction	Noted & Complied.
viii.	Any wastes from construction and demolition activities related thereto shall be managed so as to strictly conform the Construction and Demolition Waste Management Rules, 2016	Noted & Complied.

íx.	Used CFLs and TFLs should be properly collected and disposed off/sent for recycling as per the prevailing guidelines/ rules of the regulatory authority to avoid mercury contamination	Noted & Complied.  E waste generated is handed over to pollution control board approved vendor (M/s Bharat Oil and waste management limited) MOU with M/s Bharat Oil and waste management limited is attached as Annexure 18.
VII	Green Cover	
i,	Topsoil should be stripped to a depth of 20 cm from the areas proposed for buildings, roads, paved areas, and external services. It should be stockpiled appropriately in designated areas and reapplied during plantation of the proposed vegetation on site	Noted
VIII	Transport	
Ĭ,	A comprehensive mobility plan, as per MoUD best practices guidelines (URDPFI), shall be prepared to include motorized, non-motorized, public, and private networks. Road should be designed with due consideration for environment, and safety of users. The road system can be designed with these basic criteria.  a. Hierarchy of roads with proper segregation of vehicular and pedestrian traffic. b. Traffic calming measures. c. Proper design of entry and exit points.	Noted & Complied. A Comprehensive Mobility Plan Is Prepared and all roads are designed with due to consideration for environment and safety of users.
ii,	d. Parking norms as per local regulation  Vehicles hired for bringing construction material to the site should be in good condition and should have a pollution check certificate and should conform to applicable air and noise emission standards be operated only during non-peak hours	Noted & Complied.  Vehicles hired for bringing construction material to the site are in good condition and had pollution check certificate and confirm to applicable air and noise emission standards operated only during non-peak hours
IX	Human health issues	Wellers - Harris - Assertion
i.	<ul> <li>All workers washing at the construction site and involved in loading, unloading, carriage of construction material and construction debris or working in any area with dust pollution shall be provided with dust mask</li> </ul> Noted & Compliance <ul> <li>All workers we with dust m</li> <li>construction phonomics</li> </ul>	
ii.	For indoor air quality the ventilation provisions as per National Building Code of India	Noted & Complied.
III.	Emergency prepared has plan based on the Hazard identification and Risk Assessment	Noted & Complied. Emergency preparedness

	(HIRA) and Disaster Management Plan shall be implemented	plan based on the Hazard identification and Risk Assessment (HIRA) and Disaster Management Plan has been implemented.
iv.	Provision shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, creche etc. The housing may be in the form of temporary structures to be removed after the completion of the project	Noted & Complied. Local construction labour were/are deployed and all necessary facilities were/are provided including medical health care.
V.	Occupational health surveillance of the workers shall be done on a regular basis	Noted & Complied.
vi.	A First Aid Room shall be provided in the project both during construction and operations of the project	Noted & Complied.
х	Corporate Environment Responsibility:	
1.	The company shall have a well laid down environmental policy duly approved by the Board of Directors. The environmental policy should prescribe for standard operating procedures to have proper checks and balances and to bring into focus any infringements/deviation/violation of the environmental / forest / wildlife norms / conditions. The company shall have defined system of reporting infringements / deviation / violation of the environmental / forest / wildlife norms / conditions and / or shareholders / stake holders. The copy of the board resolution in this regard shall be submitted to the MoEF&CC as a part of six-monthly report	Noted & Complied. The company has well laid down Quality, Environment, Energy and health and Safety policy duly approved by the Board of Directors and signed by CEO. Copy of the same has been attached as Annexure 24.
ii,	A separate Environmental Cell both at the project and company head quarter level, with qualified personnel shall be set up under the control of senior Executive, who will directly report to the head of the organization	Noted & Complied.
III.	Action plan for implementing EMP and environmental conditions along with responsibility matrix of the company shall be prepared and shall be duly approved by competent authority. The year wise funds earmarked for environmental protection measures shall be kept in separate account and not to be diverted for any other purpose. Year wise progress of implementation of action plan shall be reported to the Ministry/Regional Office along with the Six Monthly Compliance Report	Noted & Complied.  Expenditure on Environment Management Plan is prepared and is attached as Annexure 25.  Year wise progress of implementation of action plan is reported to the Ministry/Regional Office along with the Six Monthly Compliance Report.

XI	Miscellaneous:		
Ĭ.	The project proponent shall prominently advertise it at least in two local newspapers of the District or State, of which one shall be in the vernacular language within seven days indicating that the project has been accorded environment clearance and the details of MoEFCC/SEIAA website where it is displayed	Noted & Complied. Environment Clearance Advertisement Copy is attached as Annexure 26.	
Ti.	The copies of the environmental clearance shall be submitted by the project proponents to the Heads of local bodies, Panchayats and Municipal Bodies in addition to the relevant offices of the Government who in turn has to display the same for 30 days from the date of receipt	Noted & Complied.	
iii.	The project proponent shall upload the status of compliance of the stipulated environment clearance conditions, including results of monitored data on their website and update the same on half-yearly basis		
iv.	The project proponent shall submit six-monthly reports on the status of the compliance of the stipulated environmental conditions on the website of the ministry of Environment, Forest and Climate Change at environment clearance portal	Noted & Complied.	
<b>V</b> ,	The project proponent shall submit the environmental statement for each financial year in Form-V to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently and put on the website of the company	Noted & Complied. Form V for FY 2021-22 is attached as Annexure 33	
vi.	The project proponent shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities, commencing the land development work and start of production operation by the project	The expansion Project received Occupancy-cum-completion certificate from Delhi Developmen Authority on 26/8/22	
vii.	the state of the s		
viii.	viii. The project proponent shall abide by all the commitments and recommendations made in the EIA/EMP report and commitment made during their presentation to the Expert Appraisal Committee		
ix.	No further expansion or modifications in the plan shall be carried out without prior approval of the Ministry of Environment, Forest and Climate Change (Mos F&CC).	Noted and complied	

X.	Concealing factual data or submission of false/fabricated data may result in revocation of this environmental clearance and attract action under the provisions of Environment (Protection) Act, 1986	Noted
xi.	Concealing factual data or submission of false/fabricated data may result in revocation of this environmental clearance and attract action under the provisions of Environment (Protection) Act, 1986	Noted
xii.	The Ministry reserves the right to stipulate additional conditions if found necessary. The Company in a time bound manner shall implement these conditions	Noted
xiii.	The Regional Office of this Ministry shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data / information/monitoring reports	Noted
xiv,	The above conditions shall be enforced, inter- alia under the provisions of the Water (Prevention & Control of Pollution) Act, 1974, the Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016, and the Public Liability Insurance Act, 1991 along with their amendments and Rules and any other orders passed by the Hon'ble Supreme Court of India / High Courts and any other Court of Law relating to the subject matter	Noted
XV.	Any appeal against this EC shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act. 2010	Noted



## Annexure – 1

# Consent to Establish (2013)

Delhi Pollution Control Committee

dpos

4th & 5th Floor, ISBT Building, Kashmere Gate, Delhi - 110006.
Website: http://dpcc.delhigovt.nic.in

CONSENT ORDER

Despatch No. 1022 Date. 26 0 5 2013

Certificate No. :

: 0-020107

Name of the Unit SELECT CITYWALK (SHOPPING MALL)

Address PLOT A-3&P1B, DISTRICT CENTRE, SAKET, DELHI-110001

Consent Order No : DPCC/CMC/2013/31913

Date of Issue : 30-04-2013

Date of Expiry : 29-04-2014

Product/Activity Construction of shopping mall/ Commercial space.

This Consent to Establish is hereby granted under section 21 of the Air (Prevention & Control of Pollution) Act, 1981 and under section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 under Orange Category. This consent is subject to terms and conditions specified overleaf.

NY MA has done the analysis ade report dated M/A as fallers

MON



Prescribed Handards

Elle 15 to 7419

Elle 15 to 7419

Elle 20 mile

Col 6 250 mile

All 15 to 7419

Col 6 250 mile

Col 7 50 mile

Col 7

Verified by : ENVIRONMENTAL ENGINEER

Chief MARKET of Delta Caleba

Issuing Authority : SENIOR ENVIRONMENTAL ENGINEER

Daths Pullations Control Committee

4th S 5th Floor, ISST Hooking

Karbanes Care, New Delhi-110006

## Annexure – 2

# Consent to Operate 2022



#### DELHI POLLUTION CONTROL COMMITTEE

#### (Government of N.C.T. of Delhi) 4th & 5th Floor, ISBT Building Kashmere Gate, Delhi 110006 (Visit us at https://www.dpccocmms.nic.in)



#### CONSENT ORDER

Certificate No.: G-31829

Name of the unit : SELECT CITYWALK (SHOPPING

MALL)

Address : Plot A-3 and P1B, District Centre, Saket,

Housing Complexes, Commercial Complexes (including shopping malls), office complexes including IT and Infrastructual and Town Development Projects (Built Up Area 20000 sq. meters

and above), Delhi - 110001

Consent Order No : DPCC/CMC/2022/8706964

**Date of issue** : 07/07/2023

Product/Activity: Shopping Malls, Housing / Commercial/

Office Complexes having built up area

20,000 sqm and above

Manufacturing Activities : Commercial Complex Select Citywalk

(Shopping Mall)

Category Name : [RED]

Prouct Capacity : 0 Metric Tonnes/Day

This Consent to **Operate** is hereby granted under section 21 of the Air (Prevention & Control of Pollution) Act, 1981 and under section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 under **RED** Category. This consent is subjected to terms and conditions specified overleaf. **This is being issued with reference to your application id 8706964 valid from 07/12/2022 to 06/12/2027.** 

Incharge, EIA Cell

#### Terms and Conditions

- 1. The Consentee shall meet the effluent standards i.e. pH= 5.5-9, Total Suspended Solids (TSS) 30, Biochemical Oxygen Demand (3 days at 27degree Cent.)-20, COD-250, Oil and Grease-10, Ammonical Nitrogen (as N)-50, Nitrate Nitrogen-10, Dissolved Phosphate (as P)-5. # All effluent parameters are in mg/I expect pH value.
- 2. The Consent is activity specific and based on the information provided in the consent application along with the documents/ subsequent documents/information submitted to Delhi Pollution Control Committee (DPCC). The Consentee shall apply for fresh consent in case of any change in the activity/manufacturing process.
- 3. The consentee shall display the Name of the unit along with its Address, name of the proprietor/Directors/partners etc., Contact Phone No(s) and its Activities Processes/ Product etc, on a Display Board to be placed/fixed at the main gate of the unit.
- 4. The consentee/unit shall have/take separate Electricity/Power connection in its name and shall have/install separate meter in this regard.
- 5. The consentee shall provide and maintain separate drainage system for collection of trade and sewage effluents. Terminal manholes shall be provided at the end of collection system and shall be connected to the conveyance system/ sewerage system of the area leading to common Effluent Treatment Plant of the Industrial Area/sewage Treatment Plant of the catchment area.
- 6. The Consentee shall obtain permission from Delhi Jal Board. for ground water extraction, if any, as per the various orders/Notification of Govt. of NCT of Delhi.
- 7. The Consentee shall ensure proper channelization/ control system for fugitive emissions generated from the various activities/ processes of the unit and maintain good housekeeping practices so as to maintain clean & safe environment in and around the premises of the unit
- 8. The Consentee shall comply with the noise standards laid down vide Gazette notification of Ministry of Environment and Forest(MOEF), Government of India Dated 17.05.2002 & 12.07.2004, as amended to date, for the Diesel Generator Set(s) and shall also comply with the Emission Standards prescribed for Diesel Engines [(Engine rating more than 0.8 MW) for Power Plant, Generator Set applications and other requirements], if any, as per the Gazette Notification of MOEF, Dated 09.07.2002, as amended to date. Stack Height tor sets(Engine rating more than 0.8 MW) commissioned after 01.07.2003 shall be maximum of following (i)Minimum 6 meter above the building where generator set is installed (ii) 30 meter (iii)  $14Q^{\circ 1}3(Q \text{ Total So2 emission from the plant in kg per hr)}$  and for otter DG Set(s) (up to 0.8 MW) stack height shall be as per the following formula, H = h + 0.2KVA(H-Total Height of stack in meter , h = Height of the building in meters where the Generator Set is installed, KVA -Total Generator capacity of the set in KVA).
- 9. Capacity of the DG Set (s) installed in the unit 3X2000 KVA and 2X1010 KVA. The Consentee shall properly maintain the Acoustic Enclosure/ Acoustic Treated room for DG Set(s) in good condition and maintain the adequate stack height for DG Set(s) to meet the prescribed standards/ norms as mentioned above. The Consentee shall ensure the compliance of the extant directions issued by CAQM / CPCB/ DPCC under GRAP.
- 10. The DG set shall be operated subject to compliances of the norms. The Consentee shall not operate the DG Set(s) till compliance of the prescribed norms/standards for DG Sets.
- 11. The Consentee shall comply with the provisions of the Hazardous and Other Wastes (Management and Trans boundary Movement) Rules, 2016, as amended to date, the Batteries (Management and Handling) Rules, 2001 as amended to date, Solid Waste Management Rules, 2016 and E-Waste (Management) Rules, 2016, the Manufacture, Storage and Import of Hazardous Chemicals Rules, 1989, as amended to date, wherever applicable. All such wastes generated from the unit will be managed and handled as per the provisions of the said Rules and will be disposed only through the Recycler/Reprocessor/Authorized

Agencies for such wastes, authorized by MOEF/Central Pollution Control Board/State Pollution Control Board/Committee/DPCC as per details available on their websites.

- 12. The Consentee shall comply with the provisions of the Plastic Waste Management Rules, 2016, as amended to date and any direction issued by CPCB/Department of Env.,GNCTD/DPCC, if applicable.
- 13. The Consentee shall comply the other prescribed standards of Effluent/Emissions as prescribed and as applicable under the provisions of the Environment (Protection) Act, 1986, as amended to date and the various Rules made there under including the Noise Pollution (Regulation and Control) Rules, 2000.as amended to date.
- 14. The Consentee shall promote the use of CFL and recovery of mercury from CFL Lamps and should create a system of replacing of old bulbs for new to enable recovery of mercury after the bulbs are fused.
- 15. The Consentee shall not carry out any activity falling under the Prohibited/ Negative list of Industries (Annexure III of MPD -2021) which are prohibited in National Capital Territory of Delhi, as per Master Plan of Delhi.
- 16. Quantity of Effluent/Sewage Discharge from the unit shall not exceed nil Liters/ Day (100 % waste water recycling and zero waste water discharge).
- 17. The Consentee has installed Sewage Treatment Plant (STP) of 300 KLD and shall properly operate and maintain to meet the prescribed standards as given in the Consent Order.
- 18. Flow Meters/ suitable flow measuring devices shall be provided and maintained to measure the quantity of waste water generation and treatment by the unit and to quantify the reused of treated water. No bypass (Pipe / Drain) shall be provided. The treated effluent shall be used/ recycled by the unit. Records /Logbook shall be maintained for the operation of the STP, waste water generated, treated and used/recycled and shall be produced during the inspection of DPCC official(s).
- 19. The Consentee having installed Emission Control System (ECS) shall properly operate and maintain the ECS to meet the prescribed standards as given in the Consent Order. No bypass stack/ arrangement shall be provided. Records /Logbook shall be maintained for the operation of the ECS and shall be produced during the inspection of DPCC official(s). The Consentee shall provide and maintain ports in the Stack(s) /Chimney(s) and facilities such as ladder, platform etc. in good condition for monitoring of the emissions.
- 20. Project proponent will ensure use of ozone depletion substances (ODS) free appliances so that no toxic gases in air conditioning/ refrigeration/ fire extinguishers are created.
- 21. Municipal Solid waste reduction/ Zero garbage concepts shall be implemented with appropriate technology of composting.
- 22. The Consentee shall not extract the ground water without obtaining prior permission in this regard from DJB/CGWA.
- 23. The Consentee shall ensure that there is no bore well in the premises and if exist, same shall be closed/sealed with immediate effect till permission received from DJB/CGWA.
- 24. Unit shall implement the environmental safeguards as per stipulations in Environmental Clearance issued by MoEF/ SEIAA and shall submit half yearly compliance report in respect of the terms and conditions of Environmental Clearance to Regional Office of MoEF and simultaneously to DPCC on the prescribed date.
- 25. The Consentee shall submit application for renewal of the Consent, one month in advance of the expiry date of this Consent Order.

In the event of any information furnished by the Consentee found to be false OR in case of failure to comply with any of the above mentioned consent conditions, consent granted through this Consent Order shall be deemed to be revoked without any notice and necessary action as per law shall be taken, which may include closure of the unit and prosecution for wrong declaration.

Notwithstanding anything contained in this consent order. Delhi Pollution Control Committee, reserves its right to review any / or all the conditions imposed herein above and to make such variations as deemed fit

for the purpose of enforcement of the Air (Prevention and Control of Pollution)Act, 1981, as amended to date and the Water(Prevention and Control of Pollution)Act, 1974, as amended to date.

The Consent granted to the Consentee is to ensure control of pollution from the premises of the unit in accordance with various Pollution Control Laws and in no way confers the right to the Consentee / unit to exist in violation of other laws and statutory provisions including the Master Plan of Delhi.

This issues in view of the Office Order No. F.No.DPCC/Consent/2017/569-580 dated 31.05.2017 and Office Order No. F.No.DPCC/Consent/2017/1185-1198 dated 08.09.2017 as per decision taken by Consent Management Committee for II(a) category in its meeting held on 01.06.2023.

#### 12. Standard

Parameter Name	Prescribed Standard
1 at affect Marie	11 escribed Standard

## <u>Annexure – 3</u>

Consent to
Establish for
Expansion Project
2019



#### DELHI POLLUTION CONTROL COMMITTEE

(Government of N.C.T. of Delhi)

4th & 5th Floor, ISBT Building Kashmere Gate, Delhi 110006

### (Visit us at https://www.dpccocmms.nic.in) CONSENT ORDER

Certificate No.: G-4679

Name of the unit : M/s Select Infrastructure Pvt. Ltd.

Address : "COMMERCIAL COMPLEX SELECT

CITY WALK (SHOPPING MALL)" at A-3 & P1B, District Centre, Saket, New Delhi-110017, Housing Complexes, Commercial Complexes (including shopping malls), office complexes including IT and Infrastructual and Town Development Projects (Built Up Area 20000 sq. meters

and above), Delhi - 110017

Consent Order No : DPCC/CMC/2019/2439234

**Date of issue** : 16/11/2019

Product/Activity : Shopping Malls, Housing / Commercial/

Office Complexes having built up area

20,000 sqm and above

Manufacturing Activities : Expansion/Additional construction of

"COMMERCIAL COMPLEX SELECT CITY WALK(SHOPPING MALL)"

Category Name : [RED]

This Consent to **Establish** is hereby granted under section 21 of the Air (Prevention & Control of Pollution) Act, 1981 and under section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 under **RED** Category. This consent is subjected to terms and conditions specified overleaf. **This is being issued with reference to your application id 2439234 valid from 09/10/2019 to 08/10/2021.** 

PANKAJ KAPIL Digitally signed by PANKAJ KAPIL Date: 2019.11.18 12:23:31 +05'30'

Senior Environmental Engineer

#### Terms and Conditions

- 1.The Consentee shall meet the effluent standards i.e. pH= 5.5-9, Total Suspended Solids (TSS) 30, Biochemical
- Oxygen Demand (3days at 27degree Cent.) 20, COD 250, Oil and Grease 10, Ammonical Nitrogen(as N) 50,Nitrate Nitrogen 10,Dissolved Phosphate(as P)5. #All effluent parameters are in mg/I expect pH value. 2.The Consent is activity specific and based on the information provided in the consent application along with the documents/ subsequent documents/information submitted to Delhi Pollution control Committee (DPCC). The Consentee shall apply for fresh consent in case of any change in the activity /manufacturing
- 3. The consentee shall display the Name of the unit along with its Address, name of the proprietor/ Directors/partners etc, Contact Phone No(s) and its Activities Processes/ Product etc, on a Display Board t be placed/fixed at the main gate of the unit.
- 4.The consentee/unit shall have/take separate Electricity/Power connection in its name and shall have/install separate meter in this regard.
- 5. The consentee shall provide and maintain separate drainage system for collection of trade and sewage effluents. Terminal manholes shall be provided at the end of collection system and shall be connected to the conveyance system/ sewerage system of the area leading to common Effluent Treatment Plant of the Industrial Area/sewage Treatment Plant of the catchment area.
- 6.The Consentee shall obtain permission from Delhi Jal Board. for ground water extraction, if any, as per the various orders/Notification of Govt. of NCT of Delhi.
- 7.The Consentee shall ensure proper channelization/ control system for fugitive emissions generated from the various activities/ processes of the unit and maintain good house keeping practices so as to maintenance clean & safe environment in and around the premises of the unit
- 8.The Consentee shall comply with the noise standards laid down vide Gazette notification of Ministry of Environment and Forest(MOEF), Government of India Dated 17.05.2002 & 12.07.2004, as amended to date, for the Diesel Generator Set(s) and shall also comply with the Emission Standards prescribed for Diesel Engines [(Engine rating more than 0.8 MW) for Power Plant, Generator Set applications and other requirements], if any, as per the Gazette Notification of MOEF, Dated 09.07.2002, as amended to date. Stack Height tor sets(Engine rating more than 0.8 MW) commissioned after 01.07.2003 shall be maximum of following (i)Minimum 6 meter above the building where generator set is installed (ii) 30 meter (iii) 14Q°'3(Total so2 emission from the plant in kg/hr) and for otter DG Set(s) (up to 0.8 MW) stack height shall be as per the following formula, H = h + 0.2?KVA(H-Total Height of stack in meter, h = Height of the building in meters where the Generator Set is installed, KVA -Total Generator capacity of the set in KVA).
- 9.The Consentee shall comply with the provisions of the Hazardous and Other Wastes (Management and Trans boundary Movement) Rules, 2016, as amended to date, the Batteries (Management and Handling) Rules, 2001.as amended to date, Solid Waste Management Rules, 2016 and E-Waste (Management) Rules, 2016, the Manufacture, Storage and Import of Hazardous Chemicals Rules, 1989, as amended to date, wherever applicable. All such wastes generated from the unit will be managed and handled as per the provisions of the said Rules and will be disposed only through the Recycler/Reprocessor /Authorized Agencies for such wastes, authorized by MOEF/Central Pollution Control Board/State Pollution Control Board/Committee/DPCC as per details available on their websites.
- 10. The Consentee shall comply with the provisions of the Plastic Waste Management Rules, 2016, as amended to date, if applicable.
- 11. The Consentee shall comply the other prescribed standards of Effluent/Emissions as prescribed and as applicable under the provisions of the Environment (Protection) Act, 1986, as amended to date and the various Rules made there under including the Noise Pollution (Regulation and Control) Rules, 2000.as amended to date.

- 12. The Consentee shall promote the use CFL and recovery of mercury from CFL Lamps and should create a system of replacing of old bulbs for new to enable recovery of mercury after the bulbs are fused.
- 13. The Consentee shall not carry out any activity falling under the Prohibited/ Negative list of Industries (Annexure III of MPD -2021) which are prohibited in National Capital Territory of Delhi, as per Master Plan of Delhi.
- 14.Quantity of Sewage/ trade effluent discharge from the unit shall not exceed Nil litre/Day.(100 % waste water recycling and zero waste water discharge).
- 15. Consentee shall treat the Waste water generated from labours in existing STP.
- 16. The total waste water after expansion will be 245 KLD which shall be treated into sewage treatment plant of total capacity 300 KLD (already installed).
- 17. The zero waste water discharge condition to be achieved with installation of on site STP. Trade effluent shall confirm to the norms and standards prescribed by Delhi Pollution Control Committee. The STP should be certified by an independent expert and report in this regard should be submitted to Delhi Pollution Control Committee before the project is commissioned for operation. necessary measures should be made to mitigate the odour problem from STP.
- 18. The treated wastewater of shall be recycled and reused for Horticulture/ landscape/cooling/flushing purposes to reduce the demand of fresh water as committed.
- 19. The project proponent shall provide electromagnetic flow meter at the inlet and outlet of the water supply, Inlet and outlet of the STP and any pipeline to be used for re-using the treated wastewater back into the system for cooling, flushing and for horticulture purpose/green etc. and shall maintain a record of readings of each such meter on daily basis.
- 20. The quantity of fresh water usage and water recycling shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Delhi Pollution Control Committee on six monthly basis.
- 21.Capacity of the Diesel Generator Set (s) already installed in the unit are 2X1010 kVA,3X2000 kVA. The Consentee shall provide and maintain the Acoustic Enclosure/ Acoustic Treated room for DG Set(s) in good condition and provide the adequate stack height for DG Set(s) to meet the prescribed standards/ norms. The Consentee shall not operate the DG Set(s) till compliance of the prescribed norms/standards for DG Sets. The D.G. Sets install for construction purposes shall also comply with the prescribed norms/standards. 22.The Consentee shall comply with the applicable provisions / Directions given vide Gazette Notification of Department of Environment, Govt. of NCT of Delhi, dated 23.10.2012 including the directions that no person shall manufacture, import, store, sell or transport any kind of plastic carry bags (including that of Poly Propylene, Non-woven fabric type carry bags) in the whole of National Capital Territory of Delhi. 23.The consentee shall provide wide spread Green Cover and the use of Fly Ash as per Fly Ash notification dated 14.09.1999 shall be mandatory.
- 24.Project proponent will ensure use of Ozone depletion substances (ODS) free appliances so that no toxic gases in air conditioning / refrigeration / fire extinguishers are created.
- 25.During construction Phase for control of dust pollution all precautionary measure should be ensured in compliance of Hon'ble National Green Tribunal order dated 04.12.2014 and 10.04.2015 in O.A. No. 21 c of 2014 and O.A. No. 95 of 2014 in the matter of Vardhman Kaushik Vs. Union India and other and Sanjay Kulshreshtha Vs. Union of India and Ors. and as notified by MOEF and CC, GOI vide Notification no. G.S.R. 94(E) dated 25.01.2018.
- 26.It will be the responsibility of the project proponent to obtain prior clearances/approval and ensure compliances under all other relevant Acts/ Rules/ Regulations/ guidelines/ instructions/Court Orders/Tribunal Orders as applicable to this project before starting of the project.
- 27. The consentee shall comply with the provisions of Solid Waste Management Rules, 2016.
- 28.Unit shall implement the environmental safeguards as per stipulations in Environmental Clearance issued by SEIAA Delhi and shall submit half yearly compliance report in respect of the terms and conditions of

- Environmental Clearance to Regional Office of MoEF and simultaneously to DPCC on the prescribed date. 29.The Consentee shall not extract the Ground Water without obtaining prior permission in this regard from DJB / CGWA. The Consentee shall ensure that there is no bore well in the premises and if exist, same shall be close / sealed with immediate effect till permission received from DJB / CGWA.
- 30. The Consentee shall submit application for extension of the Consent / Consent to Operate, one month in advance of the expiry date of this Consent Order.
- 31. This consent is being granted focusing only on the Water Act 1974/ Air Act 1981. The project will be regulated by the concerned local Civic Authorities under the provisions of the relevant provisions of the extant MPD2021, Building Control Regulations and Safety Regulations. The investment made in the project, if any, based on Consent so granted, in anticipation of the clearance from other statuary authorities shall be entirely at the cost and risk of the project proponent DPCC shall not be responsible in this regard in any manner.
- 32.Project Proponent is allowed to run the pollution control devices and collect and test the data. The trial for three aforesaid purpose is permitted within the period of maximum three months from the date of completion. The consentee shall give prior intimation, to DPCC, of the dates on which trial would starts and end. Thereafter Project Proponent shall apply for Consent to Operate along with requisite details and test reports to DPCC
- 33. The Consentee shall abide by the Guideline on Environmental Management of Construction and Demolition (C and D) Waste and Guidelines on Dust Mitigation Measure in Handling Construction Material and C and D waste developed and published by CPCB available at www.cpcb.nic.in
- 34.The Consentee shall display the enclosed template of Notice for Construction and Demolition Waste Management at the site.
- 35. The Consentee shall ensure the compliance of policy to be followed regarding operation of Ready Mix Concrete Plants (RMC Plants) issued vide office order No. DPCC/CMC I/RMC/2017/2596 to 2614 dated 27.12.2017 (available at DPCC website)
- 36.In the event of any information furnished by the Consentee found to be false OR in case of failure to comply with any of the above mentioned consent conditions, consent granted through this Consent Order shall be deemed to be revoked without any notice and necessary action as per law shall be taken, which may include closure of the unit and prosecution for wrong declaration.
- 37. Notwithstanding anything contained in this consent order. Delhi Pollution Control Committee, reserves its right to review any / or all the conditions imposed herein above and to make such variations as deemed fit for the purpose of enforcement of the Air (Prevention and Control of Pollution)Act, 1981, as amended to date and the Water(Prevention and Control of Pollution)Act, 1974, as amended to date.
- 38. The Consent granted to the Consentee is to ensure control of pollution from the premises of the unit in accordance with various Pollution Control Laws and in no way confers the right to the Consentee / unit to exist in violation of other laws and statutory provisions including the Master Plan of Delhi.
- 39. The Consent granted to the Consentee is to ensure control of pollution from the premises of the unit in accordance with various Pollution Control Laws and in no way confers the right to the Consentee / unit to exist in violation of other laws and statutory provisions including the Master Plan of Delhi.
- 40.Sludge from the onsite sewage treatment, including septic tanks, shall be collected, conveyed and disposed as per the Ministry of Urban Development, Central Public Health and Environmental Engineering Organization (CPHEEO) Manual on Sewerage and Sewage Treatment Systems, 2013.
- 41. The consentee will be bound to comply all the directions issued by EPCA/CPCB/DPCC under the GRAP and all other directions issued by other statutory authorities/Hon'ble Courts for prohibition of construction activity during high AQI.
- 42.As Proposed, Fresh water requirement from Saket Place Developers Association shall not exceed 240 KLD. Consent to Operate (CTO)/Occupancy Certificate shall be issued only after getting necessary permission for required water supply from DJB/Concerned authority.

This issues in view of the Office Order dated 12.04.2016 regarding processing of the Consent to Establish cases.

Template for displaying notice w.r.t. condition no 34 to be displayed on board of size 6 feet X 4 feet.

Background color- Yellow, Letters- Black
NOTICE

(Construction and demolition waste management rule 2016)

The construction/Demolition site is authorized by... Vide file no... Dated.....

1.Name and Address with contact number of contractor/developer

- 2.Address of the site
- 3. Area/length
- 4.Date of initiation of the project(dd/mm/yy)
- 5. Scheduled completion date of the project(dd/mm/yy)
- 6.Details date of completion/disposal/clearing of the site(dd/mm/yy)
- 7.Estimated waste(TPD)
- 8. Total estimated waste(MT) for the entire project
- 9. Nature of waste (concrete/iron/plastic/soil)(TPD)

i. Material	Generated	Recycled	Reused	Disposed
ii. Sand	1/5			
iii. Concrete				
iv				

- 10. Identified waste disposal site
- 11.mode of utilization of waste(reuse/recycle/converting to construction material)
- 12.Mode of disposal
- 13. Mode of handling and transportation(manual/mechanical/pneumatic)(by road/rail)
- 14. Dust mitigation measures at the site(water sprinkling/curtain/barries etc)
- 15.Reason of delay in disposing waste(in any)
- 16.Accidents reported(in any)

Name of Agency Owner

Telephone number

## Annexure – 4

Fire NOC



#### GOVERNMENT OF NATIONAL CAPITAL TERRITORY OF DELHI HEADQUARTERS: DELIII FIRE SERVICE: NEW DELHI-110001

No. F 6/DES/MS/Mall/2022/87/ 1553/S

Dated 27/07/2022

#### FIRE SAFETY CERTIFICATE

Delhi 110017 comprised of Three Tier Basement, Ground & Seven floors owned/occupied by Select Infrastructure Pvt. Ltd was issued Fire Safety Certificate by this department vide letter no. Fo/DFS/MS/Mall/SZ/2021/171 Dated 15/03/2021. The premise was re-inspected by the officer concerned of this department on 20/07/2022 in the presence of Mr. Praveen Kumar, AE (Bldg) DDA, Mr. Shashi Sharma Director/Operation (Select City Mall) & Col/ J S Chhikara GM (Eng.) and observed that there is addition/alteration is existing Mall building at First & Second Floor of the building have complied with the fire prevention and fire safety requirements in accordance with rule 33 of Delhi Fire Service Rules, 2010 and that the premises is fit for occupancy class "Mixed Occupancy (Mercantile Building) with effect from 2.7.7.0.7./2022 for a period of Three years in accordance with Rule 36 unless renewed under Rule 37 or sooner cancelled under Rule 40 and subject to compliance of the conditions under Rule 38 of the Delhi Fire Service Rules, 2010.

Issued 27/07 /2022 at New Delhi by

DIRECTOR

Copy to: -

 M.'s Select City Walk (Select Infrastructure Pvt. Ltd) Situated at A-3 & P1B, Distr. Centre Saket, New Delhi 110017

The Executive Engineer, (bldg) Building Department, DDA, Vikas Sadan, INA, New Delhi.

### Conditions for the validity of Fire Safety Certificate:

- All the fire safety arrangement provided therein shall be maintained in good working condition at all time as seen during inspection. Any loss of life property due to non-functional fire safety measures shall be at the responsibility of the management.
- The Building sanctioning authority may verify any deviation with regard to the construction/occupancy in the building. In case of any deviation, the fire safety certificate stands null and void.
- 3. All the staff members must know the correct method of operation of fire fighting system.
- The basement shall be used as per the provisions of BBL /NBC Part- IV.
- The owner/occupier shall submit a declaration every year in form 'K' provided in the first schedule of Delhi
  Fire Service Rules 2010. The form is available on <a href="https://www.dfs.delhigovt.nic.in">www.dfs.delhigovt.nic.in</a>
- This fire safety certificate may not in any way be treated as regularization (Clause 2.8 of UBBL-2016) of unauthorized construction or Alteration (Clause 1.4.3 of UBBL- 2016), if any.
- 7. "The owner/occupier shall apply for renewal of this Fire Safety Certificate to the Director in form 'J' [sub-rule (1) of rule 37] along with a copy of this Certificate, six month prior to its expiry." The form is available on www.dfs.delhipgovt.nic.in
- This FSC is valid for on Select city Walk Mall Complex, except hotel and Multiplex in the complex.

# Annexure – 5

# Environment Clearance 2007

By Speed Post

No. 21-672/2006-1A -III

Government of India

Ministry of Environment and Forests

(I.A. Division)

Paryavaran Bhawan, CGO Complex, Lodhi Road New Delhi 110003 Dated: February 14, 2007

To

M/s Select Infrastructure Pvt. Ltd. 101, Kanchenjunga, 18, Barakhamba Road, New Delhi-110001

Subject: Environmental Clearance for construction of proposed Commercial Complex Select CITYWALK (SHOPPING MALL) at A-3 & F. I B, District Centre, Saket, New Delhi.

Sir

I am directed to refer to your application seeking prior environmental clearance for the above project under the EIA Notification 2006. The above proposal has been appraised as per prescribed procedure on the basis of the mandatory documents enclosed with the application viz., the Form I and IA, EMP, and the additional clarifications furnished in response to the observations of the Expert Appraisal Committee (EAC) constituted by the competent authority in its meeting held on 15-16 December, 2006.

- 2. The project proponent is proposing for development of Commercial complex Select CITYWALK at Plot No. A.3, District Centre, Saket, New Delhi. The project involves construction of Shopping Center, Cinemas, Serviced Apartments & Offices in total plot area of 15,884.00 sq. m.On plot A3, three basements, ground floor and seven upper floors will be constructed whereas on plot PI-B two basements and a Multiplex plus two basements will be constructed. The FAR as indicated is 44,673 sq. m. Total water requirement will be 502 cu. m. /day. and wastewater generation will be 297cu, m./day. A STP having capacity of 300 cu. m./day will be installed at site.
- 3. The EAC after due consideration of the relevant documents submitted by the project proponent and additional clarifications furnished in response to its observations have recommended the grant of environmental clearance for the project mentioned above subject to compliance with the EMP and other stipulated conditions. Accordingly, the Ministry hereby accords necessary environmental clearance for the project subject to the strict compliance with the specific and general conditions mentioned below:

## PART A-SPECIFIC CONDITIONS

### L. Construction Phase

- All required sanitary and hygienic measures should be in place before starting construction activities and to be maintained throughout the construction ii.
- Soil and ground water samples will be tested to ascertain that there is no threat to groundwater quality by leaching of heavy metals and other toxic
- A First Aid Room will be provided at the project site both during construction and operation of the project.
- Adequate drinking water and sanitary facilities should be provided for construction workers at the site. The safe disposal of wastewater and solid wastes generated during the construction phase should be ensured. with a higheren have
- The Secretary No. Disposal of muck including excavated naterial during construction phase should not create any adverse effects on the neighboring communities and be disposed off taking the necessary precautions for general safety and health aspects of people.
- Diesel power generating sets used during construction phase should be of enclosed type to prevent noise and should conform to rules made under Environment (Protection) Act 1986, prescribed for air and noise emission standards.
- Ambient noise levels should conform to commercial standards both during day and night when measured at boundary wall of the premises, incremental pollution loads on the ambient air and noise quality should be closely monitored during construction phase.
- Vehicles hired for bringing construction material at site should be in good condition and should have valid pollution under check(PUC) certificate and to conform to applicable air and noise emission standards.
- Construction spoils including bituminous material and other hazardous materials must not be allowed to contaminate watercourses and the dump sites for such material must be secured so that they should not leach into the ground water.
- Any hazardous waste generated during construction phase should be disposed of as per applicable Rules & norms with necessary approvals of the Delhi
- Regular supervision of the above and other measures for monitoring should be in place all through the construction phase so as to avoid disturbance to the

### II. Operation Phase

The environmental elearance recommended to the project is subject to the specific conditions as follows:

- Necessary possission of competent authority shall be taken to store diesel in the premises for operation of DG set.
- ii. Diesel power generating sets proposed as source of back up power for lifts and common area illumination should be of enclosed type and conform to rules made under Environment (Protection) Act 1986, prescribed for air and noise emission standards as per CPCB guidelines. Exhausts should be discharged by stack, raised to 4 meters above the rooftop.
- iii. During nighttime the noise levels measured at the boundary of the building shall be restricted to the permissible levels to comply with the prevalent regulations.
- Noise barriers should be provided at appropriate locations so as to ensure that the noise levels do not exceed the prescribed standards.
- Weep holes in the compound walls shall be provided to ensure natural drainage of rainwater in the catchments area.
- vi. The sewage treatment plants should be certified by an independent expert for efficiency as well as adequacy and should submit a report in this regard to the Ministry before the project is commissioned for operation. The wastewater should be treated to tertiary level and after treatment reused for flushing of toilets and gardening. Discharge of treated sewage, if any, shall conform to the norms & standards prescribed by Delhi Pollution Control Committee.
- vii. Oil & Grease trap shall be provided to remove oil and grease from the surface run off and suspended matter shall be removed in a settling tank before its utilization for rainwater harvesting.
- viii. The solid waste generated should be properly collected & segregated. Wet garbage should be composted and dry/inert solid waste should be disposed of for land filling.
- ix. Any hazardous waste including biomedical waste should be disposed of as per applicable Rules & norms with necessary approvals of the Delhi Pollution Control Committee.
- x. The green belt design along the periphery of the plot shall achieve attenuation factor conforming to the day and night noise standards prescribed for commercial land use. The open spaces inside the plot should be suitably landscaped and covered with vegetation of indigenous variety.
- xi Incremental pollution loads on the ambient air quality, noise and water quality should be periodically monitored after commissioning of the project.
- kii. The ground water levels and its quality should be monitored regularly in consultation with Central Ground Water Authority.
- aiii. A Report on the energy conservation measures should be prepared incorporating details about building materials & technology, R & U Factors etc and submitted to the Ministry in three months time.

xiv. The values of R & 1: for the building envelope should meet the requirements of the hot & humid climatic location. Details of the building envelope should be worked out and furnished in three months time.

#### PART B. GENERAL CONDITIONS

- i) The environmental safeguards contained in the documents should be implemented in letter and spirit.
- Provision should be made for the supply of kerosene or cooking gas and pressure cooker to the laborers during construction phase.
- All the laborers to be engaged for construction works should be screened for health and adequately treated before the issue of work permits.
- (v) 6 monthly monitoring reports should be submitted to the Ministry and its Regional Office.
- 5. Officials from the Regional Office of MOEF, Chandigarh who would be important to implementation of cuvironmental safeguards should be given full cooperation, facilities and documents / data by the project proponents during their inspection. A complete set of all the documents submitted to MoEF should be forwarded to the CCF, Regional office of MOEF, Chandigarh.
- In the case of any change(s) in the scope of the project, the project would require a fresh appraisal by this Ministry.
- 7. The Ministry reserves the right to add additional safeguard measures subsequently, if found necessary, and to take action including revoking of the environment clearance under the provisions of the Environment (Protection) Act, 1986, to ensure effective implementation of the suggested safeguard measures in a time bound and satisfactory manner.
- 8. All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department (if required), etc. shall be obtained by project proponents from the competent authorities.
- A copy of the environmental clearance letter would be marked to the local NGO(s), if any.
- 10. The project proponent should advertise in at least two local Newspapers widely circulated in the region, one of which shall be in the vernacular language informing that the project has been accorded environmental cleanance and copies of cleanance letters are available with the Delhi Pollution Control Committee and may also be seen on the website of the Ministry of Environment and Forests at <a href="http://www.envfor.nic.in">http://www.envfor.nic.in</a>. The advertisement should be made within 7 days from the day of issue of the clearance letter and a copy of the same should be forwarded to the Regional office of this Ministry at Chandigarh.
- These stipulations would be enforced among others under the provisions of the Water (Prevention and Control of Pollution) Act, 1974, the Air (Prevention and

control of Pollution) act 1981, the Environment (Protection) Act and 1986, the Public Liability (Insurance) Act, 1991

- 12 The project authority will enter in to MOU with all buyers of the property flats/shops etc. to ensure operation and maintenance of the assets handed over to the society formed by the residents/owners of the buildings.
- 13. Under the provisions of Environment (Protection) Act 1986, legal action shall be initiated agains the project proponent if it was found that construction of the project had started without obtaining environmental clearance.

(K.C. RATHORE) Additional Director (IA) rathore27@yahoo.com Tele: 24360789

Copy to: -

- The Secretary, Department of Environment, Government National Capital Territory of Delhi, Old Secretariat, I. P. Estate, New Delhi.
- The Member Secretary, Delhi Pollution Control Committee, ISBT Building, 4th Floor, Kashmere Gate, Delhi.
- 3. The CCF, Regional Office, Ministry of Environment & Forests, Chandigarh.
- IA Division, MOEF, New Delhi 110001.
- 5. Guard file:

(K. C. RATHORE) Additional Director (IA)

# Annexure – 6

# Airport Authority of India Permission



#### AIRPORT AUTHORITY OF INDIA

Rajiv Gandhi Bhavan Safdarjung Airpprt, New Delhi-11003

No.AAI/20012/835/2004 - ART

Dated, New Delhi the 20.08.04

To.

Select Infrastructure Ltd. M/s. Tevatia Chauhan & Sharma Architects (P) Ltd., 13-1, Bhawani Kunj, Behind D-11, Vasat Kunj, NEW DELHI.

Sub:- Issue of NOC . Case No.

1. Please refer to your letter No. - Dated - on the subject mentioned above.

This office has no objection to the construction of the proposed bldg. By Select Infrastructure Ltd.

here in after referred to as the applicant(s) at location plot No. A-3, District Centre, Saket, New Delhi to height 38.00 /M (in figures)Thirty Eight deci Zero /Metros (in words)

ABOVE GROUND LEVEL, so that the top of the proposed structure when erected shall not exceed 226.30 /M (site Elevation)+38.00 /M/ (Height of the structure) Le. 264.30 /M

ABOVE MEAN SEA LAVEL

- 3. This no objection certificate is being issued on the express understanding that the site-elevation reduced level (height above town sea level) via 226.30 /M, relative location of the proposed Bldg/Structure & its distances and Bearings from the ARD-Rumway ends, as tendered by the applicant (s) are correct. If, However, at any stage it is established that the said data as tendered by the said applicant is actually different from the one tendered & which could adversely affect aircraft operations, the structure or part(s) thereof in respect of which this 'NOC' is being issued will have to be demolished at his own cost as may be directed by the Airports Authority of India(N.A. Division). The applicant(s) is 'are therefore advised in his/their own interest to verify the elevation and other data furnished for the site, before embarking on the proposed construction.
- 4. The issue of the 'NOC' is further subject to the provisions of Section 9-A of the Indian Aircraft Act, 1934 and those of any a notifications issued thereunder from time to time and under which the applicant may be called upon by the Airports Authority of India(N.A. Division) to demolish in whole or in part the structure now being authorised vide this 'NOC'.
- No radio/TV Antenna, lighting arresters, starcase, Muritee, Overhead water tink and attachments of fixtures of any kirls shall project above the height indicated in para 2.

6 The use of oil fired of electric fired furnace is obligatory, within 8 Kms. Of the Aerodrome.

- 7. The certificate is valid for a period of three years from the date of its issue. If the building/structure/Chimney is not constructed & completed within the above membered period of three years he will be required to obtain a fresh 'No Objection Certificate' from the Chairman Airports Authority of India(NAD) and/or the Director of Aerodromes Northern Region. The date of completion of Building/Structure/Chimney should be intimated to the AAI(NAD) and/or Aerodromes Northern Region.
- No light or a combination of lights which by reason of its intensity, configuration of colour may cause confusion with the aeronautical ground lights of the Airport shall be installed at the site at may time during or after the construction of the building.

"NOC FOR HEIGHT CLEARANCE ONLY"

Day & Night markings with secondary power supply may be provided as per ICAO standards.

(S.K. AUDITTO)

Assit GENERAL MANAGER(NOC)
For Airports Authority of India

Cenv. to:

- The Regional Executive Director, AAI Northern Region IGI Airport. New Delhi-37 w.r.t. his letter No. AAI/NOC/2004/64/295-96 Dated 29,96.04
- Sr. Manager, Maps & Maps & Charts, AAI, (NAD), Hqm.
- 3. Guard file/Airport Director.

# <u>Annexure – 7</u>

# DDA Approval Letter for Expansion

# FORM- B-1 (Chapter 2, Para 2.3)

#### **GRANT OF SANCTION**

# Delhi Development Authority <u>Building Section</u>

File No.: **SZ/0110/19-20** Dated: **17 January, 2020** 

To,

Shashi Sharma Select Infrastructure Pvt Ltd A-3 District Centre Saket, Newdelhi. 110017

#### **GRANT OF SANCTION**

Sub: Sanction U/S 12 of the Delhi Development Act 1957

Dear Sir/Madam,

With reference to your application dated **01 October, 2019** for the grant of sanction to erect/ re-erect/add to/alteration in the building to carry out the development specified in the said application relating to Plot No. **A3 & P1B** Pocket No. -- Block No. -- Sector No. -- Situated in/at **SAKET, NEW DELHI.** I have to state that the same has been sanctioned on **17 January, 2020** by the Delhi Development Authority subject to the following conditions and corrections made on the plans:-

- 1) The plans are valid up to 16 day of month 1 year 2025
- 2) The construction will be undertaken as per sanctioned plan only and no deviation from the bye-laws will be permitted without prior sanction. Any deviation done against the bye-laws is liable to be demolished and the supervising Architect, engaged on the job will run the risk of having his license cancelled.
- 3) Violation of building bye-laws will not be compounded.
- 4) It will be duty of the owner of the plot and the Architect preparing the plan to ensure that the sanctioned plans are as per prevalent building bye-laws. If any infringement of the bye-laws remain unnoticed the Delhi Development Authority reserves the right to amend the plans as and when the infringement comes to its notice and Delhi Development Authority will stand indemnified against any claim on this account.
- 5) The party shall not occupy or permit it to occupy the building or use permit the building or part there of affected by any such work until occupancy certificate is issued by the sanctioning Authority.
- 6) Delhi Development Authority will stand indemnified and kept harmless from all proceedings in courts and before other authorities of all expenses/losses/claims which the Delhi Development Authority may incur or become liable to pay as a result or in consequences of the sanction accorded by it to these building plans.

Note: "This is a computer-generated document therefore does not require any signature or stamp."

- 7) The door and window leaves shall be fixed in such a way that they shall not when open project on any street.
- 8) The party will convert the house into dwelling units of each floor as per the approved parameters of the project and shall use the premises only for residential purpose.
- 9) The building shall not be constructed within minimum mandatory distance as specified in Indian Electricity Rules and as per the requirement of Delhi Vidut Board from the voltage lines running on any side of the site.
- 10) The land left open on consequences of their enforcement of the set back rule shall form part of the public street.
- 11) The thickness of outer walls will be maintained at least 0.23 mt. (9").
- 12) The basic levels should be got ascertained from the concerned at the site of the construction.
- 13) The owner will display boards of minimum size of 3 ft. X 4ft. indicating the following
  - i. Plot No. and location A3 & P1B (South Zone).
  - ii. Name of lesse/owner Shashi Sharma.
  - iii. Use of the property as per lease deed 24174.66.
  - iv. Date of sanction of Building Plan with No. CA/BP/0111/19-20(17 January, 2020)
  - v. Sanction valid up to 16 January, 2025
  - vi. Use of different floors and areas sanctioned --
  - vii. Name of the Architect & his address Goonmeet Singh Chauhan [K-47, Kailash Colony, New Delhi-110048].
  - viii. Name of the contractor and his address --
- 14) The provision of the display board on the construction site is a mandatory requirement and non-compliance of the same will invite a penalty of Rs. 5000/-.
- 15) It will be ensured that the construction / demolition work shall be carried out in such a manner that no disturbance/nuisance is caused to residents of the neighborhood.
- 16) It will be ensured by the owner and the Architect that during the construction the building plans sanctioned shall satisfy all the Environmental Conditions for Buildings and Constructions of Chapter 3, Annexure XIV of these Bye laws and as amended from time to time or any specific orders issued by the Govt.
- 17) Intimation of Completion of work up to Plinth Level, Plinth Level inspection and the issue of Plinth level Inspection shall be done as per procedures laid down in the Chapter 2 of these bye-laws.
- 18) The building shall be constructed strictly in accordance with the sanction plan as well as in accordance with the certificate submitted jointly by the owner/Architect/Structural Engineer for safety requirement as stipulated in Chapter 9 of these Building Bye-Laws, and the structural Design including safety from any natural hazards duly incorporated in the design of the building as per the Government Of India Notification issued time to time and Annexure VII of theses Bye Laws.
- 19) The mulba during the construction will be removed on weekly basis. If the same is not done, in that case the local body shall remove the mulba and the cost shall be borne by the owner of the plot.

- 20) During construction, it is mandatory on the part of the owner to properly screen the construction site of the main road by means of erecting a screen wall not less than 8 ft. in height from ground level which is to be painted to avoid unpleasant look from the road side. In addition to this a net or some other protective material shall be hoisted at the facades or the building to ensure that any falling material remains within the protected area.
- 21) Noise related activities will not be taken up for construction at night after 10.00 PM.
- 22)
- i. Every builder or owner shall put tarpaulin on scaffolding around the area of construction and the building. No person including builder, owner can be permitted to store any construction material particularly sand on any part of the street, roads in any colony.
- ii. The construction material of any kind that is stored in the site will be fully covered in all respects so that it does not disperse in the air in any form.
- iii. The construction material and debris shall be carried in the trucks or other vehicles which are fully covered and protected so as to ensure that the construction debris or the construction material does not get dispersed into the air or atmosphere, in any form whatsoever.
- iv. The dust emissions from the construction site should be completely controlled and all precautions taken in that behalf.
- v. The vehicles carrying construction material and construction debris of any kind should be cleared before it is permitted to ply on the road after unloading of such material.
- vi. Every worker working on the construction site and involved in loading, unloading and carriage of construction material and construction debris shall be provided with mask to prevent inhalation of dust particles.
- vii. Every owner and or builder shall be under obligation to provide all medical help, investigation and treatment to the workers involved in the construction of building and carry of construction material and construction debris relatable to dust emission.
- viii. It shall be the responsibility of every builder to transport construction material and debris waste to construction site, dumping site or any other place in accordance with rules and in terms of this order.
- ix. All to take appropriate measures and to ensure that the terms and conditions of the earlier order and these orders should strictly comply with by fixing sprinklers, creations of green air barriers.
- x. Compulsory use of wet jet in grinding and stone cutting.
- xi. Wind breaking walls around construction site.
- xii. All efforts to be made to increase the 'tree cover' area by planting large number of trees of various species depending upon the quality content of soil and other natural attendant circumstances.
- xiii. All the builders who are building commercial, residential complexes which are covered under the EIA Notification of 2006 shall provide green belt around the building that they construct.
- 23) The sanctioning authority approves Architectural Drawings/Development Control norms with respect to the Building Bye Laws and Master Plan provisions only. The technical drawings/documents submitted by the owner/consultant/Architect/Engineer/Structural Engineer/Landscape Architect /Urban Designer/Engineer for Utility Services are considered as part of the records/information supporting the building permit only. The responsibility of the correctness of information/application of technical provisions fully vests with the owner/consultant/ Architect/Engineer/Structural Engineer/Landscape Architect /Urban Designer/Engineer for Utility Services and shall be liable as per laws.
- The sanctioning authority approves Architectural Drawings/Development Control norms with respect to the Building Bye Laws and Master Plan provisions only. The technical drawings/documents submitted by the

owner/consultant/Architect/Engineer/Structural Engineer/Landscape Architect /Urban Designer/Engineer for Utility Services are considered as part of the records/information supporting the building permit only. The responsibility of the correctness of information/application of technical provisions fully vests with the owner/consultant/ Architect/Engineer/Structural Engineer/Landscape Architect /Urban Designer/Engineer for Utility Services and shall be liable as per laws.

- 25) No puncture, perforation, cutting, chiseling, trimming of any kind for any purpose are permitted in the structural members (beams / columns) submitted by the structural engineer as structural drawing for building permit in accordance with the relevant structural codes.
- 26) The sanction will be void ab initio if any material fact has been suppressed or mis-represented of if auxiliary conditions mentioned above are not complied.

Plot No.: A3 & P1B Pkt. No.: --

Block No.: -- Sector No.: --

Delhi.

Encl: One set of sanctioned plan.

Yours Faithfully

Name: PARVEEN KUMAR Designation: Assistant

Engineer

Organization : DELHI DEVELOPMENT

AUTHORITY

Date: 17-Jan-2020 13: 18:13

For Vice Chairman

Delhi Development Authority

# Annexure – 8

Environment
Clearance for
Expansion Project
2019

# F.No. 21-45/2019-IA-III Government of India Ministry of Environment, Forest and Climate Change (IA.III Section)

Indira Paryavaran Bhawan, Jor Bagh Road, New Delhi - 3

Date: 1st November, 2019

To.

M/s Select Infrastructure Private Limited Select City Walk, A-3, District Centre, Saket, Hauz Khas, Delhi - 110017

Subject: Expansion of "Commercial Complex SELECT CITY WALK (Shopping Mall)" at A-3 & P1-B, District Centre, Saket, New Delhi by M/s Select Infrastructure Private Limited - Environmental Clearance - reg.

Sir.

This has reference to your online proposal No. IA/DL/MIS/91578/2006 dated 15<sup>th</sup> May, 2019, submitted to this Ministry for grant of Environmental Clearance (EC) in terms of the provisions of the Environment Impact Assessment (EIA) Notification, 2006 under the Environment (Protection) Act, 1986.

- 2. The proposal for grant of environmental clearance to the project Expansion of "Commercial Complex SELECT CITY WALK (Shopping Mall)" at A-3 & P1-B, District Centre, Saket, New Delhi by M/s Select Infrastructure Private Limited, was considered by the Expert Appraisal Committee (Infra-2) in its 42<sup>nd</sup> Meeting held during 10-12 July, 2019 and 43<sup>nd</sup> meeting held during 20-22 August, 2019. The details of the project, as per the documents submitted by the project proponent, and also as informed during the above meeting are as under-
- (i) The project will be located at Latitude 28°31'44.03"N and Longitude 77°13'10.23"E.
- (ii) The Project is Expansion. The proposed project titled expansion of "Commercial Complex SELECT CITY WALK (Shopping Mall)" at A-3 & P1-B, District Centre, Saket, New Delhi has already been granted Environmental Clearance vide letter no. 21-672/2006-IA-III dated 14/02/2007 from MoEF&CC for the development of the "Commercial Complex SELECT CITY WALK (Shopping Mall)" at A-3 & P1-B, District Centre, Saket, New Delhi for FAR area of 44,623 sqm & Built-up area (Including basement area) of 1,07,671.51 sqm.
- (iii) Due to enhancement of FAR of the above said plot under MPD 2021, there is change in FAR, Non-FAR area and increase in FAR and built-up area. The built- up area of the project after expansion will be 1,18,079.00 sqm (including basement area). The activities of the project involve Shopping Centre/ Mall building, Service Apartment, Offices, Multiplex & Hotel. The changes are proposed in Shopping Centre/ Mall building only. The details of the building are as follows:

Particulars	Unit	As per Environmental Clearance granted in February, 2007	Existing Operational Details	Proposed Details	Total After Expansion
SubTotal Plot area as per EC -A	sqm	15,884.50	15,884.50	-	15,884.50
Landscape & Surface Plot Area-B	sqm	8,290.16	8,290.16	180	8,290.16
Total plot area (A+B)	sqm	24,174.66	24,174.66	120	24,174.66
G.C (Permissible)	sqm		11,275.31	74	11,275.31
G.C (Ach)	sqm		11,160.03	-	11,160.03

J. Bose:

FAR Permissible	sqm	1.51	45,020.55		52,328.55
Proposed FAR/Built- up area excluding Non-FAR area/Basement area	sqm	44,623	44,623	7,459.84	52,082.8400
		Non-FA	R AREA		
Third Basement Area	sqm		13,345.18		13,345.18
Second Basement Area	sqm	025	25,022.53	(-)2215.22	22,807,31
First Basement Area	sqm		24,680.8028	(-)2709.99	21,970.81
Total Basement area/ service area	sqm	-	63,048.5128	(-)4925.22	58,123.30
Other Non- FAR	sqm			7872.8640	7,872.8640
Built-up Area (FAR + Basement area + other Non- FAR)	sqm	(8)	1,07,671.51	10,407.49	1,18,079.000
Total Green Area	sqm		8,290.16		8,290.16
Open area	sqm		4,724.47	30	4,724.47
No. of shops	Nos.		183	30	213
No of Towers	Nos.	-	4	4	4
Maximum No. of Floors	Nos.	-	3B+G+7	3B+G+7	3B+G+7
Max. height of building (up to terrace level)	Nos.		38	38	38
No. of Basement	Nos.	3	3	3	3

- (iv) During the construction phase, total water requirement is expected to be 12 KLD which will be met by Saket Place Developer's Association. During the construction phase, mobile toilets will be provided during peak labour force. Waste water from labours shall be treated in Exiting STP.
- (v) The total water requirement after expansion will be 699 KLD. Out of which fresh water 354 KLD will be met by Saket Place Developer's Association and remaining water will be outsourced from STP water. The total waste water generation after expansion will be 245 KLD which shall be treated into Sewage Treatment Plants (STP) of total capacity 300 KLD (already installed). 220 KLD treated water will be used in flushing & Cooling. 125 KLD of outsourced treated water shall be used for gardening purpose. No treated water shall be discharge outside the project.
- (vi) The total solid waste generation after expansion will be 1.624 TPD. Out of which the biodegradable waste (0.65 TPD) shall be treated in Organic Waste Convertor provide within the complex, recyclable waste (0.487 TPD) and Plastic waste (0.487 TPD) will be handed over to NGO Chintan Environmental Research & Action Group and Used Oil of 62 lit/month shall be collected in leak proof containers at isolated place and then it will be given to approved recycler. E- Waste of 2-3 kg/month will be collected and given to approved recycler.
- (vii) The Total power requirement during construction phase will be met by 62.5 KVA DG sets. The total power requirement after expansion will be 5660 kW (Connected load: 6340 KVA) which will be provided by BSES, Delhi, D.G. Sets of capacities 3 x 2000 kVA & 2 x 1010 kVA has already been installed for back-up. To avoid the emissions, stack height of 6 m above roof level has already been provided to reduce the air emissions, meeting all the norms prescribed by CPCB.
- (viii) Rooftop rainwater of buildings will be collected in 17 RWH tanks of total 345.67 KLD capacity for harvesting after filtration.

- (ix) Parking facility for 1170 ECS for four wheelers and 222 for two wheelers is proposed to be provided against the requirement of 1125 ECS for four-wheeler & two-wheeler.
- (x) There are two Eco-sensitive areas within 10 km radius of the project i.e. Asola Wildlife Sanctuary is at a distance of 3.26 Km from the project site & Okhla Bird Sanctuary is at a distance 9.83 Km NEE from the project site. The ESZ boundary of Okhla Bird Sanctuary is 100 m to 1.27 Km & Asola Wildlife Sanctuary is 1 Km. Hence, NBWL Clearance is not required.
- (xi) Forest Clearance is not required.
- (xii) There is no court case pending against the project.
- (xiii) Investment cost of the project. The total estimated cost of the project is Rs. 428 Crores including cost of expansion which is Rs. 32 Crores.
- (xiv) Employment potential: Labourers during construction phase 150 nos. and after expansion total staff will be 1121 persons.
- (xv) Benefits of the project: Employment opportunities provided due to the project will lead to better quality of life and will also set a standard for future developments in the area. The project will provide direct and indirect employment opportunity. The project will also enhance the infrastructure facility of the area. Corporate Environment Responsibility will also be considered for the social benefits of the society. Well connected with network of public transport, local railways and cabs. Pollution free environment with proper drainage and sewage system. Easy access to airport and local Railway Station.
- The project/activity is covered under category 'B' of item 8(a) 'Building and Construction Projects' of the Schedule to the EIA Notification, 2006, and requires appraisal at State level. However due to absence of SEIAA/SEAC in Delhi, the proposal is appraised at Central Level.
- 4. The project proponent informed the EAC that the proposed project is expansion of "Commercial Complex SELECT CITY WALK (SHOPPING MALL)" at A-3 & P1-B, District Centre, Saket, New Delhi. The project will be developed by M/s Select Infrastructure Pvt Ltd. Delhi Development Authority had handed over the land in 2004 on lease hold basis to M/s Select Infrastructure Pvt. Ltd. for development of the commercial complex, which was converted into free hold in 2009. The project has already been granted Environmental Clearance vide letter No. 21-672/2006-IA-III dated 14.02.2007 from MoEF&CC for the development of the "Commercial Complex SELECT CITY WALK (SHOPPING MALL)" at A-3 & P1-B, District Centre, Saket, New Delhi for FAR area of 44,623 sqm (excluding basement area) & Built-up area (Including basement area) of 1,07,671.51 sqm The project is already operational Commercial Complex. These include activities such as Shopping Centre/ Mall building, Service Apartment, Offices, Multiplex. Due to enhancement of FAR of the above said plot under MPD 2021, there is change in FAR, Non-FAR area and increase in FAR and built-up area. The built-up area of the project after expansion will be 1,18079.00 sqm (including basement area).

The project proponent informed the EAC that at present water supply in complex is being made through Saket Place Developer's Association (duly authorized by DDA) which is sourcing water through approved tube wells and water tankers under mutual legal agreement with DDA. The project proponent further informed that they have already got water scheme sanctioned from DJB for water connection and requisite fee of Rs. 29,09,250/-(Rs. Twenty Nine Lacs Nine Thousand Two Hundred Fifty only) has already been paid to Delhi Jal Board in the year 2010.

The EAC also deliberated on the certified compliance report letter No. 4-251/2007-RO(NZ)/111 dated 02.05.2019 issued by the MoEF&CC's Regional Office (CR), Lucknow. As per Compliance report, it is observed that PAs have complied or are in process or

J. hone.

complying the environmental conditions stipulated for this project. A discrepancy has been noticed as project has got occupancy certificate from Delhi Development Authority, Delhi (vide letter No.113(62)04/13010/93 dated 20.08.2007) whereas CTE submitted (letter no. DPCC/CMC/2013/31913) is valid from 03.04.2013, for one year. STP adequacy report has been obtained from Delhi College of Engineering Delhi vide no. Adequacy/Env/2009/07/01 dated 02.07.2009. As per the submitted document, it has been found that under Section 15, 16 & 19 of Environment (Protection) Act, 1986, a complaint filed in the court of Chief Metropolitan Magistrate, Delhi vide complaint No. 2008/0240RO297302208 dated 06.05.2008. Where, PAs have been found violating the norms by the court and agreement has been settled with DPCC dated 02.11.2012 where they have deposited Rs. 14,00,000/vide DD No. 464452 dated 21.11.2012 as compensation and then above mentioned CTE has been granted to PAs by DPCC. After that they have been granted above mentioned CTOs by DPCC.

5. The EAC in its 43<sup>rd</sup> meeting held on 20-22 August, 2019, based on the information submitted and clarifications provided by the Project Proponent and detailed discussions held on all the issues, recommended the project for grant of environmental clearance with stipulated specific conditions along with other Standard EC Conditions as specified by the Ministry vide OM dated 4<sup>th</sup> January, 2019 for the said project/activity, while considering for accord of environmental clearance. As per recommendations of the EAC, the Ministry of Environment, Forest and Climate Change hereby accords Environmental Clearance to the project Expansion of "Commercial Complex SELECT CITY WALK (Shopping Mall)" at A-3 & P1-B, District Centre, Saket, New Delhi by M/s Select Infrastructure Private Limited, under the provisions of the EIA Notification, 2006 and amendments/circulars issued thereon, and subject to the specific and general conditions as under:-

#### A. Specific Conditions:

- (i) Consent to Establish/Operate for the project shall be obtained from the State Pollution Control Board as required under the Air (Prevention and Control of Pollution) Act, 1981 and the Water (Prevention and Control of Pollution) Act, 1974.
- (ii) The project proponent shall provide for adequate fire safety measures and equipment as per National Building Code/required by Fire Service Act of the State and instructions issued by the local Authority/Directorate of fire, from time to time. Further, the project proponent shall take necessary permission/NOC regarding fire safety from Competent Authority as required.
- (iii) The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws.
- (iv) As proposed, fresh water requirement from Saket Place Developers Association shall not exceed 240 KLD. Consent to Operate (CTO)/Occupancy Certificate shall be issued only after getting necessary permission for required water supply from DJB/concerned authority.
- (v) Sewage shall be treated in the STP based on Extended Aeration Technology with tertiary treatment i.e. Ultra Filtration. The treated effluent from STP shall be recycled/re-used for flushing & HVAC Cooling. As proposed, no excess treated water shall be discharge to Municipal drain.
- (vi) The project proponents would devise a monitoring plan to the satisfaction of the State Pollution Control Board so as to continuously monitor the treated waste water being used for flushing in terms of faecal coliforms and other pathogenic bacteria.
- (vii) The project proponents would commission a third party study on the implementation of conditions related to quality and quantity of recycle and reuse of treated water, efficiency of treatment systems, quality of treated water being supplied for flushing (specially the bacterial counts), comparative bacteriological studies from toilet seats

S. Bose

- using recycled treated waters and fresh waters for flushing, and quality of water being supplied through spray faucets attached to toilet seats.
- (viii) The local bye-law provisions on rain water harvesting should be followed. If local bye-law provision is not available, adequate provision for storage and recharge should be followed as per the Ministry of Urban Development Model Building Byelaws, 2016. As proposed, 17 no. of rain water harvesting recharge pits shall be provided for rain water harvesting after filtration as per CGWB guidelines.
- (ix) Separate wet and dry bins must be provided in each unit and at the ground level for facilitating segregation of waste. Solid waste shall be segregated into wet garbage and inert materials. Wet garbage shall be composted in Organic Waste Converter. As proposed 50 sqm area shall be provided for solid waste management within the premises which will include area for segregation, composting. The inert waste from project will be sent to dumping site.
- (x) Traffic Management Plan as submitted shall be implemented in letter and spirit. Further, a detailed traffic management and traffic decongestion plan shall be drawn up to ensure that the current level of service of the roads within a 05 kms radius of the project is maintained and improved upon after the implementation of the project. This plan should be based on cumulative impact of all development and increased habitation being carried out or proposed to be carried out by the project or other agencies in this 05 kms radius of the site in different scenarios of space and time. Traffic management plan shall be duly validated and certified by the State Urban Development department and the P.W.D.J competent authority for road augmentation and shall also have their consent to the implementation of components of the plan which involve the participation of these departments.
- (xi) No tree cutting/transplantation of existing trees has been proposed in the instant project. A minimum of 1 tree for every 80 sqm of land should be planted and maintained. The landscape planning should include plantation of native species. The plantation species should be carefully chosen to avoid bird nesting and to improve pollution control and noise control measures. Water intensive and/or invasive species should not be used for landscaping. As proposed 8.290.16 sqm (34.30% of total area) area shall be provided for green area development.
- (xii) The company shall draw up and implement corporate social Responsibility plan as per the Company's Act of 2013. As per the Ministry's Office Memorandum F.No. 22-65/2017-IA.III dated 1<sup>st</sup> May, 2018, and proposed by the project proponent, an amount of Rs. 0.32 Crore (@ 1.00% of project Cost) shall be earmarked under Corporate Environment Responsibility (CER) for the activities such as drinking water supply, plantation and horticulture and skill development & computer education. The activities proposed under CER shall be restricted to the affected area around the project. The entire activities proposed under the CER shall be treated as project and shall be monitored. The monitoring report shall be submitted to the Regional Office as a part of half yearly compliance report, and to the District Collector. It should be posted on the website of the project proponent.

#### B. Standard Conditions:

#### Statutory compliance:

- i. The project proponent shall obtain all necessary clearance/ permission from all relevant agencies including town planning authority before commencement of work. All the construction shall be done in accordance with the local building byelaws.
- The approval of the Competent Authority shall be obtained for structural safety of buildings due to earthquakes, adequacy of firefighting equipment etc as per National Building Code including protection measures from lightening etc.
- The project proponent shall obtain the necessary permission for drawl of ground water / surface water required for the project from the competent authority.

J. Bose-

- iv. A certificate of adequacy of available power from the agency supplying power to the project along with the load allowed for the project should be obtained.
- v. All other statutory clearances such as the approvals for storage of diesel from Chief Controller of Explosives, Fire Department, Civil Aviation Department shall be obtained, as applicable, by project proponents from the respective competent authorities.
- The provisions of the Solid Waste Management Rules, 2016, e-Waste (Management) Rules, 2016, and the Plastics Waste Management Rules, 2016, shall be followed.
- The project proponent shall follow the ECBC/ECBC-R prescribed by Bureau of Energy Efficiency, Ministry of Power strictly.

#### II. Air quality monitoring and preservation:

- Notification GSR 94(E) dated 25.01.2018 of MoEF&CC regarding Mandatory Implementation of Dust Mitigation Measures for Construction and Demolition Activities for projects requiring Environmental Clearance shall be complied with.
- A management plan shall be drawn up and implemented to contain the current exceedance in ambient air quality at the site.
- iii. The project proponent shall install system to carryout Ambient Air Quality monitoring for common/criterion parameters relevant to the main pollutants released (e.g. PM<sub>10</sub> and PM<sub>2.5</sub>) covering upwind and downwind directions during the construction period.
- iv. Diesel power generating sets proposed as source of backup power should be of enclosed type and conform to rules made under the Environment (Protection) Act, 1986. The height of stack of DG sets should be equal to the height needed for the combined capacity of all proposed DG sets. Use of low sulphur diesel. The location of the DG sets may be decided with in consultation with State Pollution Control Board.
- v. Construction site shall be adequately barricaded before the construction begins. Dust, smoke & other air pollution prevention measures shall be provided for the building as well as the site. These measures shall include screens for the building under construction, continuous dust/ wind breaking walls all around the site (at least 3 meter height). Plastic/tarpaulin sheet covers shall be provided for vehicles bringing in sand, cement, murram and other construction materials prone to causing dust pollution at the site as well as taking out debris from the site.
- Sand, murram, loose soil, cement, stored on site shall be covered adequately so as to prevent dust pollution.
- vii. Wet jet shall be provided for grinding and stone cutting.
- Unpaved surfaces and loose soil shall be adequately sprinkled with water to suppress dust.
- ix. All construction and demolition debris shall be stored at the site (and not dumped on the roads or open spaces outside) before they are properly disposed. All demolition and construction waste shall be managed as per the provisions of the Construction and Demolition Waste Management Rules 2016.
- x. The diesel generator sets to be used during construction phase shall be low sulphur diesel type and shall conform to rules made under the Environment (Protection) Act, 1986.
- xi. The gaseous emissions from DG set shall be dispersed through adequate stack height as per CPCB standards. Acoustic enclosure shall be provided to the DG sets to mitigate the noise pollution. Low sulphur diesel shall be used. The location of the DG set and exhaust pipe height shall be as per the provisions of the Central Pollution Control Board (CPCB) norms.
- xii. For indoor air quality the ventilation provisions as per National Building Code of India.

S. Base:

#### III. Water quality monitoring and preservation:

- The natural drain system should be maintained for ensuring unrestricted flow of water. No construction shall be allowed to obstruct the natural drainage through the site, on wetland and water bodies. Check dams, bio-swales, landscape, and other sustainable urban drainage systems (SUDS) are allowed for maintaining the drainage pattern and to harvest rain water.
- Buildings shall be designed to follow the natural topography as much as possible.
   Minimum cutting and filling should be done.
- iii. The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports.
- iv. A certificate shall be obtained from the local body supplying water, specifying the total annual water availability with the local authority, the quantity of water already committed, the quantity of water allotted to the project under consideration and the balance water available. This should be specified separately for ground water and surface water sources, ensuring that there is no impact on other users.
- v. At least 20% of the open spaces as required by the local building bye-laws shall be pervious. Use of Grass pavers, paver blocks with at least 50% opening, landscape etc. would be considered as pervious surface.
- vi. Installation of dual pipe plumbing for supplying fresh water for drinking, cooking and bathing etc and other for supply of recycled water for flushing, landscape irrigation, car washing, thermal cooling, conditioning etc. shall be done.
- Use of water saving devices/ fixtures (viz. low flow flushing systems; use of low flow faucets tap aerators etc) for water conservation shall be incorporated in the building plan.
- viii. Separation of grey and black water should be done by the use of dual plumbing system. In case of single stack system separate recirculation lines for flushing by giving dual plumbing system be done.
- ix. Water demand during construction should be reduced by use of pre-mixed concrete, curing agents and other best practices referred.
- X. A rain water harvesting plan needs to be designed where the recharge bores of minimum one recharge bore per 5,000 square meters of built up area and storage capacity of minimum one day of total fresh water requirement shall be provided. In areas where ground water recharge is not feasible, the rain water should be harvested and stored for reuse. The ground water shall not be withdrawn without approval from the Competent Authority.
- xi. All recharge should be limited to shallow aquifer.
- xii. No ground water shall be used during construction phase of the project.
- xiii. Any ground water dewatering should be properly managed and shall conform to the approvals and the guidelines of the CGWA in the matter. Formal approval shall be taken from the CGWA for any ground water abstraction or dewatering.
- xiv. The quantity of fresh water usage, water recycling and rainwater harvesting shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Regional Office, MoEF&CC along with six monthly Monitoring reports.
- No sewage or untreated effluent water would be discharged through storm water drains.
- xvi. Onsite sewage treatment of capacity of treating 100% waste water to be installed. The installation of the Sewage Treatment Plant (STP) shall be certified by an

J. Brose.

independent expert and a report in this regard shall be submitted to the Ministry before the project is commissioned for operation. Treated waste water shall be reused on site for landscape, flushing, cooling tower, and other end-uses. Excess treated water shall be discharged as per statutory norms notified by Ministry of Environment, Forest and Climate Change. Natural treatment systems shall be promoted.

- xvii. Periodical monitoring of water quality of treated sewage shall be conducted. Necessary measures should be made to mitigate the odour problem from STP.
- xviii. Sludge from the onsite sewage treatment, including septic tanks, shall be collected, conveyed and disposed as per the Ministry of Urban Development, Central Public Health and Environmental Engineering Organization (CPHEEO) Manual on Sewerage and Sewage Treatment Systems, 2013.

#### IV. Noise monitoring and prevention:

- i. Ambient noise levels shall conform to residential area/commercial area/industrial area/silence zone both during day and night as per Noise Pollution (Control and Regulation) Rules, 2000. Incremental pollution loads on the ambient air and noise quality shall be closely monitored during construction phase. Adequate measures shall be made to reduce ambient air and noise level during construction phase, so as to conform to the stipulated standards by CPCB / SPCB.
- Noise level survey shall be carried as per the prescribed guidelines and report in this
  regard shall be submitted to Regional Officer of the Ministry as a part of six-monthly
  compliance report.
- Acoustic enclosures for DG sets, noise barriers for ground-run bays, ear plugs for operating personnel shall be implemented as mitigation measures for noise impact due to ground sources.

#### V. Energy Conservation measures:

- Compliance with the Energy Conservation Building Code (ECBC) of Bureau of Energy Efficiency shall be ensured. Buildings in the States which have notified their own ECBC, shall comply with the State ECBC.
- Outdoor and common area lighting shall be LED.
- iii. Concept of passive solar design that minimize energy consumption in buildings by using design elements, such as building orientation, landscaping, efficient building envelope, appropriate fenestration, increased day lighting design and thermal mass etc. shall be incorporated in the building design. Wall, window, and roof u-values shall be as per ECBC specifications.
- iv. Energy conservation measures like installation of CFLs/ LED for the lighting the area outside the building should be integral part of the project design and should be in place before project commissioning.
- v. Solar, wind or other Renewable Energy shall be installed to meet electricity generation equivalent to 1% of the demand load or as per the state level/ local building bye-laws requirement, whichever is higher.
- vi. Solar power shall be used for lighting in the apartment to reduce the power load on grid. Separate electric meter shall be installed for solar power. Solar water heating shall be provided to meet 20% of the hot water demand of the commercial and institutional building or as per the requirement of the local building bye-laws, whichever is higher. Residential buildings are also recommended to meet its hot water demand from solar water heaters, as far as possible.

#### VI. Waste Management:

J. Sose

- A certificate from the competent authority handling municipal solid wastes, indicating the existing civic capacities of handling and their adequacy to cater to the M.S.W. generated from project shall be obtained.
- Disposal of muck during construction phase shall not create any adverse effect on the neighbouring communities and be disposed taking the necessary precautions for general safety and health aspects of people, only in approved sites with the approval of competent authority.
- Organic waste compost/ Vermiculture pit/ Organic Waste Converter within the premises with a minimum capacity of 0.3 kg /person/day must be installed.
- All non-biodegradable waste shall be handed over to authorized recyclers for which a written tie up must be done with the authorized recyclers.
- Any hazardous waste generated during construction phase, shall be disposed off as per applicable rules and norms with necessary approvals of the State Pollution Control Board.
- vi. Use of environment friendly materials in bricks, blocks and other construction materials, shall be required for at least 20% of the construction material quantity. These include Fly Ash bricks, hollow bricks, AACs, Fly Ash Lime Gypsum blocks, Compressed earth blocks, and other environment friendly materials.
- vii. Fly ash should be used as building material in the construction as per the provision of Fly Ash Notification of September, 1999 and amended as on 27<sup>th</sup> August, 2003 and 25<sup>th</sup> January, 2016. Ready mixed concrete must be used in building construction.
- viii. Any wastes from construction and demolition activities related thereto shall be managed so as to strictly conform to the Construction and Demolition Waste Management Rules, 2016.
- ix. Used CFLs and TFLs should be properly collected and disposed off/sent for recycling as per the prevailing guidelines/ rules of the regulatory authority to avoid mercury contamination.

#### VII. Green Cover:

 Topsoil should be stripped to a depth of 20 cm from the areas proposed for buildings, roads, paved areas, and external services. It should be stockpiled appropriately in designated areas and reapplied during plantation of the proposed vegetation on site.

#### VIII. Transport

- i. A comprehensive mobility plan, as per MoUD best practices guidelines (URDPFI), shall be prepared to include motorized, non-motorized, public, and private networks. Road should be designed with due consideration for environment, and safety of users. The road system can be designed with these basic criteria.
  - Hierarchy of roads with proper segregation of vehicular and pedestrian traffic.
  - b. Traffic calming measures.
  - c. Proper design of entry and exit points.
  - d. Parking norms as per local regulation.
- ii. Vehicles hired for bringing construction material to the site should be in good condition and should have a pollution check certificate and should conform to applicable air and noise emission standards be operated only during non-peak hours.

#### IX. Human health issues:

- All workers working at the construction site and involved in loading, unloading, carriage of construction material and construction debris or working in any area with dust pollution shall be provided with dust mask.
- ii. For indoor air quality the ventilation provisions as per National Building Code of India.

S. Bose

- Emergency preparedness plan based on the Hazard identification and Risk Assessment (HIRA) and Disaster Management Plan shall be implemented.
- iv. Provision shall be made for the housing of construction labour within the site with all necessary infrastructure and facilities such as fuel for cooking, mobile toilets, mobile STP, safe drinking water, medical health care, crèche etc. The housing may be in the form of temporary structures to be removed after the completion of the project.
- Occupational health surveillance of the workers shall be done on a regular basis.
- vi. A First Aid Room shall be provided in the project both during construction and operations of the project.

#### X. Corporate Environment Responsibility:

- i. The company shall have a well laid down environmental policy duly approved by the Board of Directors. The environmental policy should prescribe for standard operating procedures to have proper checks and balances and to bring into focus any infringements/deviation/violation of the environmental / forest / wildlife norms / conditions. The company shall have defined system of reporting infringements / deviation / violation of the environmental / forest / wildlife norms / conditions and / or shareholders / stake holders. The copy of the board resolution in this regard shall be submitted to the MoEF&CC as a part of six-monthly report.
- ii. A separate Environmental Cell both at the project and company head quarter level, with qualified personnel shall be set up under the control of senior Executive, who will directly report to the head of the organization.
- Action plan for implementing EMP and environmental conditions along with responsibility matrix of the company shall be prepared and shall be duly approved by competent authority. The year wise funds earmarked for environmental protection measures shall be kept in separate account and not to be diverted for any other purpose. Year wise progress of implementation of action plan shall be reported to the Ministry/Regional Office along with the Six Monthly Compliance Report.

#### XI. Miscellaneous:

- The project proponent shall prominently advertise it at least in two local newspapers
  of the District or State, of which one shall be in the vernacular language within seven
  days indicating that the project has been accorded environment clearance and the
  details of MoEFCC/SEIAA website where it is displayed.
- ii. The copies of the environmental clearance shall be submitted by the project proponents to the Heads of local bodies, Panchayats and Municipal Bodies in addition to the relevant offices of the Government who in turn has to display the same for 30 days from the date of receipt.
- The project proponent shall upload the status of compliance of the stipulated environment clearance conditions, including results of monitored data on their website and update the same on half-yearly basis.
- iv. The project proponent shall submit six-monthly reports on the status of the compliance of the stipulated environmental conditions on the website of the ministry of Environment, Forest and Climate Change at environment clearance portal.
- v. The project proponent shall submit the environmental statement for each financial year in Form-V to the concerned State Pollution Control Board as prescribed under the Environment (Protection) Rules, 1986, as amended subsequently and put on the website of the company.
- vi. The project proponent shall inform the Regional Office as well as the Ministry, the date of financial closure and final approval of the project by the concerned authorities, commencing the land development work and start of production operation by the project.

- vii. The project authorities must strictly adhere to the stipulations made by the State Pollution Control Board and the State Government.
- viii. The project proponent shall abide by all the commitments and recommendations made in the EIA/EMP report and commitment made during their presentation to the Expert Appraisal Committee.
- No further expansion or modifications in the plant shall be carried out without prior approval of the Ministry of Environment, Forest and Climate Change (MoEF&CC).
- Concealing factual data or submission of false/fabricated data may result in revocation of this environmental clearance and attract action under the provisions of Environment (Protection) Act, 1986.
- The Ministry may revoke or suspend the clearance, if implementation of any of the above conditions is not satisfactory.
- xii. The Ministry reserves the right to stipulate additional conditions if found necessary. The Company in a time bound manner shall implement these conditions.
- xiii. The Regional Office of this Ministry shall monitor compliance of the stipulated conditions. The project authorities should extend full cooperation to the officer (s) of the Regional Office by furnishing the requisite data / information/monitoring reports.
- xiv. The above conditions shall be enforced, inter-alia under the provisions of the Water (Prevention & Control of Pollution) Act, 1974, the Air (Prevention & Control of Pollution) Act, 1981, the Environment (Protection) Act, 1986, Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016, and the Public Liability Insurance Act, 1991 along with their amendments and Rules and any other orders passed by the Hon'ble Supreme Court of India / High Courts and any other Court of Law relating to the subject matter.
- xv. Any appeal against this EC shall lie with the National Green Tribunal, if preferred, within a period of 30 days as prescribed under Section 16 of the National Green Tribunal Act, 2010.
- This issues with the approval of the Competent Authority.

(Dr. Subrata Bose) Scientist F

#### Copy to:

- The Secretary, Department of Environment, Government of Delhi, New Delhi.
- The Addl. Principal Chief Conservator of Forests (C), Ministry of Environment, Forests and Climate Change, Kendriya Bhavan, 5th Floor, Sector-H, Aliganj, Lucknow - 226024.
- The Chairman, Central Pollution Control Board Parivesh Bhavan, CBD-cum-Office Complex, East Arjun Nagar, New Delhi - 110 032.
- The Member Secretary, Delhi Pollution Control Committee, Department of Environment, Government of N.C.T. Delhi, 4<sup>th</sup> Floor, ISBT Building, Kashmere Gate, Delhi.
- Monitoring Cell, MoEF&CC, Indira Paryavaran Bhavan, New Delhi.
- Guard File/ Record File/ Notice Board.
- MoEFCC website.

(Dr. Subrata Bose)
Scientist F

# Annexure – 9

# Monitoring Reports



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

(For the Month of March- 2023)

Client Details			Sample Details		
Name	M/s. Select City	walk Mall a unit of	Sample Code	CCI////23/C4/\$Cb4/661 8 662	
Nume	Select Infrastru	cture Pvt. Limited	Sample Code	GCI/V/23/C4/SCM/AA1 & AA2	
	Select Infrastructure Pvt. Ltd., Select		Location	As Per Table	
Address	Citywalk, A-3, [	District Centre, Saket,	Quantity	NA	
	New Delhi – 110017		Date of Sampling	24/03/2023	
Sampling [	Done By	Mr. Kartik	Sampling Instrument	RDS, FPS	
Analysis Starts on 27/03/2023		27/03/2023	Sampling Method	IS 5182 : Part 5 : 1975	
Analysis C	ompletion On	01/04/2023	Sample Received Date	27/03/2023	

#### **AMBIENT AIR MONITORING RESULTS**

			Re	sults		
Sr. No.	Parameters	Unit	Near Main Gate	Back Side (Near STP)	Permissible Limit as per NAAQS	Reference Method
1.	Particulate Matter (PM <sub>10</sub> )	µg/m³	62.5	64.9	100	IS 5182 : Part 23 : 2006
2.	Particulate Matter (PM <sub>2.5</sub> )	µg/m³	21.8	23.5	60	IS 5182 : Part 24 : 2019
3.	Sulfur Dioxide (SO <sub>2</sub> )	µg/m³	6.4	9.2	80	IS 5182 : Part 2 : 2001
4.	Oxides of Nitrogen(NOx)	µg/m³	9.0	12.8	80	IS 5182 : Part 6 : 2006
5.	Carbon Monoxide CO	mg/m³	0.1	0.4	2.0	IS 5182 : Part 10 : 1999
6.	Ozone as O <sub>3</sub>	µg/m³	<20	<20	100	NAAQS Guidelines
7.	Lead as Pb	µg/m³	<0.05	<0.05	1.0	NAAQS Guidelines
8.	Nickel as Ni	ng/m³	<1.0	<1.0	20	NAAQS Guidelines
9.	Arsenic as As	ng/m³	<0.5	<0.5	6.0	NAAQS Guidelines
10.	Ammonia as NH3	µg/m³	<20	<20	400	NAAQS Guidelines
11.	Benzene , C6H6	µg/m³	<0.5	<0.5	5.0	IS 5182 (Part 11):2006
12.	Benzo (a) Pyrene	ng/m³	<0.05	<0.05	1.0	Gas Chromatography



Date: 01/04/2023

#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Goth Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Celt: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

**NEW DELHI** 

GOA PUNE

BENGALURU

U.K. HYDERABAD : OVERSEAS :

KOLKATA

DHARWAD

MUMBAI PORT BLAIR

AUSTRALIA OMAN KUWAIT AFRICA

VIETNAM

BANGLADESH

MYANMAR



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

(For the Month of March-2023)

Client details			Sample Details		
Name	M/s. Select Citywalk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/N1- N4	
	Select Infrastructure Pvt. Ltd., Select		Location	As per table	
Address	Citywalk, A-3, District Centre,		Nature of Sample	Noise	
	Saket, New Delhi – 110017		Date of Sampling	24/03/2023	
Sampling Done By Mr. Kartik Sampling Instrument Sound Level Meter			Lutron/SL-4001 SD inst.		
		Sound Level Meter	Sampling Method	Manual	

#### **NOISE MONITORING RESULTS**

٠.		Day Time dB (A) Leg		Night Time dB (A) Leg	
Sr. No.	Location Name	Results	CPCB Permissible	Results	CPCB Permissible
			Limit		Limit
1.	Pushpa nagar	57.9	65	52.5	55
2.	Malviya nagar	52.6	55	45.2	45
3.	CPWP Office	55.3	55	43.8	45
4.	Madan Gir	56.4	55	41.6	45

Remark: Results are within Standard as per CPCB Permissible limit.



Date: 01/04/2023

#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Goth Main Road, Vadodara - 390 021 (Gujarat), INDIA. R&D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com : ALSO AT :

**NEW DELHI** BENGALURU

**HYDERABAD** : OVERSEAS :

KOLKATA

DHARWAD

MUMBAI

PORT BLAIR

AUSTRALIA

OMAN

KUWAIT

**AFRICA** 

VIETNAM

BANGLADESH

MYANMAR

SRI LANKA



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/ G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

(For the Month of March-2023)

Client details			Sample Details		
Name	M/s. Select Citywalk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/N5- N6	
Select Infrastructure		tructure Pvt. Ltd., Select	Location	As per table	
Address	Citywalk, A-3, District Centre,		Nature of Sample	Noise	
	Saket, New Delhi – 110017		Date of Sampling	24/03/2023	
Sampling Done By       Mr. Kartik         Sampling Instrument       Sound Level Meter			Lutron/SL-4001 SD inst.		
		Sound Level Meter	Sampling Method	Manual	

#### NOISE MONITORING RESULTS

		Day Time dB (A) Leg		
Sr. No.	Location Name	Results	CPCB Permissible Limit	
5.	D.G. Sets	86.4		
J.	(Inside acoustic enclosure)	00.4	Minimum 25 dB(A)	
,	D.G. Sets (1 meter distance from	/0.1	insertion loss	
6.	Outside acoustic enclosure)	68.1		



Date: 01/04/2023

#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Goth Main Road, Vadodara - 390 021 (Gujarat), INDIA. R&D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

Date: 01/04/2023

#### (For the Month of March-2023)

Client Details		Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST1
	Select Infrastructure Pvt. Ltd., Select City walk,		Batch/Location	As per Table
Address		tre, Saket, New Delhi – 110017	Nature of Sample	Stack
	7 O, Disilier Corr	iic, sakci, iic v Beiiii 110017	Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Sta	ırts on	27/03/2023	Companiin or AA akka ad	Isokinetic Sampling,
Analysis Completion On		01/04/2022	Sampling Method	IS:11255,PART-1,2,3
Analysis Co	ompletion On	01/04/2023	Sample Received Date	27/03/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 1	
2	Rated Capacity	2000	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	33161054	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of the Plant(Hrs/Day)	As & When Required	-
8	Capacity on Sampling Day	980	kW
9	Stack Identification	Stack attached to D.G. Set No. 1	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	250	Liter/Hr.
16	Flue Gas Temperature	290	°C
17	Velocity	15.4	m/s
18	Gas Volume	4756	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA. R&D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : **NEW DELHI** GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS :

AUSTRALIA OMAN KUWAIT

AFRICA

VIETNAM

BANGLADESH

MYANMAR

SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### ANALYSIS REPORT

(For the Month of March-2023)

Client Detai	ls		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST1
	Select Infrastructure Pvt. Ltd., Select City walk,		Batch/Location	As per Table
Address			Nature of Sample	Stack
	A-3, District Centre, Saket, New Delhi – 110017		Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Sta	rts on	27/03/2023	Common line or AA o He o al	Isokinetic Sampling,
Analysis Completion On		01/04/0000	Sampling Method	IS:11255,PART-1,2,3
Analysis Co	mpletion On	01/04/2023	Sample Received Date	27/03/2023

#### **STACK MONITORING RESULTS**

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	21.1	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	11.8	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	21.0	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	6.3	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thMarch, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 01/04/2023

#### **Authorized Signatory**

SRI LANKA

UAE

• Analysis is subject to the condition In Which the Sample Is received at our Laboratory.

**AFRICA** 

- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

KUWAIT

OMAN

AUSTRALIA

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

BANGLADESH

MYANMAR

VIETNAM



AUSTRALIA

KUWAIT

OMAN

AFRICA

## GREEN CIRCLE, INC.

Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Deihi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

Date: 01/04/2023

SRI LANKA

UAE

MYANMAR

#### **ANALYSIS REPORT**

#### (For the Month of March-2023)

Client Detail	Client Details		Sample Details	
Name  M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST2	
		5	Batch/Location	As per Table
Address	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack
			Sampling Instrument	Stack Monitoring Kit
Sampling Do	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Starts on 27/03,		27/03/2023	Samuelina Madhad	Isokinetic Sampling,
Analysis Completion On 0		01./04/0002	Sampling Method	IS:11255,PART-1,2,3
		01/04/2023	Sample Received Date	27/03/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 2	
2	Rated Capacity	1010	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	25311742	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of the Plant(Hrs/Day)	As & When Required	-
8	Capacity on Sampling Day	534	kW
9	Stack Identification	Stack attached to D.G. Set No. 2	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	130	Liter/Hr.
16	Flue Gas Temperature	265	°C
17	Velocity	15.6	m/s
18	Gas Volume	4286	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

BANGLADESH

VIETNAM



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

#### (For the Month of March-2023)

Client Detail	Client Details		Sample Details	
Name  M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST2	
		5	Batch/Location	As per Table
Address	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack
			Sampling Instrument	Stack Monitoring Kit
Sampling Do	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Starts on 27/03,		27/03/2023	Samuelina Madhad	Isokinetic Sampling,
Analysis Completion On 0		01./04/0002	Sampling Method	IS:11255,PART-1,2,3
		01/04/2023	Sample Received Date	27/03/2023

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	17.1	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	74.3	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	30.3	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	17.2	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thMarch, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 01/04/2023

#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



AUSTRALIA

OMAN

KUWAIT

AFRICA

## GREEN CIRCLE, INC.

Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

Date: 01/04/2023

#### (For the Month of March-2023)

Client Deta	Client Details		Sample Details	
Name  M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST3	
	Calaat lafraats .ad	was Dut Ital Calaat City walls	Batch/Location	As per Table
Address	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack
			Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Sta	Analysis Starts on 27/03/2023		Same a line at AA a kha a d	Isokinetic Sampling,
Analysis Completion On 01/04/2023		01/04/0000	Sampling Method	IS:11255,PART-1,2,3
Analysis Co	impletion On	01/04/2023	Sample Received Date	27/03/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 3	
2	Rated Capacity	1010	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	25311741	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of the	As & When Required	-
8	Capacity on Sampling Day	520	kW
9	Stack Identification	Stack attached to D.G. Set No. 3	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	125	Liter/Hr.
16	Flue Gas Temperature	200	°C
17	Velocity	15.6	m/s
18	Gas Volume	4794	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA. R&D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : **NEW DELHI** GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : SRI LANKA

BANGLADESH

MYANMAR

UAE

VIETNAM



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

(For the Month of March-2023)

Client Detai	Client Details		Sample Details	
Name M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST3	
	Calaat lafraatsus	use Dut Ital Coloot City wells A	Batch/Location	As per Table
Address	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack
			Sampling Instrument	Stack Monitoring Kit
Sampling Do	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Starts on 27/03/202		27/03/2023	Samuelina Madhad	Isokinetic Sampling,
Analysis Completion On		01/04/0000	Sampling Method	IS:11255,PART-1,2,3
Analysis Co	mpletion On	01/04/2023	Sample Received Date	27/03/2023

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	19.9	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	108	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	26	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	6.8	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thMarch, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 01/04/2023

#### **Authorized Signatory**

SRI LANKA

UAE

Analysis is subject to the condition In Which the Sample Is received at our Laboratory.

**AFRICA** 

- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

KUWAIT

OMAN

AUSTRALIA

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

BANGLADESH

MYANMAR

VIETNAM



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Deihi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

Date: 01/04/2023

SRI LANKA

UAE

MYANMAR

#### (For the Month of March-2023)

Client Details		Sample Details		
Name  M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST4	
	Select Infrastructure Pvt. Ltd., Select		Batch/Location	As per Table
Address	City walk, A-3, District Centre, Saket,		Nature of Sample	Stack
	New Delhi – 110017		Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Sta	Analysis Starts on 27/03/2023		Samuelina Alakhad	Isokinetic Sampling,
Analysis Completion On 01/04/2023		Sampling Method	IS:11255,PART-1,2,3	
		01/04/2023	Sample Received Date	27/03/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit	
1	Name Of Emission	D.G. Set 4		
2	Rated Capacity	2000	KVA	
3	Date of Manufacturing	09/2007	Month /Year	
4	Make	Cummins	-	
5	Engine Sr. No.	33163864	-	
6	Name of the Plant/Section	DG Room	-	
7	Normal Operating schedule of the	As & When Required	-	
8	Capacity on Sampling Day	1260	kW	
9	Stack Identification	Stack attached to D.G. Set No. 4		
10	Material of Stack	Metal		
11	Stack Height from G.L.	34	Mtr.	
12	Diameter of Stack	45	cm	
13	Type of Stack	Round		
14	Fuel Type	H.S.D.		
15	Fuel Consumption	360	Liter/Hr.	
16	Flue Gas Temperature	284	°C	
17	Velocity	16.8	m/s	
18	Gas Volume	5114	Nm³/Hr.	
19	Sampling Duration	30	Min.	

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH



# GREEN CIRCLE, INC.

Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### ANALYSIS REPORT

(For the Month of March-2023)

Client Details			Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST4	
	Select Infrastruc	ture Pvt. Ltd., Select	Batch/Location	As per Table	
Address	City walk, A-3, District Centre, Saket,		Nature of Sample	Stack	
	New Delhi – 110017		Sampling Instrument	Stack Monitoring Kit	
Sampling D	one By	Mr. Kartik	Date of Sampling	25/03/2023	
Analysis Sta	arts on	27/03/2023	Sampling Mothed	Isokinetic Sampling,	
Analysis Completion On		01/04/2023	Sampling Method	IS:11255,PART-1,2,3	
Analysis Co	ompletion On	01/04/2023	Sample Received Date	27/03/2023	

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	24.8	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	124.8	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	23.5	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	17.0	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thMarch, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 01/04/2023

**Authorized Signatory** 

SRI LANKA

UAE

MYANMAR

Analysis is subject to the condition In Which the Sample Is received at our Laboratory.

**AFRICA** 

- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

KUWAIT

OMAN

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

BANGLADESH



OMAN

KUWAIT

AFRICA

# GREEN CIRCLE, INC.

Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

Date: 01/04/2023

(For the Month of March-2023)

Client Details			Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST5	
	Select Infrastruct	ure Pvt. Ltd., Select	Batch/Location	As per Table	
Address	City walk, A-3, District Centre, Saket,		Nature of Sample	Stack	
	New Delhi – 110017		Sampling Instrument	Stack Monitoring Kit	
Sampling D	one By	Mr. Kartik	Date of Sampling	25/03/2023	
Analysis Sta	arts on	27/03/2023	Sampling Method	Isokinetic Sampling,	
Analysis Completion On		01/04/2022	Sampling Memod	IS:11255,PART-1,2,3	
Analysis Co	ompletion On	01/04/2023 Sample Received Date	27/03/2023		

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 5	
2	Rated Capacity	2000	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	33161107	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of	As & When Required	-
8	Capacity on Sampling Day	1200	kW
9	Stack Identification	Stack attached to D.G. Set No. 5	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	270	Liter/Hr.
16	Flue Gas Temperature	260	°C
17	Velocity	20.2	m/s
18	Gas Volume	4534	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA. R&D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : **NEW DELHI** GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : SRI LANKA

BANGLADESH

MYANMAR

UAE



OMAN

KUWAIT

**AFRICA** 

# GREEN CIRCLE, INC.

Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Dethi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

(For the Month of March-2023)

Client Details		Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST5
	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket,		Batch/Location	As per Table
Address			Nature of Sample	Stack
	New Delhi - 110	017	Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	25/03/2023
Analysis Sta	rts on	27/03/2023	Company Administration	Isokinetic Sampling,
Analysis Completion On		01/04/2022	Sampling Method	IS:11255,PART-1,2,3
Analysis Co	mpletion On	01/04/2023	Sample Received Date	27/03/2023

#### **STACK MONITORING RESULTS**

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	17.3	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	118	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	31.1	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	19.4	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thMarch, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 01/04/2023

**Authorized Signatory** 

SRI LANKA

UAE

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

BANGLADESH

MYANMAR



## GREEN CIRCLE, INC.

Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/March-00/0007

### ANALYSIS REPORT

(For the Month of March-2023)

Client Details			Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/C4/SCM/ST6 & ST7	
	Select Infras	tructure Pvt. Ltd., Select	Batch/Location	Hot water generator No. 1& 2	
Address	Citywalk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack	
			Sampling Instrument	Stack Monitoring Kit	
Sampling Do	ne By	Mr. Kartik	Date of Sampling	25/03/2023	
Analysis Starts on		27/03/2023	Sampling Method	Isokinetic Sampling, IS:11255,PART-1,2,3	
Analysis Completion On		01/04/2023	Sample Received Date	27/03/2023	

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	39.8	Not Specified	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	81.2	Not Specified	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	17.3	Not Specified	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	12.4	Not Specified	Gas Chromatograph – Flame Ionization Detector



Date: 01/04/2023

**Authorized Signatory** 

SRI LANKA

UAE

MYANMAR

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

KUWAIT

**AFRICA** 

OMAN

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

BANGLADESH



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G141/22/SP/22-23/March-00/0007

#### **ANALYSIS REPORT**

(For the Month of January-2023)

Client De	tails		Sample Details		
Name	M/s. Select Ci	tywalk Mall a unit of	Samula Cada	GCI/V/23/C4/SCM/WW2	
Name	Select Infrastr	ucture Pvt. Limited	Sample Code	GC1/ V/23/C4/3CIVI/ VV VV2	
Select Infrastructure Pvt. Ltd., Se		ucture Pvt. Ltd., Select			
Address	Citywalk, A-3, District Centre, Saket,		Batch/Location	STP Outlet	
	New Delhi – 110017				
Sampling	Done By	Operator	Quantity	1000 ml	
Analysis S	Starts on	27/03/2023	Date of Sampling	25/03/2023	
Analysis Completion On		01/04/2023	Sampling Instrument	Manual Sampler	
Sampling	Method	APHA 1060	Sample Received Date	27/03/2023	

#### **WASTE WATER ANALYSIS RESULTS**

Sr. No.	Parameters	Unit	Results	DPCC Standard	Reference Method
1.	рН	-	7.49	5.5 – 9.0	APHA 4500-H+
2.	Total Suspended Solids	mg/L	18	30	APHA 2540 D
3.	Chemical Oxygen Demand	mg/L	60	250	APHA 5220
4.	Biochemical Oxygen Demand (3 days at 27 °C)	mg/L	14	20	APHA 5210
5.	Oil & Grease	mg/L	0.5	10	APHA 5520
6.	Phosphate	mg/L	0.54	5.0	APHA 4500 - P
7.	Nitrate Nitrogen	mg/L	3.6	10	APHA 4500 – NORG-B
8.	Fecal Coliforms	MPN/100 ml	110	<230	APHA 9221 - E
9.	Ammonical Nitrogen	mg/L	1.6	50	APHA 4500 - NH <sub>3</sub>

BDL: Below Detectable Level ND: Not Detectable



Date: 01/04/2023

**Authorized Signatory** 

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

NEW DELHI GOA PUNE BENGALURU U.K.

: ALSO AT : HYDERABAD : OVERSEAS : -

KOLKATA

DHARWAD

MUMBAI PORT BLAIR

AUSTRALIA

OMAN

KUWAIT

AFRICA

VIETNAM

BANGLADESH

MYANMAR

SRI LANKA

UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

Date: 10/01/2023

#### **ANALYSIS REPORT**

(For the Month of January- 2023)

Client Details			Sample Details		
Name	M/s. Select Citywalk Mall a unit of		Samula Cada	CC1/1/102/14/20114/19 AA0	
Name	Select Infrastru	cture Pvt. Limited	Sample Code	GCI/V/23/A1/SCM/AA1 & AA2	
	Select Infrastructure Pvt. L		Location	As Per Table	
Address	Citywalk, A-3, District Centre, Saket,		Quantity	NA	
	New Delhi – 110017		Date of Sampling	03/01/2023	
Sampling	Done By	Mr. Vikram	Sampling Instrument	RDS, FPS	
Analysis Starts on		05/01/2023	Sampling Method	IS 5182 : Part 5 : 1975	
Analysis Completion On		10/01/2023	Sample Received Date	05/01/2023	

#### **AMBIENT AIR MONITORING RESULTS**

			Res	ults		
Sr. No.	Parameters	Unit	Near Main Gate	Back Side (Near STP)	Permissible Limit as per NAAQS	Reference Method
1.	Particulate Matter (PM <sub>10</sub> )	µg/m³	60.5	65.1	100	IS 5182 : Part 23 : 2006
2.	Particulate Matter (PM <sub>2.5</sub> )	µg/m³	24.2	26.0	60	IS 5182 : Part 24 : 2019
3.	Sulfur Dioxide (SO <sub>2</sub> )	µg/m³	7.8	8.2	80	IS 5182 : Part 2 : 2001
4.	Oxides of Nitrogen(NOx)	µg/m³	12.1	13.4	80	IS 5182 : Part 6 : 2006
5.	Carbon Monoxide CO	mg/m³	0.3	0.2	2.0	IS 5182 : Part 10 : 1999
6.	Ozone as O <sub>3</sub>	µg/m³	<20	<20	100	NAAQS Guidelines
7.	Lead as Pb	µg/m³	<0.05	<0.05	1.0	NAAQS Guidelines
8.	Nickel as Ni	ng/m³	<1.0	<1.0	20	NAAQS Guidelines
9.	Arsenic as As	ng/m³	<0.5	<0.5	6.0	NAAQS Guidelines
10.	Ammonia as NH <sub>3</sub>	µg/m³	<20	<20	400	NAAQS Guidelines
11.	Benzene , C6H6	µg/m³	<0.5	<0.5	5.0	IS 5182 (Part 11):2006
12.	Benzo (a) Pyrene	ng/m³	<0.05	<0.05	1.0	Gas Chromatography



#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHA

OLKATA DHARWAD MUMBAI PORT BLAIR

AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

Date: 10/01/2023

#### **ANALYSIS REPORT**

(For the Month of January-2023)

Client de	tails		Sample Details	
Name	M/s. Select Citywalk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/N1- N4
	Select Infrastructure Pvt. Ltd., Select  ddress Citywalk, A-3, District Centre,		Location	As per table
Address			Nature of Sample	Noise
	Saket, New I	Delhi – 110017	Date of Sampling	03/01/2023
Sampling Done By		Mr. Vikram	Carrentin a Abobbo d	Lutron/SL-4001 SD inst.
Sampling Instrument		Sound Level Meter	Sampling Method	Manual

#### **NOISE MONITORING RESULTS**

Sr.		Day Time o	iB (A) Leg	Night Time dB (A) Leg	
No.	Location Name		СРСВ		СРСВ
110.		Results	Permissible	Results	Permissible
			Limit		Limit
1.	Pushpa nagar	58.5	65	51.2	55
2.	Malviya nagar	53.5	55	42.6	45
3.	CPWP Office	54.4	55	44.1	45
4.	Madan Gir	54.3	55	43.5	45

Remark: Results are within Standard as per CPCB Permissible limit.



#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :

NEW DELHI GOA PUNE BENGALURU U.K. HY

HYDERABAD : OVERSEAS : KOLKATA

DHARWAD

MUMBAI PORT BLAIR



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0 757

#### **ANALYSIS REPORT**

(For the Month of January-2023)

Client de	tails		Sample Details		
Name	M/s. Select Citywalk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/N5- N6	
	Select Infrastructure Pvt. Ltd., Select		Location	As per table	
Address	Citywalk, A-3, District Centre,		Nature of Sample	Noise	
	Saket, New Delhi – 110017		Date of Sampling	03/01/2023	
Sampling Done By Mr. Vikram		Comments of Administration	Lutron/SL-4001 SD inst.		
Sampling Instrument		Sound Level Meter	Sampling Method	Manual	

#### NOISE MONITORING RESULTS

		Day Tim	e dB (A) Leg	
Sr. No.	Location Name	Results	CPCB Permissible Limit	
5.	D.G. Sets	90.6		
J.	(Inside acoustic enclosure)	70.0	Minimum 25 dB(A)	
	D.G. Sets (1 meter distance from	65.2	insertion loss	
6.	Outside acoustic enclosure)	63.2		

#### Remark:

- The premises is used as shopping mall.
- The unit has 5 D.G.Set(1010 KVA),1010 KVA,2000 KVA,2000KVA and 2000 KVA bearing engine no.25311742,25311741,33161054,33163864 and 33161107 with stack height 6.0 m each, above from building height.
- > D.G Set of the unit is installed in an acoustically treated room at rear side basement-2 of the building. During monitoring all D.G set were operational.
- The D.G.Set Monitored is meeting the permissible limit as per the G.S.R.371 (E) dated 17th May 2002 and amended till date. However ambient air quality standards in respect of noise as mentioned in schedule III of the environment (Protection) Rules, 1986 is meeting.



Date: 10/01/202

#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & ; Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA. R&D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

**NEW DELHI** 

GOA

PUNE

BENGALURU

: ALSO AT : HYDERABAD : OVERSEAS :

KOLKATA

DHARWAD

MUMBAI

PORT BLAIR

UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### **ANALYSIS REPORT**

Date: 10/01/2023

(For the Month of January - 2023)

Client Deta	ils		Sample Details	
Name	M/s. Select City Infrastructure Pv	walk Mall a unit of Select rt. Limited	Sample Code	GCI/V/23/A1/SCM/ST1
	Select Infrastructure Pvt. Ltd., Select City walk,		Batch/Location	As per Table
Address		tre, Saket, New Delhi – 110017	Nature of Sample	Stack
	7 O, Disilier Ceri	ine, saker, riew Beilii 110017	Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	04/01/2023
Analysis Sta	arts on	05/01/2023	Sampling Method	Isokinetic Sampling,
Analysis Completion On		10/01/2023	Sumpling Memod	IS:11255,PART-1,2,3
Analysis Co	ompletion On	10/01/2023	Sample Received Date	05/01/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 1	
2	Rated Capacity	2000	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	33161054	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of the Plant(Hrs/Day)	As & When Required	-
8	Capacity on Sampling Day	980	kW
9	Stack Identification	Stack attached to D.G. Set No. 1	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	250	Liter/Hr.
16	Flue Gas Temperature	294	°C
17	Velocity	15.7	m/s
18	Gas Volume	4854	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : HYDERABAD NEW DELHI GOA PUNE BENGALURU U.K. KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : KUWAIT AUSTRALIA OMAN AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

 $Re\ port\ No: -\ G\ C\ I/\ V/\ IAB/\ G\ 0\ 1\ 3\ 7/\ 2\ 1/\ SP/\ 2\ 2\ -\ 2\ 3/\ Ja\ nua\ ry\ -\ 0\ 0/\ 0\ 7\ 5\ 7$ 

#### ANALYSIS REPORT

(For the Month of January 2023)

Client De tai	ils		Sample Details		
Name	M/s. Se lect City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCVV/23/A1/SCM/STI	
			Batch/Location	As per Table	
Address		ture Pvt. Ltd., Se le c t City walk, tre, Saket, New Delhi – 110017	Nature of Sample	Sta c k	
	A-3, District Cen	tre, Saket, New Deini – 110017	Sampling Instrument	Stack Monitoring Kit	
Sampling D	one By	Mr. Kartik	Date of Sampling	04/01/2023	
Analysis Sta	rtson	05/01/2023	C P M d l	Iso kine tic Sampling,	
		10/01/0000	Sampling Method	IS:11255,PART-1,2,3	
Analysis Co	mple tion On	10/01/2023	Sample Received Date	05/01/2023	

#### STACK MONITORING RESULTS

Sr. No.	Pa ra m e te r	Units	Re sult	Em issio n Standard	Reference Method
1.	Particulate Matter (PM)	${ m mg/nm^3}$	20.9	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	10.43	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	23.8	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	7.6	100	Gas Chromatograph – Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Die sel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9th January, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 10/01/2023

Authorized Signatory

- · Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judic iary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: -GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### ANALYSIS REPORT

Date: 10/01/2023

(For the Month of January - 2023)

Client Detai	ils		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST2
	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Batch/Location	As per Table
Address			Nature of Sample	Stack
	A-3, District Cen	rre, saket, New Deini – 110017	Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	04/01/2023
Analysis Sta	ırts on	05/01/2023	Samuelina Alakhad	Isokinetic Sampling,
Analysis Completion On		10/01/0000	Sampling Method	IS:11255,PART-1,2,3
Analysis Co	impletion On	10/01/2023	Sample Received Date	05/01/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 2	
2	Rated Capacity	1010	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	25311742	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of the Plant(Hrs/Day)	As & When Required	-
8	Capacity on Sampling Day	534	kW
9	Stack Identification	Stack attached to D.G. Set No. 2	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	-
14	Fuel Type	H.S.D.	
15	Fuel Consumption	130	Liter/Hr.
16	Flue Gas Temperature	262	°C
17	Velocity	15.2	m/s
18	Gas Volume	4280	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : HYDERABAD NEW DELHI GOA PUNE BENGALURU U.K. KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: -GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### **ANALYSIS REPORT**

(For the Month of January - 2023)

Client Detai	Client Details			Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST2	
			Batch/Location	As per Table	
Address		ture Pvt. Ltd., Select City walk,	Nature of Sample	Stack	
	A-3, DISTRICT CEN	tre, Saket, New Delhi – 110017	Sampling Instrument	Stack Monitoring Kit	
Sampling D	Sampling Done By Mr. Kartik		Date of Sampling	04/01/2023	
Analysis Starts on 05/01/2023		05/01/2023	Sampling Method	Isokinetic Sampling,	
Analysis Co	mpletion on	10/01/2023	sumpling Memod	IS:11255,PART-1,2,3	

#### **STACK MONITORING RESULTS**

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	16.3	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	79.5	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm <sup>3</sup>	32.1	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	15.8	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9th January, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 10/01/2023

**Authorized Signatory** 

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : NEW DELHI GOA BENGALURU HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### **ANALYSIS REPORT**

Date: 10/01/2023

(For the Month of January-2023)

Client Deta	ils		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST3
	Calaat lafaada.	t D. t. I.t.al. C. I. a.t. Cit	Batch/Location	As per Table
Address	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack
	A-3, District Cert	ire, saker, New Deini – 110017	Sampling Instrument Stack Monitoring Kit	
Sampling D	one By	Mr. Kartik	Date of Sampling	04/01/2023
Analysis Sto	arts on	05/01/2023	Companiin or AA akha ad	Isokinetic Sampling,
			Sampling Method	IS:11255,PART-1,2,3
Analysis Co	ompletion On	10/01/2023	Sample Received Date	05/01/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 3	
2	Rated Capacity	1010	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	25311741	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of the	As & When Required	-
8	Capacity on Sampling Day	520	kW
9	Stack Identification	Stack attached to D.G. Set No. 3	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	125	Liter/Hr.
16	Flue Gas Temperature	206	°C
17	Velocity	14.1	m/s
18	Gas Volume	4692	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : HYDERABAD NEW DELHI GOA PUNE BENGALURU U.K. KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : KUWAIT AUSTRALIA OMAN AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### ANALYSIS REPORT

(For the Month of January-2023)

Client Deta	iils		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST3
	Calaatlafaaataa	t D. t. 11-1 C-11 Cit	Batch/Location As per Table	
Address	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack
	A-3, DISTRICT CER	ire, saker, New Deini – 110017	Sampling Instrument Stack Monitoring Kit	
Sampling D	Oone By	Mr. Kartik	Date of Sampling	04/01/2023
•		05/01/2023	Sampling Method	Isokinetic Sampling,
		10/01/2023	Sample Received Date	IS:11255,PART-1,2,3 05/01/2023

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm <sup>3</sup>	18.6	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	121	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	32	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	7.4	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9th January, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 10/01/2023

**Authorized Signatory** 

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### **ANALYSIS REPORT**

Date: 10/01/2023

(For the Month of January-2023)

Client Deta	Client Details		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST4
	Select Infrastructure Pvt. Ltd., Select		Batch/Location	As per Table
Address	City walk, A-3, D	District Centre, Saket,	Nature of Sample	Stack
	New Delhi - 110	017	Sampling Instrument	Stack Monitoring Kit
Sampling [	Done By	Mr. Kartik	Date of Sampling	04/01/2023
Analysis Starts on		05/01/2023	Consulting Adulting d	Isokinetic Sampling,
Analysis Completion On		10/01/0002	Sampling Method	IS:11255,PART-1,2,3
Analysis Co	ompletion On	10/01/2023	Sample Received Date	05/01/2023

#### STACK DETAILS

Sr. No.	Particulars	Details	Unit	
1	Name Of Emission	D.G. Set 4		
2	Rated Capacity	2000	KVA	
3	Date of Manufacturing	09/2007	Month /Year	
4	Make	Cummins	-	
5	Engine Sr. No.	33163864	-	
6	Name of the Plant/Section	DG Room	-	
7	Normal Operating schedule of the	As & When Required	-	
8	Capacity on Sampling Day	1260	kW	
9	Stack Identification	Stack attached to D.G. Set No. 4		
10	Material of Stack	Metal		
11	Stack Height from G.L.	34	Mtr.	
12	Diameter of Stack	45	cm	
13	Type of Stack	Round		
14	Fuel Type	H.S.D.		
15	Fuel Consumption	360	Liter/Hr.	
16	Flue Gas Temperature	284	°C	
17	Velocity	17.2	m/s	
18	Gas Volume	5009	Nm³/Hr.	
19	Sampling Duration	30	Min.	

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D

Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : HYDERABAD NEW DELHI GOA PUNE BENGALURU U.K. KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### **ANALYSIS REPORT**

(For the Month of January-2023)

Client Details		Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST4
Address	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket,		Batch/Location	As per Table
Address	New Delhi – 110		Nature of Sample Stack	
	New Dellii - 1100	517	Sampling Instrument	Stack Monitoring Kit
Sampling D	Sampling Done By Mr. Kartik		Date of Sampling	04/01/2023
Analysis Starts on 05/01/2023		05/01/2023		Isokinetic Sampling,
Analysis Completion On		10/01/2023	Sampling Method	IS:11255,PART-1,2,3

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	20.8	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	129.1	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	26.4	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	17.7	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thJanuary, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 10/01/2023

**Authorized Signatory** 

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT :
NEW DELHI GOA PUNE BENGALURU U.K. HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR
: OVERSEAS :

AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### **ANALYSIS REPORT**

Date: 10/01/2023

(For the Month of January-2023)

Client Details		Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST5
	Select Infrastructure Pvt. Ltd., Select		Batch/Location	As per Table
Address	City walk, A-3, D	istrict Centre, Saket,	Nature of Sample	Stack
	New Delhi – 1100	017	Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	04/01/2023
Analysis Starts on		05/01/2023	Consulting Advillaged	Isokinetic Sampling,
Analysis Completion On		10/01/0000	Sampling Method	IS:11255,PART-1,2,3
		10/01/2023	Sample Received Date	05/01/2023

#### **STACK DETAILS**

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 5	
2	Rated Capacity	2000	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	-
5	Engine Sr. No.	33161107	-
6	Name of the Plant/Section	DG Room	-
7	Normal Operating schedule of	As & When Required	-
8	the Plant (Hrs (Day) Capacity on Sampling Day	1200	kW
9	Stack Identification	Stack attached to D.G. Set No. 5	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	n 270	
16	Flue Gas Temperature	264	°C
17	Velocity	19.3	m/s
18	Gas Volume	4562	Nm³/Hr.
19	Sampling Duration	30	Min.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : HYDERABAD NEW DELHI GOA PUNE BENGALURU U.K. KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : KUWAIT AUSTRALIA OMAN AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### ANALYSIS REPORT

(For the Month of January-2023)

Client Detai	Client Details		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST5
	Select Infrastructure Pvt. Ltd., Select		Batch/Location	As per Table
Address	City walk, A-3, D	istrict Centre, Saket,	Nature of Sample	Stack
	New Delhi – 1100	)17	Sampling Instrument	Stack Monitoring Kit
Sampling D	one By	Mr. Kartik	Date of Sampling	04/01/2023
Analysis Sta	Analysis Starts on 05/01/2		Sampling Method	Isokinetic Sampling,
Analysis Completion On		10/01/2023	Sampling Memod	IS:11255,PART-1,2,3
Alidiysis Co	inplemon On	10/01/2023	Sample Received Date	05/01/2023

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	14.2	75	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	125	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	32.0	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	20.0	100	Gas Chromatograph– Flame Ionization Detector

Note: Generator sets commissioning Date – after 01. 07. 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9th January, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



Date: 10/01/2023

**Authorized Signatory** 

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D

Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : NEW DELHI GOA BENGALURU HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : **AUSTRALIA** OMAN KUWAIT **AFRICA** VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW) (ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### **ANALYSIS REPORT**

(For the Month of January-2023)

Client Details			Sample Details		
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/V/23/A1/SCM/ST5 & ST6	
Address	Select Infrastructure Pvt. Ltd., Select Citywalk, A-3, District Centre, Saket, New Delhi – 110017		Batch/Location	Hot water generator No. 1& 2	
			Nature of Sample	Stack	
			Sampling Instrument	Stack Monitoring Kit	
Sampling Done By Mr. Kartik		Mr. Kartik	Date of Sampling	04/01/2023	
Analysis Starts on 05/01/202		05/01/2023	Sampling Method	Isokinetic Sampling, IS:11255,PART-1,2,3	
Analysis Completion On 10/01/2023		10/01/0002		13.11233,FAR1-1,2,3	
		10/01/2023	Sample Received Date	05/01/2023	

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	38.4	Not Specified	IS 11255: Part 1
2.	NOx (as NO <sub>2</sub> )	ppmv	86.1	Not Specified	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	16.5	Not Specified	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	11.8	Not Specified	Gas Chromatograph – Flame Ionization Detector



Date: 10/01/2023

#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & : Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA.

R & D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

: ALSO AT : NEW DELHI GOA BENGALURU HYDERABAD KOLKATA DHARWAD MUMBAI PORT BLAIR : OVERSEAS : AUSTRALIA OMAN KUWAIT AFRICA VIETNAM BANGLADESH MYANMAR SRI LANKA UAE



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognised By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (F. No. - 15018 / 06 / 2016 - CPW)

(ISO 9001, 14001, 45001 & NABL / 17025 Certified Organisation)

Report No: - GCI/V/LAB/G0137/21/SP/22-23/January-00/0757

#### ANALYSIS REPORT

(For the Month of January-2023)

Client Details			Sample Details		
Name	M/s. Select Citywalk Mall a unit of		Sample Code	GCI/V/23/A1/SCM/WW2	
Name	Select Infrastructure Pvt. Limited		Sample Code		
	Select Infrastructure Pvt. Ltd., Select		Batch/Location	STP Outlet	
Address	Citywalk, A-3, District Centre, Saket,				
	New Delhi – 110017				
Sampling Done By		Operator	Quantity	1000 ml	
Analysis Starts on		05/01/2023	Date of Sampling	04/01/2023	
Analysis Completion On		10/01/2023	Sampling Instrument	Manual Sampler	
Sampling Method		APHA 1060	Sample Received Date	05/01/2023	

#### **WASTE WATER ANALYSIS RESULTS**

Sr. No.	Parameters	Unit	Results	DPCC Standard	Reference Method
1.	рН	-	7.68	5.5 – 9.0	APHA 4500-H+
2.	Total Suspended Solids	mg/L	16	30	APHA 2540 D
3.	Chemical Oxygen Demand	mg/L	40	250	APHA 5220
4.	Biochemical Oxygen Demand (3 days at 27 °C)	mg/L	12	20	APHA 5210
5.	Oil & Grease	mg/L	0.9	10	APHA 5520
6.	Phosphate	mg/L	0.55	5.0	APHA 4500 - P
7.	Nitrate Nitrogen	mg/L	3.6	10	APHA 4500 – NORG-B
8.	Fecal Coliforms	MPN/100 ml	120	<230	APHA 9221 - E
9.	Ammonical Nitrogen	mg/L	3.4	50	APHA 4500 - NH₃

**BDL: Below Detectable Level** 

**ND: Not Detectable** 



Date: 10/01/2023

#### **Authorized Signatory**

- Analysis is subject to the condition In Which the Sample Is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

CORP. OFFICE & ; Green Empire (Anupushpam), Above AXIS Bank, Nr. Yash Complex, Gotri Main Road, Vadodara - 390 021 (Gujarat), INDIA. R&D Tel.: +91 - 265 - 2371269 Cell: +91 93285 83835 Email: info@greencircleinc.com Website: www.greencircleinc.com

BENGALURU NEW DELHI

: ALSO AT : HYDERABAD KOLKATA : OVERSEAS :

DHARWAD MUMBAI PORT BLAIR

AUSTRALIA

OMAN KUWAIT

**AFRICA** 

BANGLADESH VIETNAM

MYANMAR

SRI LANKA

# Annexure – 10

Adequacy Report of Rain Water

Harvesting

विल्ली सरकार

WH ADEQUACY CERTIFICATE



CATCH RAIN, IT'S USEFUL

This is awarded to Select Infrastructure Put. Ut.

regarding adequacy and functionality for RWH structure at Select City walk Mall, A-3,

District Centre, Saket, New Delhi-110017.

Refering to your letter dated 3105-2022. In which you have informed that Rain Water Harvesting has been installed at your said premise. The rain water harvesting structure was inspected by NGT/DJB inspection team on dated 02-06-2022 and found sufficient and adequate to harvest the catchment area of your premises. This certificate is issued based on the above joint inspection report and same is valid for two years subject to terms and condition as under:

1. RWH system maintained neat and clean at every time for proper recharge of rain water.

2. Owner may allow for inspection of RWH by any NGT/DJB and other inspection teams for inspection and also facilitate for the same.

3. In case, if any dispute/litigation on the premises for which above certificate issued, the above certificate will be treated as cancelled.

4. In case, owners make changes in above RWH system, he may intimate to this office.

No./Year 381/2022 Date of Issue 02-06-2022

Executive Engineer (RWH/GWC)

Delhi Jal Board, Room No. 101 Caranaliya Phase-1 Thandewalan

Contact No. 011-23558264 E-mail many phase-1 Thandewalan

IMANDEWALAN, N.

# Annexure – 11

# MOU with M/s Chintan



#### INDIA NON JUDICIAL

#### **Government of National Capital Territory of Delhi**

#### e-Stamp

Certificate No.

Certificate Issued Date

Account Reference Unique Doc. Reference

Purchased by

Description of Document

Property Description

Consideration Price (Rs.)

First Party

Second Party

Stamp Duty Paid By

Stamp Duty Amount(Rs.)

IN-DL44687793374253U

10-Jun-2022 10:53 AM

IMPACC (IV)/ dl853303/ DELHI/ DL-DLH

SUBIN-DLDL85330373871436398627U

SELECT INFRASTRUCTURE PVT LTD

Article 5 General Agreement

Not Applicable

(Zero)

: SELECT INFRASTRUCTURE PVT LTD

Not Applicable

SELECT INFRASTRUCTURE PVT LTD

100

(One Hundred only)



masse write or type below this line

#### AGREEMENT

This Agreement is made and entered into on the 5th July, 2022 at New Delhi by and between:

Select Infrastructure Pvt. Ltd., a company incorporated under the Companies Act, 1956 and having its registered office at 4th Floor Office Tower, Select CITYWALK, A – 3, District Centre, Saket, New Delhi – 119 017 (hereinafter referred to as "SIPL" which expression shall, and the present to

6

The same of the sa

TOPOT CHINTAN

the context or meaning thereof, be deemed to mean and include its successors, and permitted assigns) represented through Mr. Shashi Sharma, Dir. – Operations & Projects, the party of the one Part;

#### AND

M/s. Chintan Environmental Research and Action Group, a non-profit organization having its corporate address at 238, Sidhartha Enclave, New Delhi – 110 014, (hereinafter referred to as "Chintan" which expression shall, unless it be repugnant to the context or the meaning thereof, be deemed to mean and include its successors, legal representative and permitted assigns) represented through its Director Ms. Bharati Chaurvedi, the party of the other Part.

WHEREAS, SIPL provides various services and facilities within a mixed-use commercial complex interalia consisting of a Shopping Centre, Landscape Plaza etc. along with parking and other utilities in the basements, on Plot Nos. A-3 & P-18 at District Centre, Saket, New Delhi – 110017 (hereinafter known as to 'Select CITYWALK').

AND WHEREAS, Chintan represents, confirms, assures SIPL that Chintan has the expertise, standard operating procedures and trained manpower to collect, manage, disposal and maintain the waste (solid and e-waste) material generating or emanating out of various properties including Commercial buildings, multistoried buildings, Mixed used Commercial Complexes, etc. Chintan has confirmed, declared and assured SIPL, after understanding, evaluating and satisfying itself about the building plans, specifications, concept, infrastructure, utilities, etc., at Select CITYWALK; that it has the professional skills, statutory permissions, standard operating procedures and experience as also wherewithal and financial means to provide services relating to the collection, maintenance and management of waste (solid and e-waste) material at Select CITYWALK of such nature and magnitude which are in line with best available global standards and practices followed in the industry in accordance with the applicable Laws.

AND WHEREAS, SIPL relying upon the above representation, confirmation, and assurance from Chintan and in good faith proposed to engage Chintan to collect and dispose off waste (solid and e-waste) from Select CITYWALK and Chintan unequivocally accepted the same, subject to the terms and conditions mentioned in this Agreement.

#### NOW THIS AGREEMENT WITNESSETH AS FOLLOWS:

#### 1. Definition:

"Agreement" shall mean and include this Agreement, together with all Annexures, Schedules & Attachments and its modifications thereof.

Applicable Law" means all Acts, Rules and Regulations, including labour laws and laws cellating to environment, solid and e-waste management, collection and disposit, safety,

Page 2 of 6



labour, land and property, in force and in effect as of the date hereof and which may be promulgated or brought into force and effect hereinafter in India including judgements, decrees, injunctions, writs of or orders of any court of record, as may be in force and effect during the subsistence of this Agreement applicable to or relating to the maintenance and management of waste (solid and e-waste) material taking away and disposal services, provided by Chintan to SIPL.

"Parties" shall mean the joint reference to SIPL and Chintan.

"Party" shall mean either SIPL or Chintan.

#### 2. Scope of Services:

- a) SIPL permits to Chintan to collect and take away municipal solid waste (MSD) from the garbage room at Select CITYWALK;
- b) Chintan shall take away e-waste of SIPL, whenever it will be requested by SIPL and dispose of adequately;
- c) Chintan hereby covenants with SIPL as follows:
  - Chintan shall segregate the solid waste material in dry and wet category.
  - ii. Chintan shall ensure that all plastic bags/ items, glass items, silver foils and/ or any non-biodegradable items shall be removed from the wet garbage.
  - iii. After segregating the wet garbage, Chintan shall feed the segregated wet garbage into Shredder and thereafter, the end product of the shredder solid waste material shall be put into the Organic Waste Converter machine in different batches and raw compost will be placed into the compositing system.
  - iv. In case, Chintan find any material, which is not a solid waste material, same shall be handed over to the Housekeeping Manager of Select CITYWALK;
  - v. Chintan shall take away solid waste material from the garbage room and carry out the operations mentioned above at Select CITYWALK on everyday basis, at its own cost and expenses;
- d) Chintan shall adequately take away and dispose off the waste (solid and e-waste) material at its own cost and expenses and shall ensure and adhere with the rules and compliances of the Solid Waste Management Rules, 2016, e-Waste (Management) Rules 2016, (including any new enactment/ amendment/rules, modification, etc., in future), and other acts, rules, etc. in this regard.

Chintan shall maintain and manage a record book of all solid waste material to be taken away from Select CITYWALK on everyday basis and shall submit a copy of the same to Housekeeping Manager of SIPL.



- f) Chintan shall obtain and procure all requisite licenses, permissions, etc. from the concerned statutory authority / department, if any, required under the law for taking away the waste material (solid and e-waste) from Select CITYWALK and disposing off the same as per the applicable laws, rules, etc. Chintan shall submit a copy of license and proof of disposing of waste (solid/ e-waste) material as per the relevant law to SIPL on monthly basis/ time to time, as the case may be.
- g) It is clarified that all equipments or movable property placed or installed in the garbage area of Select CITYWALK are owned and possessed by SIPL. CHINTAN shall not be authorized to take away any equipment or movable property from Select CITYWALK.
- h) Chintan hereby agrees and confirms that it shall not transfer, assign the rights and the benefits of this Agreement to any other third party and/ or appoint any third party for completing the scope of services, as mentioned herein above, without prior written consent of SIPL in this regard.

#### 3. Tenure:

The Agreement with respect to the taking away and dispose off of waste (solid and e-waste) material services shall come into with retrospective effect from 1<sup>st</sup> August, 2022 (the "Commencement Date") and shall remain operative for a fixed tenure of 02 (Two) years. This Agreement may be renewed/ extended for further tenure, subject to the mutual agreed terms of the agreement between both parties.

#### 4. Manpower:

- a) Chintan shall depute its employees with requisite skill and experience to properly, safely, ethically and carry-out the scope of services at Select CITYWALK. Chintan shall depute one (01) Supervisor, who will visit and supervise the performance of services at Select CITYWALK, twice a week or more, as requested by SIPL. All matters pertaining to the employment, supervision, compensation, promotion, and discharge of such manpower are the sole responsibility of Chintan. Chintan shall maintain a record-book of its employees and supervisors, including a copy of each document, i.e., Employee ID, Government issued Photo ID and any other documents, as requested by SIPL and shall furnish the employees' record-book, as and when demanded by SIPL and/ or its authorised representative, within 3 (three) working days.
- b) All employees of Chintan deployed at Select CITYWALK must be trained and equipped to handle the extra ordinary situations, such as suffocation and/ or health deterioration during the segregation and/ or any other activity relating thereto at Select CITYWALK.

#### 5. Compliance with the Labour Laws:

Chintan shall fully comply with all applicable laws and regulations, any amendments and/ or modification thereto, pertaining to employees/ workers and obtain insurance policy to cover its liability under all applied labour laws, in force, during tenure of this Agreement, including

Page 4 of 6

any amendment or modification thereto. It is further agreed by the parties that Chintan shall at all times act and be responsible as employer/principal employer of all/any of the employees/ workmen engaged by it.

#### 6. Indemnification:

Chintan shall at all times completely indemnify and keep SIPL completely harmless and indemnified from any civil, and criminal liabilities including vicarious liabilities by Chintan in performing its obligations including taking away and disposal of waste material (solid and ewaste) as per the applicable rules and regulations, under this Agreement. This indemnity provision shall survive the termination or expiration of this Agreement.

#### 7. Termination of the Agreement:

This Agreement shall expire automatically after a period of Two (02) years from the Commencement Date, unless terminated earlier as provided in this Agreement.

Notwithstanding, either party can terminate the Agreement by serving a written notice, 30 (thirty) days prior, to the other party before the expiry of the Agreement.

SIPL reserves the right to terminate this Agreement incase of any default on part of Chintan in the performance of the services and / or breach and/ or non-compliance of any of the terms of the Agreement or non-conformity to the any of the instructions of SIPL, notified by SIPL time to time. Such a decision will be intimated to Chintan by written notice. The cure period, if any, shall be specified by SIPL in the written notice depending upon the event of default.

#### 8. Obligation of Chintan on Termination:

Upon the end of this Agreement (either by afflux of tenure or earlier termination), Chintan shall handover to SIPL and/ or its authorised representative, within 07 (seven) days, without demur, reservation and/ or protest, all the equipments, record book and other data in the possession of Chintan pertaining to Select CITYWALK and other information, documents pursuant to the terms of this Agreement duly reconciled in all respects to the satisfaction of SIPL and all the keys or combinations to locks then in possession of Chintan.

#### Arbitration and Jurisdiction —

Any difference or dispute arising between the Parties arising out of or in relation to this Agreement shall be referred to the sole Arbitrator appointed by SIPL. The arbitration shall be conducted under the Arbitration & Conciliation Act, 1996. The award of the Arbitrator shall be final and binding upon the parties. The venue of the arbitration shall be at New Delhi. This Agreement shall be subject to the exclusive jurisdiction of the Courts of Delhi.

#### 10. Waiver of Right:

The delay, failure, negligence or forbearance on the part of SIPL to enforce at any time or for any period to time any right or provisions hereof, shall not be construed as a waiver of any

Page 5 of 6

provision or any right and it shall nor preclude that Party from subsequently enforcing such provisions or right.

IN WITNESS WHEREOF, the above terms and conditions this Agreement and a duplicate copy thereof have been executed on the date above first mentioned.

Signed and agreed by and between.

For SIPL

through Mr. Shashi Sharma

Designation: Director - Operations & P

For Chintan

through

Designation:

Witnesses:

1. (

Select Chynulle

2.

PRAGUN GOEL

C-14 FF Cajfort Magar - 3

Lett

# Annexure – 12


# Traffic Management Plan

# TRAFFIC CIRCULATION PLAN





Expansion of "Commercial Complex SELECT CITY WALK (SHOPPING MALL)" by M/s Select Infrastructure Private Limited

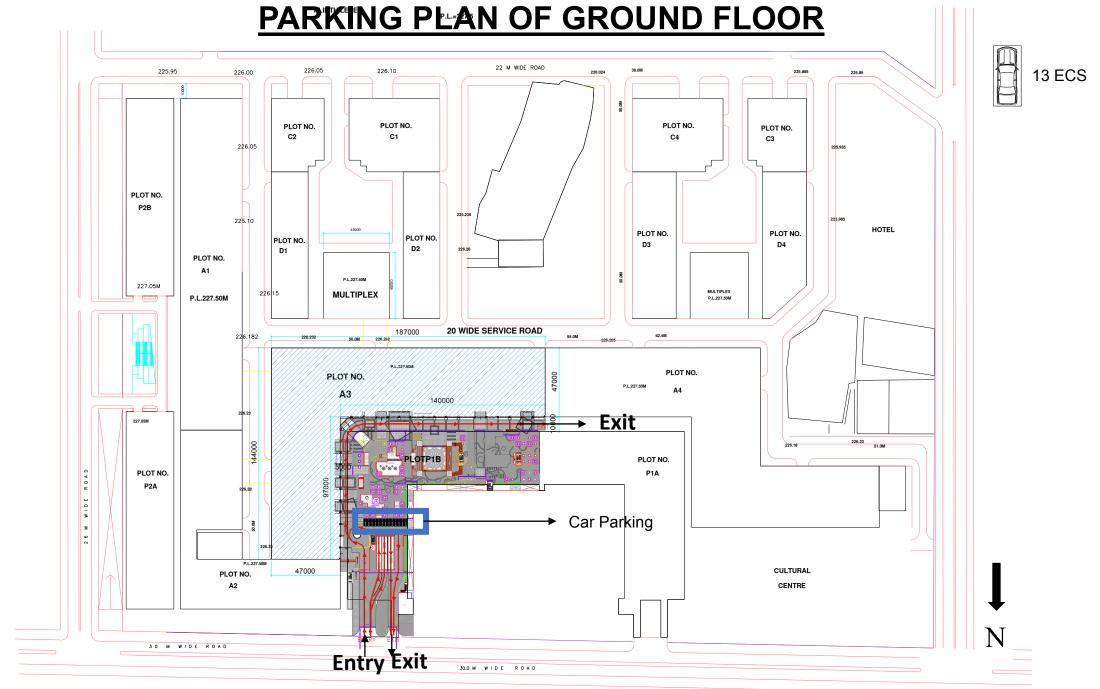


#### GENERAL AIR EXHAUST CUTOUT FIRE EXHAUST SHAFT (1200X4870) FOR 3RD BASEMENT MEZZANINE SLAB LIFT LOBBY AIR WASHER ELECTRICAL PANEL ROOM GENERAL AIR EXHAUST SHAFT (1200X1335) FOR 2ND BASEMEN GENERAL AIR SUPPLY SHAFT (1200X4640) FOR 2ND BASEMEN GENERAL AIR SUPPLY SHAFT (1200X4770) FOR 3RD BASEMENT GENERAL AIR EXHAUST SHAFT (1200X2785) FOR 3RD BASEMENT (JET LIFT) GENERAL AIR EXHAUST SHAFT (1200X1335) FOR 3RD BASEMENT 4700 WIDE DRIVE WAY 666 GB GB GB SENERAL AIR EXHAUST SHAFT 1200X1335) FOR 2ND BASEMENT FIRE EXHAUST SHAFT (1200X4640) FOR 2ND BASEMENT GENERAL AIR EXHAUST SHAFT (1200X2900) FOR 2ND BASEMEN GENERAL AIR EXHAUST SHAFT (1200X2785) FOR 3RD BASEMENT 6000 WIDE VEHICULAR AISLE FIRE EXHAUST SHAFT (1200X4870) FOR 3RD BASEMENT GENERAL AIR EXHAUST SHAFT (1200X2900) FOR 2ND BASEMEN FIRE EXHAUST SHAFT (1200X4840) FOR 2ND BASEMEN GENERAL AIR EXHAUST SHAFT (1200X1335) FOR 2ND BASEMENT GENERAL AIR EXHAUST SHAFT (1200X1335) FOR 3RD BASEMENT FIRE EXHAUST SHAFT (1200X4870) FOR 3RD BASEMENT GENERAL AIR EXHAUST SHAFT (1200X2785) FOR 3RD BASEMENT PROPOSED / MODIFIED AREA **EID EID EID EID EID** HSD TANKS ABOVE

# PARKING PLAN OF BASEMENT 1

61 Nos.

271 ECS



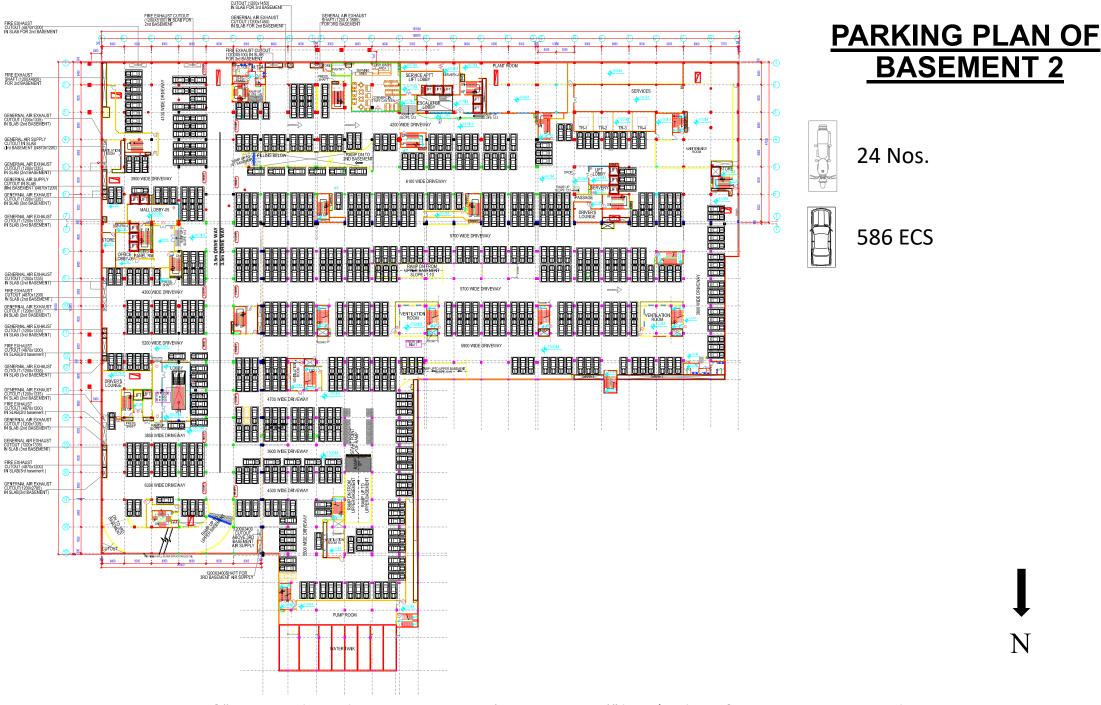

N

## FIRE EXHAUSTCUTOUT (1200X4870) IN SLAB (3rd BASEMENT) GENERNAL AIR EXHAUST CUTOUT (1200x1450) IN SLAB (3R BASEMENT) FIRE EXHAUST CUTOUT (1200X4950) IN SLAB (3rd BASEMENT SPACE FOR SERVICES (CHILLER PLANT) 888-888 88 VENT ROOM VEN ROOM GENERNAL AIR SUPPLY CUTOUT(1200X4870) IN SLAB (3rd BASEMENT) een een een PASSAGE LIFT LIFT MALL LOBBY GENERNAL AIR EXHAUST CUTOUT(1200x1450) IN SI AB (3rd BASEMENT) N

# PARKING PLAN OF BASEMENT 3



137 Nos.




**300 ECS** 

# **TRAFFIC SURVEY**


Traffic Densities within 5 KM radius of project site :-

Source:- Traffic Survey conducted by TPA Engineering Consultancy (I) Pvt. Ltd.

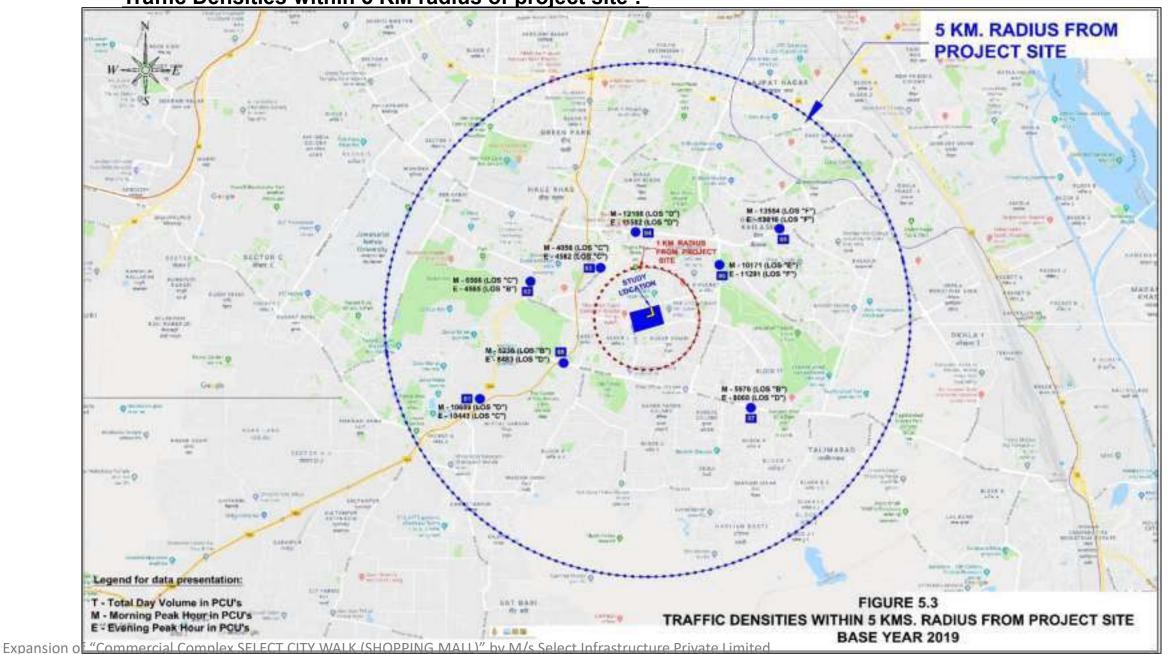

#### TRAFFIC SURVEY

#### STUDY AREA WITH ROAD CHARACTERISTICS:-

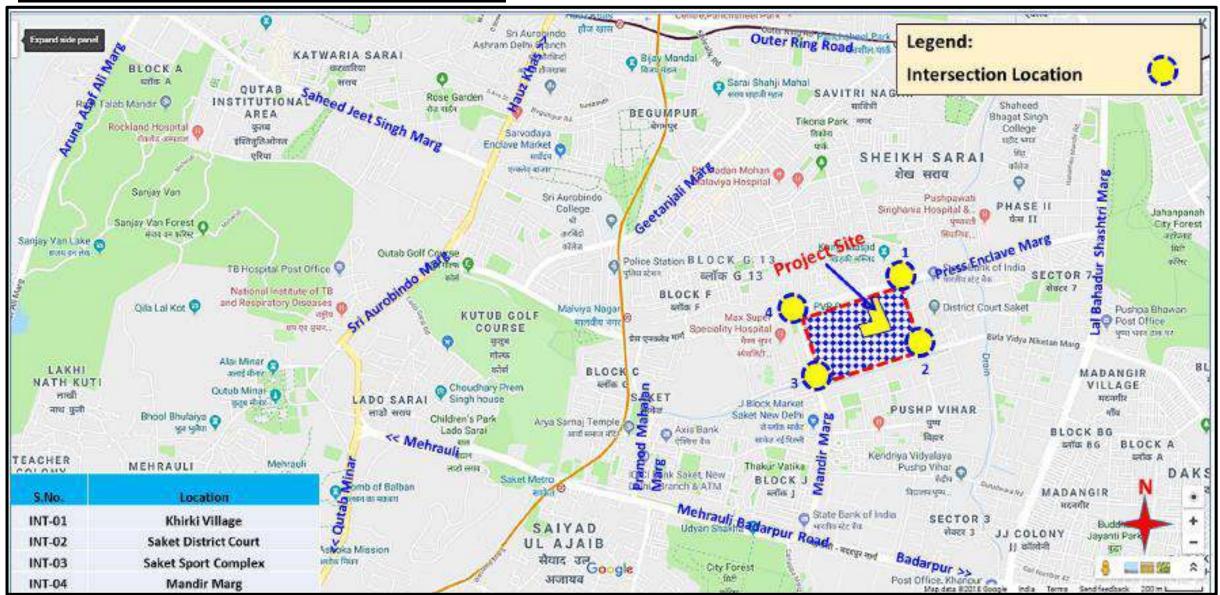

Source:- Traffic Survey conducted by TPA Engineering Consultancy (I) Pvt. Ltd.

#### **TRAFFIC SURVEY**

#### Traffic Analysis with & without project during Morning Peak Hour :-

			Without Project			W	ith Project	
Year	Location	Approach Road	Traffic Volume (PCU)	V/c Ratio	LOS	Traffic Volume (PCU)	V/c Ratio	LOS
			Morning Peak Hour	•	•			
	MB-01	Select City walk (Press Enclave Marg)	2977	0.39	LOS B	2977	0.39	LOS B
	MB-02	Mandir Marg	2221	0.54	LOS B	2221	0.54	LOS B
2019	MB-03	Court Chowk Road	1237	0.30	LOS A	1237	0.30	LOS A
2019	MB-04	Saheed Pankaj Juniyal Marg	2091	0.50	LOS B	2091	0.50	LOS B
	MB-05	Vocational College (Press Enclave Marg)	4053	0.53	LOS B	4053	0.53	LOS B
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	2647	0.34	LOS A	2647	0.34	LOS A
	MB-01	Select City walk (Press Enclave Marg)	3126	0.41	LOS B	3169	0.41	LOS B
	MB-02	Mandir Marg	2332	0.56	LOS C	2341	0.57	LOS C
2020	MB-03	Court Chowk Road	1299	0.31	LOS A	1308	0.32	LOS A
2020	MB-04	Saheed Pankaj Juniyal Marg	2195	0.53	LOS B	2204	0.53	LOS B
	MB-05	Vocational College (Press Enclave Marg)	4256	0.55	LOS C	4269	0.55	LOS C
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	2779	0.36	LOS B	2792	0.36	LOS B
	MB-01	Select City walk (Press Enclave Marg)	3624	0.47	LOS B	3965	0.51	LOS B
	MB-02	Mandir Marg	2703	0.65	LOS C	2934	0.71	LOS C
0005	MB-03	Court Chowk Road	1506	0.36	LOS B	1638	0.40	LOS B
2025	MB-04	Saheed Pankaj Juniyal Marg	2545	0.61	LOS C	2763	0.67	LOS C
	MB-05	Vocational College (Press Enclave Marg)	4933	0.64	LOS C	5352	0.69	LOS C
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	3222	0.42	LOS B	3500	0.45	LOS B
	MB-01	Select City walk (Press Enclave Marg)	4201	0.54	LOS B	4542	0.59	LOS C
	MB-02	Mandir Marg	3134	0.76	LOS C	3365	0.81	LOS D
2030	MB-03	Court Chowk Road	1746	0.42	LOS B	1878	0.45	LOS B
2030	MB-04	Saheed Pankaj Juniyal Marg	2950	0.71	LOS C	3168	0.76	LOS C
	MB-05	Vocational College (Press Enclave Marg)	5719	0.74	LOS C	6138	0.80	LOS D
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	3735	0.48	LOS B	4013	0.52	LOS B
	MB-01	Select City walk (Press Enclave Marg)	4870	0.63	LOS C	5211	0.68	LOS C
	MB-02	Mandir Marg	3633	0.88	LOS D	3864	0.93	LOSE
2025	MB-03	Court Chowk Road	2024	0.49	LOS B	2156	0.52	LOS B
2035	MB-04	Saheed Pankaj Juniyal Marg	3420	0.83	LOS D	3638	0.88	LOS D
	MB-05	Vocational College (Press Enclave Marg)	6630	0.86	LOS D	7048	0.91	LOS D
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	4330	0.56	LOS C	4608	0.60	LOS C

Traffic Analysis with & without project during Evening Peak Hour:

Veer	Location	Annuach Dood	Wi	ithout Project		V	Vith Project	
Year	Location	Approach Road	Traffic Volume (PCU)	V/c Ratio	LOS	Traffic Volume (PCU)	V/c Ratio	LOS
			Evening Peak Ho	our				
	MB-01	Select City walk (Press Enclave Marg)	2815	0.36	LOS B	2815	0.36	LOS B
Γ	MB-02	Mandir Marg	2737	0.66	LOS C	2737	0.66	LOS C
2019	MB-03	Court Chowk Road	2021	0.49	LOS B	2021	0.49	LOS B
2019	MB-04	Saheed Pankaj Juniyal Marg	1940	0.47	LOS B	1940	0.47	LOS B
	MB-05	Vocational College (Press Enclave Marg)	2931	0.38	LOS B	2931	0.38	LOS B
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	3060	0.40	LOS B	3060	0.40	LOS B
	MB-01	Select City walk (Press Enclave Marg)	2956	0.38	LOS B	3117	0.40	LOS B
Γ	MB-02	Mandir Marg	2873	0.69	LOS C	2906	0.70	LOS C
	MB-03	Court Chowk Road	2122	0.51	LOS B	2154	0.52	LOS B
2020	MB-04	Saheed Pankaj Juniyal Marg	2036	0.49	LOS B	2069	0.50	LOS B
Γ	MB-05	Vocational College (Press Enclave Marg)	3078	0.40	LOS B	3126	0.41	LOS B
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	3213	0.42	LOS B	3261	0.42	LOS B
	MB-01	Select City walk (Press Enclave Marg)	3427	0.44	LOS B	3870	0.50	LOS B
F	MB-02	Mandir Marg	3331	0.80	LOS D	3637	0.88	LOS D
	MB-03	Court Chowk Road	2459	0.59	LOS C	2694	0.65	LOS C
2025	MB-04	Saheed Pankaj Juniyal Marg	2361	0.57	LOS C	2587	0.62	LOS C
	MB-05	Vocational College (Press Enclave Marg)	3568	0.46	LOS B	3909	0.51	LOS B
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	3725	0.48	LOS B	4079	0.53	LOS B
	MB-01	Select City walk (Press Enclave Marg)	3972	0.51	LOS C	4415	0.57	LOS C
F	MB-02	Mandir Marg	3862	0.93	LOS F	4167	1.01	LOS F
	MB-03	Court Chowk Road	2851	0.69	LOS C	3086	0.74	LOS C
2030	MB-04	Saheed Pankaj Juniyal Marg	2737	0.66	LOS C	2963	0.72	LOS C
Γ	MB-05	Vocational College (Press Enclave Marg)	4136	0.54	LOS C	4478	0.58	LOS C
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	4318	0.56	LOS C	4672	0.61	LOS C
	MB-01	Select City walk (Press Enclave Marg)	4605	0.60	LOS C	5048	0.65	LOS C
F	MB-02	Mandir Marg	4477	1.08	LOSF	4783	1.15	LOS F
	MB-03	Court Chowk Road	3305	0.80	LOS D	3540	0.85	LOS D
2035	MB-04	Saheed Pankaj Juniyal Marg	3173	0.77	LOS D	3399	0.82	LOS D
Ī	MB-05	Vocational College (Press Enclave Marg)	4795	0.62	LOS C	5136	0.67	LOS C
	MB-06	Malviya Nagar Metro Station (Press Enclave Marg)	5006	0.65	LOS C	5360	0.69	LOS C



#### **TRAFFIC SURVEY (MITIGATION MEASURES)**

#### **CONCLUSION:-**

During most intense peak hour, the incremental traffic from the proposed expansion is insignificant and its contribution to existing network is quite minimal.

Hence it could be said that the project site will contribute insignificant traffic to surrounding road network and hence cause no impact on the adjacent road network tan existing. However it is necessary to correct the situation for future by suggesting few mitigating measures along immediate road network.

#### **Mitigation Measures:-**

The Traffic impacts of the expansion of Select City Walk could be mitigated by adopting few measures:-

- The signage scheme around the project site must provide adequate information in time and every time in a simple sign language which is appropriate for road users so that they can take safe measures.
- On street parking on approach roads outside the project site must be prohibited through regulatory measures. At the entry/ exit gates of project site parking must be strictly avoided to facilitate easy entry and exit as well maintain site distance for entering and leaving traffic. Within the project site, the users must be directed through signs and marshals to basement parking. It is suggested that the guests and physically challenged users must be allow to park at surface level and signs must be posted to make these parking slots clearly visible.
- Pedestrian movement outside and inside the project site must be guided through signs and protected through footpath
  about 150 mm above the road surface. Wherever the pedestrians cross the road, a ramp of suitable gradients (1 in 12)
  must be provided to interchange between levels. On the road, Zebra crossings must be provided to guide the crossing
  pedestrians.

# Green Belt Development Plan

	Green Belt Development at Select City walk						
S.No.	Year	Area Covered	No. of plants planted	Species of plants planted			
1	2008-10	Indoor Plants	600 plants	Arica palm, jed plant, dry cina, royal palm, luca, pansatia, rafish palm, ascodium, zanadu etc			
2	2008-10	8290 Sq Mtr, Open plaza area	328 plants of different varietes & varoius others ground coverage plants	Ficus Benjamina			
			<b>,</b>	Magnolia champaca ( champa )			
				Date Palm ( khajoor )			
				Foxtail Palm Fishtail Palm			
				Rubber Tree			
				Bottle brush plant			
				Herbaceous plant (Banana Tree )			
				Ficus			
3	2008-10	Complete Development of DDA park	168 plants of different varietes	Magnolia champaca ( champa )			
				Ficus Benjamina			
				Bottle brush Plant			
				Hyophorbe lagenicaulis ( Bottle Palm )			
				Azadirachta Indica (Neem )			
4	Aug-10	DDA Park	600 Plants	Black Ficus			
5	Mar-11	Drop Off Point Open Plaza	55 Plants	Bamboo			
6	Mar-11	Drop Off Point Open Plaza	50 Plants	Ficus Panda			
7	May-11	Rear Side of Mall	grass cover in 168m2 area	Grass			
8	Aug-11	Plaza	4	Washingtonian 5' - 6'			
9	Aug-11	Rear side of Mall	50	Ashoka Tree 6' - 7'			
10	Aug-11	DDA Park	350	Ficus 8' - 10'			
11	Nov-11	Rear Side of Mall	100	Golden Panda 4' - 5'			

12	Nov-11	Rear Side of Mall & DDA Park	20000	Enermy 12"
13	Nov-11	DDA Park	25	Neem 4' - 5'
14	May-12	Front side of the mall	800 Plants	Ficus 4' - 8'
15	May-12	Front side of the mall	20000 sq ft of grass cover	Grass
16	Sep-12	DDA Park/Plaza	300	Ficus Panda
17	Sep-12	Plaza	22	Ficus Starlike
18	Sep-12	Mall area/Plaza	175	Ficus
19	Sep-12	Mall area/ Basement	150	Arika Palm
20	Sep-12	DDA Park	1000	Rose
21	Sep-12	DDA Park/Plaza	100	Raat Ki Rani
22	Sep-12	DDA Park/Plaza	1000	Hibiscus
23	Oct-12	DDA Park	1000	Bougenvilia
24	Oct-12	DDA Park	500	Enermy 12"
25	Jul-13	DDA Park	200	Ficus 3' - 4'
26	Jul-13	DDA Park	25	Azadirachta Indica 5' - 6'
27	Jul-13	DDA Park	500	Tikoma Gaudi Chaudi 4' - 5'
28	Jul-13	DDA Park	500	Hibicus 2' 3'
29	Jul-13	DDA Park	500	Bougenvilia 2' - 3'
30	Jul-13	DDA Park	10000	Enermy 12"
31	May-14	DDA Park/Plaza	200	Bougainvillea-2'
32	May-14	Plaza	800	Denali-8"
33	Dec-14	Terrace area	10	Ficus Reginald-9'-10'
34	Dec-14	Terrace area	6	Bougainvillea-6'-8'
35	Dec-14	Terrace area	30	Bougainvillea-2'-3'
36	Dec-14	Rear Side of Mall/Terrace area	61	Plumeria alba (Champa)-10'-12'
37	Dec-14	DDA Park/Plaza	11	Washington Philiphons-8'-10'
38	Jan-15	DDA Park/Plaza	23	Ficus 9'-10'
39	Jan-15	Open Terrace area	6	Bougenvilia 4' - 5'
40	Jan-15	DDA Park	1	Bottle brush plant-6'-8'
41	Jan-15	Open Terrace area/DDA Park	15	Plumeria alba (Champa)-10'-12'
42	Jan-15	DDA Park	1	Hibicus 3-4'
43	Jan-15	Rear Side of Mall	2	Rafish palm-2'-3'
44	Jan-15	Rear Side of Mall/DDA Park	2	Drycina(Green)6
45	Jan-15	Open Terrace area/DDA Park	5	chinese palm
46	Jan-15	Rear Side of Mall/DDA Park	5	Jed plant

47	Jan-15	DDA Park	1	Arica palm
48	Jan-15	Open Terrace area/Plaza	17	Phoenix plant
49	Jan-15	Open Terrace area	1	Pedilanthus plant-6"-8"
50	Jan-15	Open Terrace area/DDA Park	9	Spray grass-2"-3"
51	Dec-15	Back side of the mall	100	Ficus 4'-5'
52	Dec-15	DDA Park	30	Ficus 5'-6'
53	Mar-16	Mall staircase area	200	Arika Palm
54	Sep-16	DDA Park	70	Bougainvillea-2'-3'
55	Sep-16	DDA Park	200	Ficus Panda 9"-12"
56	Sep-16	DDA Park/1st Floor	400	Enermy 12"
			5	Plumeria alba (dwarf) 18" pot (10' Ht. 150mm Girth- 2 Mts
57	Mar-17	SDMC( JAMUN WALA PARK)		canopy)
			15	Bottle palm 6' 7' ht stem (6'-7' stem Ht. 450mm Girth- 2 Mts
58	Mar-17	SDMC( JAMUN WALA PARK)		canopy)
59	Mar-17	SDMC( JAMUN WALA PARK)	15	Cycus palm
60	Mar-17	SDMC( JAMUN WALA PARK)	21	Fish tail palm
			35	Pheonix palm 1' - 2' ht stem (Phoenix roebelleni 1'-6" stem Ht.
61	Mar-17	SDMC( JAMUN WALA PARK)		150mm Girth- 1.5 Mts canopy)
62	Mar-17	SDMC( JAMUN WALA PARK)	5	Cycus Cersanalasis( Ravina Palm)
63	Mar-17	SDMC( JAMUN WALA PARK)	7	Caryota Mitis
64	Mar-17	SDMC( JAMUN WALA PARK)	50	Leropetnun
65	Mar-17	SDMC( JAMUN WALA PARK)	30	Rapis Palm ( 2.5 ft ht)
66	Mar-17	SDMC( JAMUN WALA PARK)	30	Rapis Palm ( 4 ft ht)
67	Mar-17	SDMC( JAMUN WALA PARK)	5	Nolina
68	Mar-17	SDMC( JAMUN WALA PARK)	5	Adenium
69	Mar-17	SDMC( JAMUN WALA PARK)	6	Yuca Elegance
70	Mar-17	SDMC( JAMUN WALA PARK)	12	Silver yucca 14" pot (2' Ht. )
71	Mar-17	SDMC( JAMUN WALA PARK)	30	Juniperous orientalis 4' to 5' ht (4'-5' Ht. well shaped)
72	Mar-17	SDMC( JAMUN WALA PARK)	12	Furcuria 14" pot (Furcaerea 2'-6" dia.)
73	Mar-17	SDMC( JAMUN WALA PARK)	20	Ficus Panda
74	Mar-17	SDMC( JAMUN WALA PARK)	15	Podo carpus
75	Mar-17	SDMC( JAMUN WALA PARK)	200	lxora
76	Mar-17	SDMC( JAMUN WALA PARK)	300	chandni
77	Mar-17	SDMC( JAMUN WALA PARK)	500	boxes
78	Mar-17	SDMC( JAMUN WALA PARK)	50	chinese caronda
		-	·	

Mar-17	SDMC( JAMUN WALA PARK)	100	kevada
Mar-17	SDMC( JAMUN WALA PARK)	20	umberalla palm
Mar-17	SDMC( JAMUN WALA PARK)	600	dynella
Mar-17	SDMC( JAMUN WALA PARK)	100	pittospera
Mar-17	SDMC( JAMUN WALA PARK)	15	Topiary Casurina/ficus panda/
Mar-17	SDMC( JAMUN WALA PARK)	15	Weeping willow
Mar-17	SDMC( JAMUN WALA PARK)	15	Bottle brush
Mar-17	SDMC( JAMUN WALA PARK)	5	Kathal Champa
Mar-17	SDMC( JAMUN WALA PARK)	15	Lyrata compacta
Mar-17	SDMC( JAMUN WALA PARK)	15	Plumerai Alba
Mar-17	SDMC( JAMUN WALA PARK)	5	Brachichitan
		10	Accacia auriculiformis 5' to 6' ht (Acacia auriculiformis 5'-6' Ht.
Mar-17	SDMC( JAMUN WALA PARK)		Girth 60mm Canopy 1 Mt.)
Mar-17	SDMC( JAMUN WALA PARK)	5	Michalia Champa
		10	Ficus nerifolia 4' to 5' ht (4'-5' Ht. Girth 50mm Canopy 0.6 Mt.)
Mar-17	SDMC( JAMUN WALA PARK)		` ' '
		15	Alstonia scholoris 7' to 8' ht (Alastonia scholaris 7'-8' Ht. Girth
Mar-17	SDMC( JAMUN WALA PARK)		100mm Canopy 1.5 Mt.)
Mar-17	SDMC( JAMUN WALA PARK)	5	Neem
		235	F.Benjamina (dark green leaf) 5' to 6' ht (5'-6' Ht. Girth 60mm
Mar-17	SDMC( JAMUN WALA PARK)		Canopy 1 Mt.)
Mar-17	SDMC( JAMUN WALA PARK)	5	Ficus decora
		12	F.retusa 5' to 6' ht (Ficus retusa5'-6' Ht. Girth 100mm Canopy
Mar-17	SDMC( JAMUN WALA PARK)		1.5 Mt.)
Mar-17	SDMC( JAMUN WALA PARK)	12	Ashok (desi) 7' to 8' ht (7'-8' Ht. Girth 60mm Canopy 1 Mt.)
Mar-17	SDMC( JAMUN WALA PARK)	30	Bamboo multiplea
Mar-17	SDMC( JAMUN WALA PARK)	50	Bamboo yellow 8' to 10' ht (8'-10' Ht.)
Mar-17	SDMC( JAMUN WALA PARK)	15	Buddha bally bamboo 6' to 7' ht (6'-7' Ht.)
Mar-17	SDMC( JAMUN WALA PARK)	15	Giant bamboo
Mar-17	SDMC( JAMUN WALA PARK)	4000	Shrubs
Mar-17	SDMC( JAMUN WALA PARK)	14000	Ground cover
Apr-17	Rear Side of Mall	90	RAPHIS PALM 3' -4'
Apr-17	Rear Side of Mall	70	ARECA PALM 4'-5'
•	Danie Ciala af Brail	500	
Apr-17	Rear Side of Mall	500	DINAELIA VARIEGATED
	Mar-17	Mar-17 SDMC( JAMUN WALA PARK)	Mar-17         SDMC( JAMUN WALA PARK)         20           Mar-17         SDMC( JAMUN WALA PARK)         600           Mar-17         SDMC( JAMUN WALA PARK)         100           Mar-17         SDMC( JAMUN WALA PARK)         15           Mar-17         SDMC( JAMUN WALA PARK)         15           Mar-17         SDMC( JAMUN WALA PARK)         15           Mar-17         SDMC( JAMUN WALA PARK)         5           Mar-17         SDMC( JAMUN WALA PARK)         15           Mar-17         SDMC( JAMUN WALA PARK)         15           Mar-17         SDMC( JAMUN WALA PARK)         5           Mar-17         SDMC( JAMUN WALA PARK)         12           Mar-17         SDMC( JAMUN WALA PARK)         12           Mar-17         SDMC( JAMUN WALA PARK)         50

109	Apr-17	Rear Side of Mall	200	sefhlera
110	Apr-17	Rear Side of Mall	200	sefhlera green
111	Apr-17	Rear Side of Mall	200	Drenna rosay
112	Dec-17	Rear Side of Mall	150	RAPHIS PALM 3' -4'
113	Jan-18	Plaza area	250	RAPHIS PALM 3'-4'
114	May-18	Plaza area	100	Bougainvillea 3-4 ft in 16" pot
115	May-18	Plaza area	200	Ixoag Singapuria Red flower , 1.5" height
116	May-18	Plaza area	200	Hybrid Roses bunch flower, with 8" pot
117	May-18	Plaza area	5000	Elorodendan Enermy
118	May-18	Plaza area	2000	Erenthemum
119	May-18	Rear Side of Mall	125	RAPHIS PALM 3'-4'
120	Jul-18	SDMC( JAMUN WALA PARK)	4500sqft	Grass (selection No.1)
121	Jul-18	SDMC( JAMUN WALA PARK)	100	Hybrid Roses bunch flower, with 8" pot
122	Jul-18	SDMC( JAMUN WALA PARK)	600	Green wall plants
123	Aug-18	DDA Park	50	Golden Panda 1'-2'
124	Nov-18	Distribution	150	Herbal (indoor air purifying)
125	Nov-18	DDA park	500	Rose with 1 feet height
126	Nov-18	Plaza	100	Poinsettia with 8" pot
127	Nov-18	Plaza	400	Earthern Pot (clay ) 8" Dia
128	Nov-18	Opposite Gate no 2	3000	Good Earth (one truck having 600 cfeet)
129	Jan-19	DDA park	500	Rose plant
130	Jan-19	Plaza	600	Earthern Pot (clay ) 8" Dia
131	Jan-19	Opposite Gate no 2	3000	Good Earth
132	Jul-19	Plaza area	200	Tikoma Gwaraf 1'.5"-'2'.5"
133	Sep-19	SDMC( JAMUN WALA PARK)	105	Tikoma Gaudi Chaudi 1'
134	Sep-19	SDMC( JAMUN WALA PARK)	17	Neem 1-'2'
135	Sep-19	SDMC( JAMUN WALA PARK)	7	Aam Tree 2' - 3'
136	Sep-19	SDMC( JAMUN WALA PARK)	6	Jamun Tree 2' - 3'
137	Oct-19	SDMC( JAMUN WALA PARK)	16	Hibicus 3'-4'
138	Oct-19	SDMC( JAMUN WALA PARK)	200	Bougenvilia 2' - 3'
139	Oct-19	Rear Side of Mall ( Gate No.02 )	170	Tikoma Gaudi Chaudi 1'
140	Oct-19	Plaza area (water body)	150	Tikoma Gaudi Chaudi 1'
141	Nov-19	DDA Park	25	Hibiscus-1'-2'
142	Nov-19	DDA Park	30	Ficus Panda-1'-2'
143	Dec-19 to Feb-2020	Plaza area and DDA Park	1390	Calendula

144	Dec-19 to Feb-2020	Plaza area and DDA Park	1470	Salvia
145	Dec-19 to Feb-2020	Plaza area and DDA Park	2000	Babuna
146	Dec-19 to Feb-2020	Plaza area and DDA Park	800	Cinneneria
147	Dec-19 to Feb-2020	Plaza area and DDA Park	707	Dianthus
148	Dec-19 to Feb-2020	Plaza area and DDA Park	1280	Ice flower
149	Dec-19 to Feb-2020	Plaza area and DDA Park	1150	Phlox
150	Dec-19 to Feb-2020	Plaza area and DDA Park	421	Stock
151	Dec-19 to Feb-2020	Plaza area and DDA Park	430	Marigold
152	Dec-19 to Feb-2020	Plaza area and DDA Park	250	Hollyhocks (alcea rosea)
153	Dec-19 to Feb-2020	Plaza area and DDA Park	452	Dahlia double
154	Dec-19 to Feb-2020	Plaza area and DDA Park	1150	Dahlia single
155	Dec-19 to Feb-2020	Plaza area and DDA Park	4000	Alyssum
156	Dec-19 to Feb-2020	Plaza area and DDA Park	200	Kale
157	Dec-19 to Feb-2020	Plaza area and DDA Park	180	Marigold jafri
158	Dec-19 to Feb-2020	Plaza area and DDA Park	400	Guldavri single
159	Dec-19 to Feb-2020	Plaza area and DDA Park	125	Guldavri double
160	Dec-19 to Feb-2020	Plaza area and DDA Park	320	Straw
161	Dec-19 to Feb-2020	Plaza area and DDA Park	841	Gazania
162	Dec-19 to Feb-2020	Plaza area and DDA Park	134	Sweet William
163	Dec-19 to Feb-2020	Plaza area and DDA Park	150	kalanchoe
164	Dec-19 to Feb-2020	Plaza area and DDA Park	800	Antirrhinum (dog flower)
165	Dec-19 to Feb-2020	Plaza area and DDA Park	525	Pansy
166	Dec-19 to Feb-2020	Plaza area and DDA Park	2740	Petunia
167	Dec-19	Inside mall	200	Poinsettia with 8" pot
168	Feb-20	Plaza area	500	Dahlia double hybrid
169	Apr-20	Plaza area and DDA Park	500	Sadabahar
170	Apr-20 to July -20	Plaza area and DDA Park	1700	Kochia
171	Apr-20 to June -20	Plaza area and DDA Park	1200	Zinia
172	Apr-20 to June -20	Plaza area and DDA Park	900	Sunflower
173	Apr-20 to June -20	Plaza area and DDA Park	700	Cosmos
174	Jun-20	Plaza area	115	Acalypha
175	Jul-20	DDA Park	120	Ficus
176	Aug-20	Plaza area	500	Tikoma Gaudi Chaudi 1'
177	Aug-20	DDA Park	40	Money plant
178	Aug-20	DDA Park	35	Hibiscus-1'-2'
			-	

180   Nov-20   SDMC( JAMUN WALA PARK)   500   Tikoma Gaudi Chaudi 1'   181   Nov-20   DDA Park   200   Tikoma Gaudi Chaudi 1'   182   Nov-20   DDA Park   200   Tikoma Gaudi Chaudi 1'   182   Nov-20 to Mar 21   Plaza area and DDA Park   600   Guldwari flower   183   Nov-20 to Mar 21   Plaza area and DDA Park   4500   Elasium flower   185   Nov-20 to Mar 21   Plaza area and DDA Park   2600   Calendula   186   Nov-20 to Mar 21   Plaza area and DDA Park   550   Gazania   187   Nov-20 to Mar 21   Plaza area and DDA Park   1400   Salvia   188   Nov-20 to Mar 21   Plaza area and DDA Park   1400   Salvia   188   Nov-20 to Mar 21   Plaza area and DDA Park   1400   Salvia   188   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Marigold   190   Nov-20 to Mar 21   Plaza area and DDA Park   300   Marigold   190   Nov-20 to Mar 21   Plaza area and DDA Park   700   Dahlia double   191   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Pitonia   191   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Pitonia   191   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Antirrhinum (dog flower)   193   Nov-20 to Mar 21   Plaza area and DDA Park   500   Antirrhinum (dog flower)   193   Nov-20 to Mar 21   Plaza area and DDA Park   500   Antirrhinum (dog flower)   193   Nov-20 to Mar 21   Plaza area and DDA Park   500   Babuna   194   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus   194   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus   195   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus   196   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus   197   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus   197   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus   197   Nov-20 to Mar 21   Plaza area and DDA Park   500   Poinsettia with 8" pot   198   Nov-20 to Mar 21   Plaza area and DDA Park   500   Poinsettia with 8" pot   198   Nov-20 to Mar 21   Plaza area and DDA Park   500   Poinsettia with 8" pot   198   Nov-20 to Mar 21   Plaza area and DDA Park   5	179	Sep-20	DDA Park	110	Jatropha
181	180	•	SDMC( JAMUN WALA PARK)	500	•
183   Nov-20 to Mar 21   Plaza area and DDA Park   4500   Elasium flower	181	Nov-20		200	Tikoma Gaudi Chaudi 1'
183   Nov-20 to Mar 21   Plaza area and DDA Park   4500   Elasium flower	182	Nov-20	DDA Park	240	Ficus Panda
184   Nov-20 to Mar 21	183	Nov-20 to Mar 21	Plaza area and DDA Park	600	•
185   Nov-20 to Mar 21   Plaza area and DDA Park   2600   Calendula	184	Nov-20 to Mar 21	Plaza area and DDA Park	4500	
187   Nov-20 to Mar 21   Plaza area and DDA Park   1400   Salvia	185	Nov-20 to Mar 21	Plaza area and DDA Park	2600	
188         Nov-20 to Mar 21         Plaza area and DDA Park         1000         Stock           189         Nov-20 to Mar 21         Plaza area and DDA Park         300         Marigold           190         Nov-20 to Mar 21         Plaza area and DDA Park         700         Dahlia double           191         Nov-20 to Mar 21         Plaza area and DDA Park         2000         Pittonia           192         Nov-20 to Mar 21         Plaza area and DDA Park         500         Antirrhinum (dog flower)           193         Nov-20 to Mar 21         Plaza area and DDA Park         200         Babuna           194         Nov-20 to Mar 21         Plaza area and DDA Park         600         Cinneneria           195         Nov-20 to Mar 21         Plaza area and DDA Park         500         Dianthus           196         Nov-20 to Mar 21         Plaza area and DDA Park         500         Dianthus           197         Nov-20 to Mar 21         Plaza area and DDA Park         500         December 1           198         Nov-20 to Mar 21         Plaza area and DDA Park         200         Pansy           199         Nov-20 to Mar 21         Plaza area and DDA Park         200         Poinsettia with 8" pot           200         Dec-20         I	186	Nov-20 to Mar 21	Plaza area and DDA Park	550	Gazania
189   Nov-20 to Mar 21   Plaza area and DDA Park   300   Marigold     190   Nov-20 to Mar 21   Plaza area and DDA Park   700   Dahlia double     191   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Pitonia     192   Nov-20 to Mar 21   Plaza area and DDA Park   500   Antirrhinum (dog flower)     193   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Babuna     194   Nov-20 to Mar 21   Plaza area and DDA Park   600   Cinneneria     195   Nov-20 to Mar 21   Plaza area and DDA Park   800   Sweet William     196   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus     197   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus     198   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Ice flower     198   Nov-20 to Mar 21   Plaza area and DDA Park   200   Pansy     199   Nov-20 to Mar 21   Plaza area and DDA Park   200   Poinsettia with 8" pot     199   Nov-20   Inside mall   200   Poinsettia with 8" pot     200   Dec-20   Inside mall   200   Poinsettia with 8" pot     201   Feb-21   Plaza area   400   Dahlia double     202   Mar-21   DDA Park   200   Pansy     203   Mar-21   DDA Park   375   Bimca     204   Mar-21   Plaza area   400   Celosia     205   Mar-21   Plaza area   400   Celosia     206   Apr-21   Plaza area and DDA Park   2500   Kochia     207   Apr-21   Plaza area and DDA Park   400   Zinia     208   Apr-21   Plaza area and DDA Park   400   Sunflower     209   Apr-21   Plaza area and DDA Park   600   Sunflower     209   Apr-21   Plaza area and DDA Park   600   Porttaloca     210   Apr-21   Plaza area and DDA Park   200   Porttaloca     211   Apr-21   Plaza area and DDA Park   200   Porttaloca     212   Apr-21   Plaza area and DDA Park   200   Porttaloca     212   Apr-21   Plaza area and DDA Park   200   Porttaloca     212   Apr-21   Plaza area and DDA Park   200   Porttaloca     213   Apr-21   Plaza area and DDA Park   200   Porttaloca     214   Apr-21   Plaza area and DDA Park   200   Porttaloca     215   Apr-21   Plaza area and DDA Park   200   Porttaloca     216   Apr-21	187	Nov-20 to Mar 21	Plaza area and DDA Park	1400	Salvia
190   Nov-20 to Mar 21   Plaza area and DDA Park   700   Dahlia double     191   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Pitonia     192   Nov-20 to Mar 21   Plaza area and DDA Park   500   Antirrhinum (dog flower)     193   Nov-20 to Mar 21   Plaza area and DDA Park   200   Babuna     194   Nov-20 to Mar 21   Plaza area and DDA Park   600   Cinneneria     195   Nov-20 to Mar 21   Plaza area and DDA Park   800   Sweet William     196   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus     197   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Dianthus     198   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Lee flower     198   Nov-20 to Mar 21   Plaza area and DDA Park   200   Pansy     199   Nov-20   Inside mall   200   Poinsettia with 8" pot     200   Dec-20   Inside mall   200   Poinsettia with 8" pot     201   Feb-21   plaza area   400   Dahlia double     202   Mar-21   DDA Park   200   Pansy     203   Mar-21   DDA Park   375   Bimca     204   Mar-21   plaza area   400   Celosia     205   Mar-21   plaza area   400   Celosia     206   Apr-21   Plaza area   400   Celosia     207   Apr-21   Plaza area   400   Celosia     208   Apr-21   Plaza area and DDA Park   2500   Sunflower     209   Apr-21   Plaza area and DDA Park   400   Sunflower     209   Apr-21   Plaza area and DDA Park   400   Cosmos     200   Apr-21   Plaza area and DDA Park   400   Cosmos     201   Apr-21   Plaza area and DDA Park   400   Caladium     202   Apr-21   Plaza area and DDA Park   400   Caladium     203   Apr-21   Plaza area and DDA Park   400   Caladium     204   Apr-21   Plaza area and DDA Park   400   Caladium     207   Apr-21   Plaza area and DDA Park   400   Caladium     208   Apr-21   Plaza area and DDA Park   400   Caladium     209   Apr-21   Plaza area and DDA Park   400   Caladium     210   Apr-21   Plaza area and DDA Park   400   Caladium     211   Apr-21   Plaza area and DDA Park   400   Caladium     212   Apr-21   Plaza area and DDA Park   400   Caladium     213   Apr-21   Plaza area and DDA	188	Nov-20 to Mar 21	Plaza area and DDA Park	1000	Stock
190   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Pitonia     191   Nov-20 to Mar 21   Plaza area and DDA Park   2000   Pitonia     192   Nov-20 to Mar 21   Plaza area and DDA Park   500   Antirrhinum (dog flower)     193   Nov-20 to Mar 21   Plaza area and DDA Park   200   Babuna     194   Nov-20 to Mar 21   Plaza area and DDA Park   600   Cinneneria     195   Nov-20 to Mar 21   Plaza area and DDA Park   800   Sweet William     196   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus     197   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Lice flower     198   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Lice flower     198   Nov-20 to Mar 21   Plaza area and DDA Park   200   Pansy     199   Nov-20   Inside mall   200   Poinsettia with 8" pot     200   Dec-20   Inside mall   200   Poinsettia with 8" pot     201   Feb-21   plaza area   400   Dahlia double     202   Mar-21   DDA Park   200   Pansy     203   Mar-21   DDA Park   375   Bimca     204   Mar-21   plaza area   400   Celosia     205   Mar-21   plaza area   400   Celosia     206   Apr-21   Plaza area and DDA Park   2500   Kochia     207   Apr-21   Plaza area and DDA Park   2500   Sunflower     208   Apr-21   Plaza area and DDA Park   400   Zinia     209   Apr-21   Plaza area and DDA Park   400   Sunflower     209   Apr-21   Plaza area and DDA Park   400   Cosmos     200   Apr-21   Plaza area and DDA Park   400   Cosmos     201   Apr-21   Plaza area and DDA Park   400   Cosmos     202   Apr-21   Plaza area and DDA Park   400   Cosmos     203   Apr-21   Plaza area and DDA Park   400   Cosmos     204   Apr-21   Plaza area and DDA Park   400   Cosmos     205   Apr-21   Plaza area and DDA Park   400   Cosmos     206   Apr-21   Plaza area and DDA Park   400   Cosmos     207   Apr-21   Plaza area and DDA Park   400   Cosmos     208   Apr-21   Plaza area and DDA Park   400   Cosmos     209   Apr-21   Plaza area and DDA Park   400   Cosmos     210   Apr-21   Plaza area and DDA Park   400   Cosmos     211   Apr-21   Plaza area and D	189	Nov-20 to Mar 21	Plaza area and DDA Park	300	Marigold
192   Nov-20 to Mar 21   Plaza area and DDA Park   500   Antirrhinum (dog flower)     193   Nov-20 to Mar 21   Plaza area and DDA Park   200   Babuna     194   Nov-20 to Mar 21   Plaza area and DDA Park   600   Cinneneria     195   Nov-20 to Mar 21   Plaza area and DDA Park   800   Sweet William     196   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus     197   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Ice flower     198   Nov-20 to Mar 21   Plaza area and DDA Park   200   Pansy     199   Nov-20 to Mar 21   Plaza area and DDA Park   200   Poinsettia with 8" pot     190   Dec-20   Inside mall   200   Poinsettia with 8" pot     201   Feb-21   Plaza area   400   Dahlia double     202   Mar-21   DDA Park   200   Pansy     203   Mar-21   DDA Park   200   Pansy     204   Mar-21   DDA Park   375   Bimca     205   Mar-21   DDA Park   375   Bimca     206   Apr-21   Plaza area   400   Celosia     207   Apr-21   Plaza area   350   Tikoma hybrid     208   Apr-21   Plaza area and DDA Park   400   Zinia     209   Apr-21   Plaza area and DDA Park   400   Sunflower     209   Apr-21   Plaza area and DDA Park   400   Cosmos     200   Apr-21   Plaza area and DDA Park   400   Cosmos     201   Apr-21   Plaza area and DDA Park   400   Cosmos     202   Apr-21   Plaza area and DDA Park   400   Cosmos     203   Apr-21   Plaza area and DDA Park   400   Pointaloca     204   Apr-21   Plaza area and DDA Park   400   Pointaloca     207   Apr-21   Plaza area and DDA Park   400   Pointaloca     208   Apr-21   Plaza area and DDA Park   400   Pointaloca     209   Apr-21   Plaza area and DDA Park   400   Pointaloca     210   Apr-21   Plaza area and DDA Park   400   Caladium     211   Apr-21   Plaza area and DDA Park   400   Caladium     212   Apr-21   Plaza area and DDA Park   400   Galadium     213   Apr-21   Plaza area and DDA Park   400   Galadium     214   Apr-21   Plaza area and DDA Park   400   Galadium	190	Nov-20 to Mar 21	Plaza area and DDA Park	700	
193   Nov-20 to Mar 21   Plaza area and DDA Park   200   Babuna     194   Nov-20 to Mar 21   Plaza area and DDA Park   600   Cinneneria     195   Nov-20 to Mar 21   Plaza area and DDA Park   800   Sweet William     196   Nov-20 to Mar 21   Plaza area and DDA Park   500   Dianthus     197   Nov-20 to Mar 21   Plaza area and DDA Park   1500   Ice flower     198   Nov-20 to Mar 21   Plaza area and DDA Park   200   Pansy     199   Nov-20   Inside mall   200   Poinsettia with 8" pot     200   Dec-20   Inside mall   200   Poinsettia with 8" pot     201   Feb-21   plaza area   400   Dahlia double     202   Mar-21   DDA Park   200   Pansy     203   Mar-21   DDA Park   200   Pansy     204   Mar-21   plaza area   400   Celosia     205   Mar-21   plaza area   400   Celosia     206   Apr-21   Plaza area   350   Tikoma hybrid     207   Apr-21   Plaza area and DDA Park   2500   Kochia     208   Apr-21   Plaza area and DDA Park   400   Zinia     209   Apr-21   Plaza area and DDA Park   400   Sunflower     209   Apr-21   Plaza area and DDA Park   600   Sunflower     209   Apr-21   Plaza area and DDA Park   400   Cosmos     210   Apr-21   Plaza area and DDA Park   200   Porttaloca     211   Apr-21   Plaza area and DDA Park   200   Porttaloca     211   Apr-21   Plaza area and DDA Park   200   Caladium     212   Apr-21   Plaza area and DDA Park   150   Gumfrina     200   Caladium     212   Apr-21   Plaza area and DDA Park   150   Gumfrina     200   Caladium     212   Apr-21   Plaza area and DDA Park   150   Gumfrina     200   Caladium     200   Caladium     201   Apr-21   Plaza area and DDA Park   150   Gumfrina     201   Apr-21   Plaza area and DDA Park   200   Porttaloca     202   Caladium     203   Caladium     204   Apr-21   Plaza area and DDA Park   200   Caladium     204   Apr-21   Plaza area and DDA Park   200   Caladium     205   Apr-21   Plaza area and DDA Park   200   Caladium     206   Apr-21   Plaza area and DDA Park   200   Caladium     207   Apr-21   Plaza area and DDA Park   200   Caladium     208   Apr-21   Plaz	191	Nov-20 to Mar 21	Plaza area and DDA Park	2000	Pitonia
194         Nov-20 to Mar 21         Plaza area and DDA Park         600         Cinneneria           195         Nov-20 to Mar 21         Plaza area and DDA Park         800         Sweet William           196         Nov-20 to Mar 21         Plaza area and DDA Park         500         Dianthus           197         Nov-20 to Mar 21         Plaza area and DDA Park         1500         Ice flower           198         Nov-20 to Mar 21         Plaza area and DDA Park         200         Pansy           199         Nov-20 to Mar 21         Plaza area and DDA Park         200         Poinsettia with 8" pot           200         Dec-20         Inside mall         200         Poinsettia with 8" pot           201         Feb-21         plaza area         400         Dahlia double           202         Mar-21         DDA Park         200         Pansy           203         Mar-21         DDA Park         375         Bimca           204         Mar-21         plaza area         400         Celosia           205         Mar-21         plaza area         350         Tikoma hybrid           206         Apr-21         Plaza area and DDA Park         2500         Kochia           207         Apr-21 <td>192</td> <td>Nov-20 to Mar 21</td> <td>Plaza area and DDA Park</td> <td>500</td> <td>Antirrhinum (dog flower)</td>	192	Nov-20 to Mar 21	Plaza area and DDA Park	500	Antirrhinum (dog flower)
195         Nov-20 to Mar 21         Plaza area and DDA Park         800         Sweet William           196         Nov-20 to Mar 21         Plaza area and DDA Park         500         Dianthus           197         Nov-20 to Mar 21         Plaza area and DDA Park         1500         Ice flower           198         Nov-20 to Mar 21         Plaza area and DDA Park         200         Pansy           199         Nov-20         Inside mall         200         Poinsettia with 8" pot           200         Dec-20         Inside mall         200         Poinsettia with 8" pot           201         Feb-21         plaza area         400         Dahlia double           202         Mar-21         DDA Park         200         Pansy           203         Mar-21         DDA Park         375         Bimca           204         Mar-21         plaza area         400         Celosia           205         Mar-21         plaza area         350         Tikoma hybrid           206         Apr-21         Plaza area and DDA Park         2500         Kochia           207         Apr-21         Plaza area and DDA Park         400         Sunflower           208         Apr-21         Plaza area and DDA	193	Nov-20 to Mar 21	Plaza area and DDA Park	200	Babuna
196 Nov-20 to Mar 21 Plaza area and DDA Park 1500 Dianthus  197 Nov-20 to Mar 21 Plaza area and DDA Park 1500 Ice flower  198 Nov-20 to Mar 21 Plaza area and DDA Park 200 Pansy  199 Nov-20 Inside mall 200 Poinsettia with 8" pot  200 Dec-20 Inside mall 200 Poinsettia with 8" pot  201 Feb-21 plaza area 400 Dahlia double  202 Mar-21 DDA Park 200 Pansy  203 Mar-21 DDA Park 375 Bimca  204 Mar-21 plaza area 400 Celosia  205 Mar-21 plaza area 350 Tikoma hybrid  206 Apr-21 Plaza area and DDA Park 2500 Kochia  207 Apr-21 Plaza area and DDA Park 400 Tinia  208 Apr-21 Plaza area and DDA Park 400 Tinia  209 Apr-21 Plaza area and DDA Park 400 Tombour 200 Cosmos  209 Apr-21 Plaza area and DDA Park 400 Tombour 200 Cosmos  209 Apr-21 Plaza area and DDA Park 400 Tombour 200 Cosmos  209 Apr-21 Plaza area and DDA Park 400 Tombour 200 Cosmos  210 Apr-21 Plaza area and DDA Park 200 Porttaloca  211 Apr-21 Plaza area and DDA Park 200 Caladium  212 Apr-21 Plaza area and DDA Park 100 Caladium  213 Apr-21 Plaza area and DDA Park 100 Caladium  214 Apr-21 Plaza area and DDA Park 150 Gumfrina	194	Nov-20 to Mar 21	Plaza area and DDA Park	600	Cinneneria
197         Nov-20 to Mar 21         Plaza area and DDA Park         1500         Ice flower           198         Nov-20 to Mar 21         Plaza area and DDA Park         200         Poinsettia with 8" pot           199         Nov-20         Inside mall         200         Poinsettia with 8" pot           200         Dec-20         Inside mall         200         Poinsettia with 8" pot           201         Feb-21         plaza area         400         Dallia double           202         Mar-21         DDA Park         200         Pansy           203         Mar-21         DDA Park         375         Bimca           204         Mar-21         plaza area         400         Celosia           205         Mar-21         plaza area         350         Tikoma hybrid           206         Apr-21         Plaza area and DDA Park         2500         Kochia           207         Apr-21         Plaza area and DDA Park         400         Zinia           208         Apr-21         Plaza area and DDA Park         400         Sunflower           209         Apr-21         Plaza area and DDA Park         300         Cosmos           210         Apr-21         Plaza area and DDA Park	195	Nov-20 to Mar 21	Plaza area and DDA Park	800	Sweet William
198         Nov-20 to Mar 21         Plaza area and DDA Park         200         Poinsettia with 8" pot           199         Nov-20         Inside mall         200         Poinsettia with 8" pot           200         Dec-20         Inside mall         200         Poinsettia with 8" pot           201         Feb-21         plaza area         400         Dahlia double           202         Mar-21         DDA Park         200         Pansy           203         Mar-21         DDA Park         375         Bimca           204         Mar-21         plaza area         400         Celosia           205         Mar-21         plaza area         350         Tikoma hybrid           206         Apr-21         Plaza area and DDA Park         2500         Kochia           207         Apr-21         Plaza area and DDA Park         400         Zinia           208         Apr-21         Plaza area and DDA Park         600         Sunflower           209         Apr-21         Plaza area and DDA Park         300         Cosmos           210         Apr-21         Plaza area and DDA Park         200         Porttaloca           211         Apr-21         Plaza area and DDA Park         10	196	Nov-20 to Mar 21	Plaza area and DDA Park	500	Dianthus
199         Nov-20         Inside mall         200         Poinsettia with 8" pot           200         Dec-20         Inside mall         200         Poinsettia with 8" pot           201         Feb-21         plaza area         400         Dahlia double           202         Mar-21         DDA Park         200         Pansy           203         Mar-21         DDA Park         375         Bimca           204         Mar-21         plaza area         400         Celosia           205         Mar-21         plaza area         350         Tikoma hybrid           206         Apr-21         Plaza area and DDA Park         2500         Kochia           207         Apr-21         Plaza area and DDA Park         400         Zinia           208         Apr-21         Plaza area and DDA Park         600         Sunflower           209         Apr-21         Plaza area and DDA Park         300         Cosmos           210         Apr-21         Plaza area and DDA Park         200         Porttaloca           211         Apr-21         Plaza area and DDA Park         100         Caladium           212         Apr-21         Plaza area and DDA Park         150         Gumfr	197	Nov-20 to Mar 21	Plaza area and DDA Park	1500	Ice flower
200Dec-20Inside mall200Poinsettia with 8" pot201Feb-21plaza area400Dahlia double202Mar-21DDA Park200Pansy203Mar-21DDA Park375Bimca204Mar-21plaza area400Celosia205Mar-21plaza area350Tikoma hybrid206Apr-21Plaza area and DDA Park2500Kochia207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	198	Nov-20 to Mar 21	Plaza area and DDA Park	200	Pansy
201Feb-21plaza area400Dahlia double202Mar-21DDA Park200Pansy203Mar-21DDA Park375Bimca204Mar-21plaza area400Celosia205Mar-21plaza area350Tikoma hybrid206Apr-21Plaza area and DDA Park2500Kochia207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	199	Nov-20	Inside mall	200	Poinsettia with 8" pot
202Mar-21DDA Park200Pansy203Mar-21DDA Park375Bimca204Mar-21plaza area400Celosia205Mar-21plaza area350Tikoma hybrid206Apr-21Plaza area and DDA Park2500Kochia207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	200	Dec-20	Inside mall	200	Poinsettia with 8" pot
203Mar-21DDA Park375Bimca204Mar-21plaza area400Celosia205Mar-21plaza area350Tikoma hybrid206Apr-21Plaza area and DDA Park2500Kochia207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	201	Feb-21	plaza area	400	Dahlia double
204Mar-21plaza area400Celosia205Mar-21plaza area350Tikoma hybrid206Apr-21Plaza area and DDA Park2500Kochia207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	202	Mar-21	DDA Park	200	Pansy
205Mar-21plaza area350Tikoma hybrid206Apr-21Plaza area and DDA Park2500Kochia207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	203	Mar-21	DDA Park	375	Bimca
206Apr-21Plaza area and DDA Park2500Kochia207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	204	Mar-21	plaza area	400	Celosia
207Apr-21Plaza area and DDA Park400Zinia208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	205	Mar-21	plaza area	350	Tikoma hybrid
208Apr-21Plaza area and DDA Park600Sunflower209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	206	Apr-21	Plaza area and DDA Park	2500	Kochia
209Apr-21Plaza area and DDA Park300Cosmos210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	207	Apr-21	Plaza area and DDA Park	400	Zinia
210Apr-21Plaza area and DDA Park200Porttaloca211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	208	Apr-21	Plaza area and DDA Park	600	Sunflower
211Apr-21Plaza area and DDA Park100Caladium212Apr-21Plaza area and DDA Park150Gumfrina	209	Apr-21	Plaza area and DDA Park	300	Cosmos
212 Apr-21 Plaza area and DDA Park 150 Gumfrina	210	Apr-21	Plaza area and DDA Park	200	Porttaloca
	211	Apr-21	Plaza area and DDA Park	100	Caladium
213 Apr-21 Plaza area and DDA Park 500 Gladia	212	Apr-21	Plaza area and DDA Park	150	Gumfrina
	213	Apr-21	Plaza area and DDA Park	500	Gladia

214	Apr-21	Plaza area and DDA Park	300	Sadabhar
215	Apr-21 to July-21	Plaza area and DDA Park	80	Aglonima
216	Apr-21 to July-21	Plaza area and DDA Park	170	Aklifa
217	Apr-21 to July-21	Plaza area and DDA Park	120	Enermy
218	Apr-21 to July-21	Plaza area and DDA Park	500	Desi Ticoma
219	Apr-21 to July-21	Plaza area and DDA Park	100	Panda
220	Apr-21 to July-21	Plaza area and DDA Park	51	Hibiscus
221	Apr-21 to July-21	Plaza area and DDA Park	200	Lalsa
222	Apr-21 to July-21	Plaza area and DDA Park	150	Tulsi plant
223	Apr-21 to July-21	Plaza area and DDA Park	50	Money plant
224	Apr-21 to July-21	Plaza area and DDA Park	300	Long iland panda
225	Apr-21 to July-21	Plaza area and DDA Park	50	Benjumina Ficus panda
226	Aug-21	Plaza area and DDA Park	200	Acalypha plant
227	Aug-21	Plaza area and DDA Park	150	Hibiscus plant
228	Aug-21	Plaza area and DDA Park	75	Aglonema plant
229	Aug-21	Plaza area and DDA Park	170	Ficus plant
230	Aug-21	Plaza area and DDA Park	4	Tecoma Hybrid
231	Aug-21	Plaza area and DDA Park	500	Batelia belt
232	Aug-21	Plaza area and DDA Park	350	Red grass
233	Aug-21	Plaza area and DDA Park	600	Panda plant
234	Aug-21	Plaza area and DDA Park	700	Tecoma desi
235	Aug-21	Plaza area and DDA Park	150	Enermy plat
236	Aug-21	Plaza area and DDA Park	50	Champa flower
237	Nov-21 to feb 22	Plaza area and DDA Park	3000	Pitonia
238	Nov-21 to feb 22	Plaza area and DDA Park	500	Dianthus
239	Nov-21 to feb 22	Plaza area and DDA Park	900	Stock
240	Nov-21 to feb 22	Plaza area and DDA Park	600	Antirrhinum (dog flower)
241	Nov-21 to feb 22	Plaza area and DDA Park	1500	Elasium flower
242	Nov-21 to feb 22	Plaza area and DDA Park	250	Cabbage flower
243	Nov-21 to feb 22	Plaza area and DDA Park	250	Babuna
244	Nov-21 to feb 22	Plaza area and DDA Park	300	Calendula
245	Nov-21 to feb 22	Plaza area and DDA Park	1200	Sweet William
246	Nov-21 to feb 22	Plaza area and DDA Park	500	Gazania
247	Nov-21 to feb 22	Plaza area and DDA Park	1500	Hibrid Dhalia
248	Nov-21 to feb 22	Plaza area and DDA Park	900	Guldawri local

249	Nov-21 to feb 22	Plaza area and DDA Park	200	Guldawri hybrid
250	Nov-21 to feb 22	Plaza area and DDA Park	700	Jafri
251	Nov-21 to feb 22	Plaza area and DDA Park	1000	Salvia
252	Nov-21 to feb 22	Plaza area and DDA Park	700	Cookscomb Murga flower
253	Nov-21 to feb 22	Plaza area and DDA Park	300	Pansy
254	Nov-21 to feb 22	Plaza area and DDA Park	300	Cinneneria
255	Nov-21 to feb 22	Plaza area and DDA Park	100	Hollyhocks (alcea rosea)
256	Nov-21 to feb 22	Plaza area and DDA Park	300	Barbina
257	Nov-21 to feb 22	Plaza area and DDA Park	50	Tulip
258	Nov-21 to feb 22	Inside mall	200	Poinsettia with 8" pot
259	Apr-22 to Jun.22	Plaza area and DDA Park	600	Ice flower
260	Apr-22 to Jun.22	Plaza area and DDA Park	1200	Zinia
261	Apr-22 to Jun.22	Plaza area and DDA Park	350	Vinca
262	Apr-22 to Jun.22	Plaza area and DDA Park	3500	Kochia
263	Apr-22 to Jun.22	Plaza area and DDA Park	400	Sadabhar
264	Apr-22 to Jun.22	Plaza area and DDA Park	600	Sunflower
265	Apr-22 to Jun.22	Plaza area and DDA Park	200	Celosia
266	Apr-22 to Jun.22	Plaza area and DDA Park	500	Cooks Murga flower
267	Apr-22 to Jun.22	Plaza area and DDA Park	300	Photuelaca
268	Apr-22 to Jun.22	Plaza area and DDA Park	300	Gamphirina
269	Apr-22 to Jun.22	Plaza area and DDA Park	500	Gladia
270	Apr-22 to Jun.22	Plaza area and DDA Park	500	Cosmos
271	Apr-22 to Jun.22	SDMC( Jamun park)	300	Zinia
272	Apr-22 to Jun.22	SDMC( Jamun park)	150	Sunflower
273	Apr-22 to Jun.22	SDMC( Jamun park)	100	Sadabhar
274	Apr-22 to Jun.22	SDMC( Jamun park)	300	Kochia
275	Sep-22	Gandhi Park	3	Champa
276	Sep-22	Gandhi Park	8	Phoenix plam
277	Sep-22	Gandhi Park	100	Draceana dwraf
278	Sep-22	Gandhi Park	50	Draceana Victoria
279	Sep-22	Gandhi Park	100	Draceana chlorima Red
280	Sep-22	Gandhi Park	100	Draceana chlorima Var
281	Sep-22	Gandhi Park	50	Draceana Mahalma
282	Sep-22	Gandhi Park	897	Saflera Vari
283	Sep-22	Gandhi Park	50	Xemardo Selam
		<u> </u>		<del></del>

284	Sep-22	Gandhi Park	260	Arica palm
285	Sep-22	Gandhi Park	100	Cefolia elegance
286	Sep-22	Gandhi Park	100	Chandani Dwraf
287	Sep-22	Gandhi Park	50	Crotom pilra
288	Sep-22	Gandhi Park	99	Pitosphora
289	Sep-22	Gandhi Park	50	Alpinea vari
290	Sep-22	Gandhi Park	500	Draceana Milky
291	Sep-22	Gandhi Park	498	Song of india
292	Sep-22	Gandhi Park	2046	Wadelia
293	Sep-22	Gandhi Park	2037	Ribbon grass
294	Sep-22	Gandhi Park	1045	Fiens Longice land
295	Sep-22	Gandhi Park	1039	Dinella
296	Sep-22	Gandhi Park	208	Satcasia
297	Sep-22	Gandhi Park	3	Saflera Vari
298	Sep-22	Gandhi Park	1	Pittospera
299	Sep-22	Gandhi Park	10	Mitis palm
300	Nov-22	Mall area	450	Bougenvellia
301	Dec-22	Mall area	450	Poinsettia
302	Mar-23	My square	120	Rapis plam
303	Mar-23	My square	30	Aglonima
304	Mar-23	Mall area	50	Arica palm
305	Mar-23	Mall area	20	Aglonima
306	Mar-23	Mall area	20	Money plant
307	Mar-23	Mall area	250	Ticoma Hybrid

# Structural Stability Certificate

JAITLY ASSOCIATES
Consulting Engineers

E-60, 2nd Floor
Masjid Moth
Greater Kallash-III
New Delhi-110048
Tel. 011-4056-9877
E-mail: njaitly49@gmail.com
njaitly49@yahoo.com

Date: 28.01.2020

#### TO WHOM SO EVER IT MAY CONCERN

This is to certify that the proposed Select City Walk at Plot No A- 3, and P1B, District Centre, Saket, New Delhi - 17 for M/S Select Infrastructure has been designed in accordance with the logical provisions of latest edition of National Building Code of India and prevailing relevant Codes of Bureau of Indian Standards for structural stability and to withstand the earthquake impact. The seismic zone considered in design is Zone IV as per IS -1893 (part I) 2016. Further, we certify that the structure is considered safe for the purpose it has been designed for

Yours Truly,

Naveen Jaitly

(For Jaitly Associates)

MCD REG. No: SE/0416

ASSOC

New Delhi

Willing Eng

# Certificate from Electrical Inspector

#### GOVERNMENT OF NATIONAL CAPITAL TERRITORY OF DELHI LABOUR DEPARTMENT OFFICE OF THE ELECTRICAL INSPECTOR 5. SHAM NATH MARG, DELHI-110054

No.ED5 (143 )/2019/ 10 2 8 To. Dated:- 10 01 2020

M/s Select Infrastructure Pvt. Ltd., Select City Walk, A-3, District Centre, Saket, New Delhi – 110017,

Sub:- Periodical inspection of electrical installation of S/Stn. comprising of four nos. of dry type transformers of capacity 2000 KVA each, 33 KV five panel board (having SF6 Breakers) and EHV (33 KV) XLPE Cables installed in the premises of M/s Select Infrastructure Pvt. Ltd., Select City Walk, A-3, District Centre, Saket, New Delhi

With reference to your letter no. SIPL/Engg/19-20/039 dated 13/11/2019, the inspection of electrical installation of S/Stn. comprising of four nos. of dry type transformers of capacity 2000 KVA each, 33 KV five panel board (having SF6 Breakers) and EHV (33 KV) XLPE Cables installed in the premises of M/s Select Infrastructure Pvt. Ltd., Select City Walk, A-3, District Centre, Saket, New Delhi was carried out by the undersigned alongwith Sh. Daya Ram, Electrical Overseer of this Inspectorate on 06/01/2020. It is to inform you that at the time of inspection, the said installation has been found in accordance with the provisions of the Central Electricity Authority (Measures relating to Safety and Electric Supply) Regulations, 2010.

There is no objection, so far as this office is concerned, if the use of the said installation is continued subject to consistent compliance of the regulations. The said installation shall be due for periodical inspection under Regulation 30 of the said regulations within interval not exceeding five years from the date of this inspection.

No change, addition, alteration, replacement or shifting etc. in the said installation is permitted under the above regulations without prior permission of Electrical Inspector. In the event of any violation this permission shall deemed to be cancelled.

#### DETAILS OF THE INSTALLATION:-

(a) Transformer (Dry Type): 04 Nos.

Capacity : 2000 KVA each Voltage Ratio : 33/0.433 KV each

Make : Kirloskar Power Equipments each

St. nos. : 07COG005/04 (Tr. no. 1), 07COG005/03 (Tr. no. 2)

07COG005/01 (Tr. no. 3), 07COG005/02 (Tr. no. 4)

#### (b) EHV (33 KV) five Panel Board (with 5 nos.of SF6 breakers) :-

Rated Current : 1250 Amp each Rated Voltage : 33 KV each

Rated Voltage : 33 KV each Make : ABB each

Sr.No. S22963 (I/C), S22960 (O/G-1),

S22961 (O/G-2), S22958 (O/G-3), S22959 (O/G-4)

#### (c) EHV (33 KV) XLPE Cables of size 3x300 Sq.mm each :- 5 nos.

(i) Length: 53 Mtrs.

Route: From BSES Metering Cubicle to breaker S.No. S22963

(ii) Length: 36 Mtrs.

Route: From breaker S. No. S22960 to transformer S. No. 07COG005/04

(iii) Length: 30 Mtrs.

Route: From breaker S.No. S22961 to transformer S. No. 07COG005/03

(iv) Length: 24 Mtrs.
Route: From breaker S.No. S22958 to transformer S. No. 07COG005/01

(v) Length: 18 Mtrs.Route: From breaker S.No. S22959 to transformer S. No. 07COG005/02

(Mukesh Kumar Sharma) Electrical Inspector

#### GOVERNMENT OF NATIONAL CAPITAL TERRITORY OF DELHI LABOUR DEPARTMENT OFFICE OF THE ELECTRICAL INSPECTOR 5, SHAM NATH MARG, DELHI-110054

No.ED9 (30 )/2019/ 1627

Dated - 10 01 2020

To.

M/s Select Infrastructure Pvt. Ltd., Select City Walk, A-3, District Centre, Saket, New Delhi – 110017.

Sub:- Periodical inspection of electrical installation of three nos. DG sets of capacity 2000 KVA each and two nos. DG sets of capacity 1010 KVA each installed in the premises of M/s Select Infrastructure Pvt. Ltd., Select City Walk, A-3, District Centre, Saket. New Delhi

With reference to your letter no. SIPL/Engg/19-20/040 dated 13/11/2019, the inspection of electrical installation of three nos. DG sets of capacity 2000 KVA each and two nos. DG sets of capacity 1010 KVA each installed in the premises of Select Infrastructure Pvt. Ltd., Select City Walk, A-3, District Centre, Saket, New Delhi was carried out by the undersigned alongwith Sh. Daya Ram, Electrical Overseer of this Inspectorate on 06/01/2020. It is to inform you that at the time of inspection, the said installation has been found in accordance with the provisions of the Central Electricity Authority (Measures relating to Safety and Electric Supply) Regulations, 2010.

There is no objection, so far as this office is concerned, if the use of the said installation is continued subject to consistent compliance of the regulations. The said installation shall be due for periodical inspection under Regulation 30 of the said regulations within interval not exceeding five years from the date of this inspection.

No change, addition, alteration, replacement or shifting etc. in the said installation is permitted under the above regulations without prior permission of Electrical Inspector. In the event of any violation this permission shall deemed to be cancelled.

#### Details of Diesel Generating sets -.

ALTERNATOR

DG sets of capacity -2000 KVA each- 3 nos.

- 2000 KVA each Capacity - 1500 each Volts - 415 Volts each RPM Make - Stamford each - Cummins each Make Sr. nos. - 0198502/001 - 33161054 Sr. nos. 0210487/003 33163864 0194572/001 33161107

P.T.O

ENGINE-

2. DG set of capacity -1010 KVA - 2 nos.

#### ALTERNATOR

#### ENGINE-

Capacity - 1010 KVA each
Volts - 415 Volts each
Make - Stamford each
Sr. nos - 06042620
06042463

RPM - 1500 each
Make - Cummins each
Sr. nos. - 25311742
Sr. nos. - 25311741

(Mukesh Kumar Sharma) Electrical Inspector.

# **Electricity Bills**





#### **BSES Rajdhani Power Limited**

Vaccine + Mask + Washing hands + Social Distancing = Victory over Covid

Due Date(देय तिथि):

28-06-2023

#### **EBILL Customer**

Billing Address

Mobile / Tel. No.

District / Division

Walking Sequence

Email ID

Bill Month

Bill Date

#### Bill of Supply for Electricity

: M/s. SELECT INFRASTRUCTURE PVT LTD Sanctioned Load : 6604.00 (kVA)

Contract Demand : 5000.00 (kVA) SELECT CITY WALK PLOT NO-A-3 DISTRICT MDI : 3600.00 (kVA)

**NEW DELHI 110017** Power Factor : 0.992 Supply Address: SELECT CITY WALK PLOT NO-A-3 DISTRICT Pole No. : NA

> Meter Reading Status : DL Cycle No.

**Tariff Category** : Non-Domestic [ HT ]

CA No. : 100014206 **Energisation Date** : 11-06-2009 Meter Type : 3PSK Supply Type : HT(33KV) Bill No. : 100098357314 Bill Basis

: Actual O.D. No. : R/23/10366685571

**CCTV Tagged** : No Street Light Tagged : No Wi Fi Tagged : No

Energy Charge, Surcharge on Energy Charge, PPAC amount & OD Surcharge/Rebate amount = "H

विद्युत शुल्क, विद्युत शुल्क के अधिमार |पीएसी राशि एवम् टीओडी अधिमार/

**छूट पर, 5% विद्युत कर)** 

1081571.71

#### Customer Care Centre No.(ग्राहक सेवा केन्द्र का नंबर) 19123 (24x7 Toll Free)

Meter No.	Unit	Billed Consumption		Billed Consumption (	Previous)	Multiplication Factor	Current Consum	ption(वर्तमान खपत)
(मीटर सं.)	(यूनिट)	Date of Meter Reading (मीटर रीडिंग की तिथि)	Reading (रीडिंग)	Date of Meter Reading (मीटर रीडिंग की तिथि)	Reading (रीडिंग)	(गुणांक)	Days (दिन)	Unit (यूनिट)
			Meter	Details in Annexure				

Billing Details (बिल का विवरण)

: 9654339936

: Saket

: JUN-23

: 13-06-2023

: sushil@selectcitywalk.com

: MH1KC0304A0AA

Current Period Charges (वर्तमान अविध का शुल्क) (12-05-2023 to 11-06-2023 )

ı	T: f D (TOD) Ob	Curchama @ 89/	Electricity Toy @ 5% on	Total Amount
	Adopt e-bill, Save trees	, Frovide eman det	ans to us through we	osite/can/eman.

Fixed Charge="A"	Consumption Measured During	Energy Units Consumed /		se Energy Charge आधारित विद्युत शुल्क)	Adjusti	Power Purchase ment Charge वेद्युत क्रय समंजन शुल्क)		Day (TOD) Charge ॉफ डे (टीओडी) शुल्क	on (Energy Fixed Char	ge @ 8% y Charge + ge - Rebate)	L
₹ (स्थायी शुल्क)	(खपत अवधि माप)	Billed (खपत /बिल में शामिल विद्युत यूनिट)	Units Rate ₹ (यूनिट दर)	Amount = "B" ₹ (राशि)	PPAC % on B (B पर पीपीएसी प्रतिशत)	PPAC Amount = "C" ₹ (पीपीएसी राशि)	TOD % on "B" (B पर टीओडी प्रतिशत)	TOD Surcharge/ Rebate Amount = "D" ₹ टीओडी अधिमार / छूट राशि	;	'E" ₹ + स्थायी शुल्क 8% अविमार)	(हिं पी
1264784.94	NORMAL(S)	1186800.00	8.50	10087800.00	20.692	087165.82			14458	398.58	L
1.02 Mth(s)	OFFPEAK(S)	236400.00	8.50	2009400.00	20.69	332595.89(	20.00)	(401880.00)		harge @ 7% on irges + Fixed	Γ
PPAC on Fixed	PEAK(S)	570000.00	8.50	4845000.00	20.69	202916.60	20.00	969000.00	Charge - R	ebate) = "F"	
Charge = "G" ₹									12651	161.25	
261684.01									TCS Amo	ount ₹ "I"	
CCTV Units									Base Amt.	Surcharge	
0.00											1
Street Light Units									Other Cha	arges "J" *	1
											1
Wi-Fi Units									CCTV Bil	II Amount	
	Total Units =	1993200	Total (	<b>B)=</b> 16942200.00	Total (C	)=3622678.	3 <b>ĭ</b> lotal (□	)= 567120.00	0.	00	1
Doot D.	aa / Dafee	d / C	الما الما	. /	,	ء بھے					-



(K = A+B+C+D+E

(कुल राशि)

26451098.80

Past Dues / Refunds / Subsidy (पिछला बकाया / वापसी / सिंभाई) Consumer registered under GST may submit it's GSTIN at concerned division

Provisional Bill	Refunds/(वापसी)	Arr	ears (बकाया)	Late Payment Surcharge (LPSC)	Total Charges Payable	Rebate / Subsidy*	Net Amount Pavable
Refund Unit	Refund Amount	Amount (राशि)	Period to which it relates (जिस अवधि से संबद्ध है)	(देरी से भुगतान पर अधिभार)	rayable (कुल देय शुल्क)	(छूट / सब्सिडी)	(कुल देय राशि)
0		21965.86	Since MAR-23	244.01	26473308.67	(845279.93)/	25628028.74

Amount not immedi (राशि जो तुरंत देय	ately payable, if any. नहीं है, यदि हो तो)	BG Security Deposit	₹
₹		BG Expiry Date	
Service line cum Development Cha (भुगतान किया गया सर्विसलाईन एवं डेव्लपमेंत	arges paid इ. शुल्क) ₹ 0.00	Cash Security Deposit	₹9510000.00
Interest accrued for FY 202	2-23, already adjusted	in bill No.	₹ (665700.00)
100098199958 (generated fo	r the period 12-03-2023 to_	11-04-2023	, , , , ,
Interest for FY 2023-24	will be adjusted in your first	t hill to be generated in FY	2024-25

**Bill Amount Payable** (बिल देय राशि)

25628030.00

**Due Date of Payment** (भुगतान देय तिथि) 28-06-2023

If payment is made after the due date, LPSC for the delay, shall be charged in the next bill. (नियत तिथि के बाद भुगतान करने पर इस विलंब हेतु अगले बिल में एलपीएससी जोड़ दिया जाएगा.)

Last payment ₹ 22031466.00 \_\_received on 17-05-2023 . Payment accounted upto 10-06-2023 . The connection shall be liable for disconnection on non-payment of all dues (including arrears of previous bill(s) by due date, after notice as per Section 56(1) of the Electricity Act, 2003. Charges for reconnection - Single phase ₹ 200, Three phase ₹ 500. "LET'S MOVE TO ELECTRIC VEHICLES FOR BETTER TOMORROW (अच्छे भविष्य के लिए विद्युत वाहन की तरफ बदलाव करें।"

#### IMPORTANT MESSAGE (महत्वपूर्ण सूचना)

Power Purchase Adjustment Charge (PPAC) @ 20.69% been levied on energy & fixed charge w.e.f 10.06.2022. CCTV Bill amount include Energy,RA,PPAC,PTC and Electricity Tax on CCTV consumption. In case any variation in SLD charges noted, consumer may visit divisional office for requisite correction. Pension Surcharge @ 7.00% has been levied on energy & fixed charge w.e.f. 01.10.2021. The amount of Security Deposit against your connection is mentioned herewith under the heading "Security Deposit with DISCOM". Please check this amount and report any discrepancy by furnishing documentary proof in that regard available with you, at the customer care centre of respective division office. Anyone treating Electricity Bill as conclusive proof of Residence is advised to verify the particulars. Switch off lights and appliances from mains when not in use. This will conserve energy and reduce your electricity bill.ELCB is a safeguard against faulty internal wiring and prevents shock, fire and el

(This bill is computer generated, hence does not require any signature.)



Powered by



#### BSES Rajdhani Power Limited

Payment slip

ELECTRICITY BILL

- Make your digital payment to BRPL CA No. 100014206
- Cheque should not be post dated.
- Write your telephone number on backside of the cheque

· Cheque should be account payee and payable at Delhi.

• Do not staple. only clip the cheque to payment slip.

#### Tariff structure

#### The revised tariff schedule is effective from 1st October 2021

0.1	B	Fixed/Demar	nd Charge		Ene	ergy Ch	arge		Categories	Description	Fixed/Demand	Energy Charge	Т	emporary	
Categories	Description	Load(kW)	(₹/month)	0 - 200 Units	201-400 Units	401-800 Units		Above 1200 Units	"		Charge		Categories	Fixed Charge	Energy Charge
Domestic	Individual connections:	Upto 2kW	20/kW/mth	Units	Units	Units	Units	1200 Units	Agriculture	Agriculture	125/kW/mth	₹1.50/kWh	Domestic	Same as	Same as
	Domestic Light / Mixed Domestic	>2kW to 5kW	50/kW/mth	æ o oo	34.F0	æ 0 F0	æ 7 00	<b>=</b> 0.00	Mushroom	Mushroom Cultivation upto 100 kW	200/kW/mth	₹ 3.50/kWh	including	relevant	relevant
	Power, Farm House upto 21kW	>5kW to 15kW >15kW to 25kW	100/kW/mth 200/kW/mth		<b>₹4.50</b>	K 6.50	₹ 7.00	₹ 8.00	Public Utility	Delhi Jal Board, DMRC, Public Lighting etc.	250/kVA/mth	₹ 6.25/kVAh	GHS	category	category
		>25kW	250/kW/mth						Delhi Int	ternational Airport Limited (DIAL)	250/kVA/mth	₹7.75/kVAh	Threshers during the	MCD E.Tax	Flat Rate -
	Single point supply at 11kV for GHS - Domestic Lighting / Fan and Power	150/kW	/mth		₹	4.50/k	Wh		Adv	vertisements and Hoardings	250/kVA/mth	₹8.50/kVAh	threshing season	of ₹ 270 / conn/mth	₹ 5400/mth
Non-Domestic	Shopkeepers	Upto 3kVA	250 kVA/mth		₹	6.00/k\	VAh		Chargi	ng Stations for E-Rickshaw/	LT	₹4.50/kWh	All other	Same as	1.30 times
HOH-DOMESTIC	Other Non-Domestic	>3kVA				8.50/k\				cle on Single Point Delivery	UT	₹ 4.00/L\/AL	including construction	relevant	of relevant category
Industrial	Industrial	250/kVA	/mth		₹	7.75/k\	VAh			olo oli oliigio i olii olii olii oli	HT	₹ 4.00/kVAh	COLISTIACION	category	of tariff

Schedule of Time of Day (TOD) Tariff

Month	Peak hours	Surcharge on Energy Charges	Off-Peak hours	Rebate on Energy Charges
May-September	1400-1700 hrs and 2200-0100 hrs	20% (*waived for Sep 2020)	0400-1000 hrs	20%
For other than peak & off-peak hours	normal energy charges are applicab	le. Mandatory for >10kW / 11kVA other	er than Domestic. Optional for 3 Pha	se Domestic Consumers.

#### Consumption History (खपत का विवरण) :

Per	Period		Units (kwh/kvah)	Total Bill Payable	Bill Basis
From	То	No. of Days	Olitis (KWII/KVIII)	Total Bill I ayabic	Dili Basis
12-04-2023	11-05-2023	30	1735200	22053520.00	Actual
12-03-2023	11-04-2023	31	1568400	7442490.00	Actual
10-02-2023	11-03-2023	30	1398000	17973360.00	Actual
12-01-2023	09-02-2023	29	1087200	14264770.00	Actual
09-12-2022	11-01-2023	34	1280400	16666670.00	Actual
12-11-2022	08-12-2022	27	1189200	15327800.00	Actual

#### Paying your electricity bill (Bill payment information)

- yment Options

  You can pay your bill by cash / cheque /DD /Pay Order up to Rs 4000/- and for amount more than Rs 4000/- by cheque /DD/Pay Order.

  According to DERC's recent tariff order, it is mandatory for all consumers (except Domestic, Agriculture & Mushroom Cultivation) to pay their monthly electricity bills exceeding Rs 20,000/- through digital modes we.f (20ctbor 1, 2021\*

  Drop your cheque in our drop boxes at various RWA offices and at BRPL Counters. The list of drop boxes is available on the website.

  Bill payment counters are open from 0900 hrs, to 1500 hrs, from Monday to Saturday.

  Bill payment upto Rs 50,000/- can be paid in cash at Bank branches of PNB and Bank of Baroda.

- Points to remember while paying your bill

- Please pay your electricity bill inonly on obtaining computer generated bill.

  Do not make payment to unauthorized agencies / touts.

  In case your cheque is returned unpaid / dishonored by bank, cheque return charges (presently Rs. 200 + GST, as applicable) will be imposed and action will be taken under Section 138 of the Negotiable in struments Act 1881.

  Convenience lete on card swipe and online payments applicable on payment amount above Rs 5000/- is to be borne by the consumer. For charge details, kindly

#### **Customer Complaint Management:**

For any query / complaint, you may contact us using any of the following options:

- Call Center No. 19123 (24x7 Toll Free)
- Customer Care Centers (Timing Mon to Fri : 9:30 AM to 5:30 PM & Sat: 9:30 AM to 1:00 PM)
- Email brpl.customercare@relianceada.com
- · www.bsesdelhi.com

#### Escalation matrix for complaints:

- 1. In case you are not satisfied with the resolution of your query / complaint, you may contact the below listed BRPL
- Customer Care Officer (Timing 09:15 AM to 3:15 PM)
- Business Manager (between 10 AM to 11 AM on any working day)
- Circle Head (with prior appointment)

#### 2. Head-Customer Care,

BSES Raidhani Power Limited. BSES Bhawan, Nehru Place, New Delhi-110019 Email - <a href="mailto:brplhead.customercare@relianceada.com">brplhead.customercare@relianceada.com</a>

- 3. Consumer Grievance Redressal Forum (CGRF): In case you are not satisfied with the response of the above, you may approach CGRF-BRPL, Sub-station Building, Sector-V. Pushp Vihar, New Delhi-110017. Email: cgrfbrpl@gmail.com
- 4. Electricity Ombudsman: An appeal against the CGRF order may be filed with Electricity Ombudsman. B-53, Paschimi Marg, Vasant Vihar, New Delhi-110057.

किसी तरह के पूछताछ / शिकायत के लिए कृपया आप हमें निम्नवत् विकल्पों के जिरए संपर्क कर सकते है:

- कॉल सेंटर नंबर 19123 (24x7 टोल फ्री)
- करत्मर केयर सेंटर समय (सोमवार से शुक्रवार सुबह 9:30 बजे से अपराहन 530 बजे और शनिवार सुबह 9:30 से अपराहन 1:00 बजे तक)
- <u>brpl.customercare@relianceada.com</u> पर ईमेल करें
- www.bsesdelhi.com

#### शिकायतों के लिए यहां भी संपर्क करें :

- 1. अगर आप अपने पूछताछ / शिकायत के निवारण से संतुष्ट नहीं है तो आप निम्नवत बीआरपीएल अधिकारियों से संपर्क कर सकते है-
- कस्ट्रमर केयर ऑफिसर (सुबह 9:15 बजे से अपरा्हन 3:15 बजे)
- बिजनेस मैनेजर (किसी भी कार्यदिवस के दिन सुबह 10 बजे से 11 बजे तक)
- सर्किल हेड (पूर्व निश्चित समय लेकर)

#### 2. हेड कस्ट्मर केयर,

बीएसईएसं राजधानी पावर लिमिटेड, बीएसईएस भवन, नेहरु प्लेस, नई दिल्ली 110019 ईमेलः brplhead. customercare@relianceada.com

- 3. कंज्यमर ग्रिवांस रिडसल फोरम (सीजीआरएफ) : यदि आप अपनी शिकायत पर सेवा प्रदाता के जवाब से संतुष्ट नहीं है तो आप सीजीआरएफ–बीआरपीएल, सब स्टेशन बिल्डिंग, सेक्टर – V, पुष्पविहार, नई दिल्ली 110017, ईमेल cgrfbrpl@gmail.com में -अपनी शिकायत दर्ज कर सकते हैं।
- 4. इलैक्ट्रिसिटी ऑम्बड्समैन : सीजीआरएफ के आदेश के . खिलाफ अपील इलैक्टिसिटी ऑम्बडसमैन, बी—53.पश्चिमी मार्ग, वसंत विहार, नई दिल्ली—110057, में दायर कर सकते हैं।

**Disclaimer-** This electricity bill is only for electricity supply to the premises occupied by the consumer and should not be construed as having bearing on the rights or titles over the premises

अस्वीकरणः यह बिजली का बिल उपमोक्ता के निवास/कार्यालय पर बिजली की आपूर्ति के लिए हैं, और इसे उस स्थान पर उपमोक्ता के अधिकार या स्वामित्व समान न समझा जाए।

"GoNCTD vide Order No. F.6/54/Power/Subsidy/2023/725 dated 14.04.2023 has extended subsidy to Domestic Consumers for Financial Year 2023-24 of entire bill amount upto 200 Units/ month. Slab 201-400 Units/ month will get subsidy upto Rs 800/ month. No subsidy for consumption above 400 Units/ month"

दिल्ली सरकार की आदेश संख्या F.6/54/Power/Subsidy/2023/725 दिनांक 14.04.2023 के अनुसार घरेलु उपमोक्ताओं के लिए सब्सिडी वित्तीय वर्ष 2023-24 तक बढ़ा दी है, 200 यूनिट ∕ माह तक के संपूर्ण बिल राशि, रलैब 201-400 यूनिटस ∕ माह पर ₹800 सब्सिडी मिलेगी। 400 यूनिट प्रति माह से ऊपर खपत के लिए कोई सब्सिडी नहीं है।



मुफ्त कानूनी सहायता (Free Legal Aid)

मुन्न अब्दारी सेवाओं के लिए आप दिलों करना विशिष्ठ सेवाएं पाणिककरा (DSLSA) के उपकं के स्थार दिलों राज्य विशिष्ठ सेवाएं पाणिककरा, पारियाना इसक बगावानव परिस्त, इसे दिलीं हेम्पालाकः 1516 (24X7) के तमें, देनेके प्रदेशकेडिकुप्पांग, प्रतिश्राक्ष (EW washistor) — Tackbok considisa अबचा आप किसी भी जिला ब्याचानव परिस्तर में रिस्त जिला विशिष्ठ सेवाएं पाणिकरण (DLSA) के कार्यालय में भी संपर्क कर सकते हैं।

बिजली से संबंधित विवाद के निपटारे / समाधान के लिए संपर्क करें।

- . खार्ची लोक अवालत- । & II (PLA-1&II) (वीएसईएस आरपीएल, बीएसईएस वाईपीएल, और टीपीडीडीएल के लिए)माता सुंदरी लेन, आईटीओ के पास, नई दिल्ली- 110002.
- स्थायी लोक अवलत- III (PLA-III) (केंवल बीएसईएस आरपीएल) पीवीआर रोड, नी-ब्लॉक,पीवीआर के पास, विकास पुरी नई दिल्ली- 110018.

#### आपका बिल भुगतान

#### बिल भुगतान सूचना

#### भुगतान विकल्प

- आप 4000 रुपये तक के अपने बिल का भुगतान नकद/चेक/डीडी/पे ऑर्डर के माध्यम से कर सकते हैं। 4000 रुपये से अधिक की रकम का भुगतान चेक/डीडी/ पे ऑर्डर के माध्यम से कर सकते हैं।
- माध्यम सं कर सकते हैं। डीईआरसी के हालिया टैरिफ ऑर्डर के मुताबिक, सभी उपमोक्ताओं (घरेलू, कृषि और मश्लाम की खेती को छोड़करें) के लिए यह आवश्यक हैं कि वे 20,000 रूपये से अधिक के बिलों का मुगतान 1 अवरृद्ध, 2021 से डिफिटल माध्यमों से करें। आरडब्लूए ऑफिसेज और विभिन्न बीआपपीएल काउंटर्स पर लगे हमारे ड्रॉप बॉक्सेज में आप अपना येक डाते। ड्रॉप बॉक्सेज की लिस्ट हमारी वेबसाइट पर उपलब्ध हैं। बिल मुगतान केंद्र सुबह 9 को से शाम 3 को तक खुले रहेंगें।

- पंजाब नेशनल बैंक और बैंक ऑफ बड़ौदा की शाखाओं में 50000 रुपये तक बिजली का भुगतान नकद में करा सकते हैं।
- बिल मुगतान करते समय ये बातें याद रखें
- कंप्यूटरीकृत बिल पाने के बाद ही अपने बिजली बिल का भुगतान करें।
- अनाधिकत एजेंसियों / दलालों को भुगतान न करें
- अनार आपना चेक बैंक द्वारा बगैर भुगतान के/ अस्वीकृत होकर वापस आ जाता है तो चेक वापसी शुक्त (मीजुदा 200 रुपये + जीएसटी, जैसा लागू हो) वसूला जाएगा और निर्माशिएबल इस्ट्मेंटस एक्ट् 1881 की घारा 138 के तहत कार्यवाही की जाएगी।
- कार्ड स्वाइप और ऑनलाइन के द्वारा 5000 रुपये से अधिक के मुगतान पर लगने वाले सुविधा सुक्क को उपमोक्ता को वहन करना होगा। सुक्क के विस्तृत ब्यौरा के लिए कृपया हमारे वेबसाइट् <u>www.bsesdelhi.com</u> पर जाएं।

#### Contact details:(संपर्क संबंधी विवरणः)

#### Nearest Payment Centre

1ST FLOOR, A-BLOCK, BSES BHAWAN NEHRU PLACE NEW DELHI 110019 (Tel No: 49209493

Business Manager: MR BHUVESH GOYAL (49209435) Commercial Officer : MR BHUPESH DHASMANA 49209485)

#### Pay your electricity bills conveniently by any of the following options:

		Payment Options	Timings		For payment of en	nergy bill	
Digital Online Payments	Bharat QR code - QR Code on Bill     BSES Mobile App / Website - UPI, IMPS	BBPS enabled Payments App (Paytm etc.) (Zero Charges)  6, Internet Banking, Credit / Debit Cards, Mobile Wallets, QR Code	24x7	Details	SBI Bank	Axis Bank	
	RTGS/NEFT/ECS  BRPL Cash Counters:     Cash-Upto Rs. 4000/-     Cheque & Demand Draft- No amount	t limit for Domestic, Agriculture & Mushroom Cultivation category		Beneficiary Name	BSES Rajdhani Power Limited	BSES Rajdhani Power Limited	
Cash Counters		umers maximum allowed is upto Rs. 20,000/	9AM - 3PM	Beneficiary	SBIBRE (Fixed) + 9 Digit Customer Account	VBRE(Fixed) + 9 digit customer account number (Variable)	
24*7 self payment Kiosk	24*7 self payment Kiosks by cards, each	n division office	24x7	A/C No.	Number (Variable)	(For eg. VBRE123456789)	
	Bank of Baroda, PNB and SBI:     Cash- Upto Rs. 50,000/- only for Dome for other category consumers maximum	estic, Agriculture & Mushroom Cultivation category consumers and		IFSC Code	SBIN0004266	UTIB0CCH274	
Bank Branches	Cheque & Demand Draft- No amount	limit for Domestic, Agriculture & Mushroom Cultivation category umers maximum allowed is upto Rs. 20,000/	Bank Timings	Bank Name	State Bank of India	Axis Bank Ltd	
	Select RWA locations	Cheque & Demand Draft- No amount limit for Domestic,				9th floor, Solaris C wing,	
Cheque Drop boxes	BRPL owned drop boxes at counters	Agriculture & Mushroom Cultivation category consumers and for other category consumers maximum allowed is upto Rs. 20,000/	9AM - 5PM	Branch	State Bank of India,	Opp L&T gate no. 6,	
Cheque by Post		nand Draft- No amount limit for Domestic, Agriculture & Mushroom ther category consumers maximum allowed is upto Rs. 20,000/	24x7	Address	CMP Centre	Sakhi Vihar Road, Powai, Mumbai-400072	



#### **Meter Details Annexure**

Name : M/s. SELECT INFRASTRUCTURE PVT LTD

: SELECT CITY WALK PLOT NO-A-3 DISTRICT CENTRE SAKET NEW DELHI 110017 Billing Address

Supply Address: SELECT CITY WALK PLOT NO-A-3 DISTRICT Mobile / Tel. No. : 9654339936

Email ID : sushil@selectcitywalk.com

District / Division : Saket

Walking Sequence : MH1KC0304A0AA

Bill Month : JUN-23 Bill Date : 13-06-2023 Sanctioned Load

: 6604.00 (kVA) Contract Demand

: 0.992

: NA

: 5000.00 (kVA) : 3600.00 (kVA)

Meter Type Supply Type Bill No.

CA No.

Energisation Date: 11-06-2009 : 3PSK : HT(33KV)

: 100014206

: 100098357314 Bill Basis : Actual

Meter Reading Status : DL Cycle No. : KC

MDI

Pole No.

Power Factor

**Tariff Category** : Non-Domestic [ HT ]

	Net Meter Consumption Details (Date Of Reading: )														
Total	Solar	For the Bil	ling Period	Cumulati	ve Genera	ation in FY	Color I	nstallation	Dotoilo	Date of Ir	stallation	Capaci	ty kWp		
Generation	on Units						Solal II	istaliation	Details						
B/F Units	E	xport Read	ling	lm	port Read	ling	Ne	t Differen	се	Mod	derated U	nits	Excess		C/F Units
(If any)	Normal	Peak	Offpeak	Normal	Peak	Offpeak	Normal	Peak	Offpeak	Normal	Peak	Offpeak	Gen Unit	by Prim	(If any)

(Consumption in the above table are in kWh/kVah, as applicable)

Meter No	Units	Billed Consumption (Current)		Billed Consumption (	Billed Consumption (Previous)			onsumption
		Date of Meter Reading(24:00Hrs)	Reading	Date of Meter Reading	Reading	Factor	Days	Units
XH413006	KWH	11-06-2023	433.67	11-05-2023	417.19	120000.00	31	1977600.00
XH413006	KW	11-06-2023	0.03			120000.00		3600.00
XH413006	KVAH	11-06-2023	436.62	11-05-2023	420.01	120000.00	31	1993200.00
XH413006	KVA	11-06-2023	0.03			120000.00		3600.00
XH413006	KVAHP	11-06-2023	122.62	11-05-2023	117.87	120000.00	31	570000.00
XH413006	KVAHO	11-06-2023	53.29	11-05-2023	51.32	120000.00	31	236400.00

# Diesel Storage License



#### भारत सरकार /Government of India

#### वाणिज्य और उद्योग मंत्रालय /Ministry of Commerce & Industry

#### पेट्रोलियम तथा विस्फोटक सुरक्षा संगठन (पैसो) /Petroleum & Explosives Safety Organisation (PESO) PESO's ONLINE LICENSING SYSTEM

इमेल /E-mail: explosives@explosives.gov.in

दूरभाष /Phone/Fax No : 0712 -2510248, Fax-2510577

#### सेवा में / To.

M/s Select Infrastructure Pvt.Ltd.,

A-3, District Centre, Saket New Delhi-110017, A-3, District Centre, Saket New Delhi-110017,

Saket,

Taluka: Saket, District: DELHI, State: Delhi PIN: 110017

विषय / Sub :

License to import and store petroleum in an installation situated at Plot No, Plot no.- A-3, Select

City Walk, District Centre, Saket, District: DELHI, State: Delhi, PIN: 999999, Licence no.

P/NC/DL/15/323(P179467) granted in Form XV of the Petroleum Rules, 2002 - Online Renewal of

Licence regarding.

महोदय / Sir(s),

Please refer to your online renewal application filed in the PESO's online Licensing System on 12/09/2020. The license No. P/NC/DL/15/323(P179467) granted under Petroleum Rules, 2002 has been renewed up to 31/12/2023 and PESO's records have been updated accordingly.

The validity of the subject license can be verified by entering Dockey through the Public Domain link available on PESO's website: http://peso.gov.in. You are advised to keep this communication attached with your subject original/latest amended license issued by this organisation.

For further renewal, please submit application online on or before the date on which the subject license expires.

This is a system generated online letter which does not require signature and reply to this letter is not warranted.

#### PESO's ONLINE LICENSING SYSTEM

[अधिक जानकारी जैसे आवेदन की स्थिति, शुल्का तथा अन्यе विवरण के लिए कृपया हमारी वेबसाइट http://peso.gov.in देखें ।] (For more information regarding status,fees and other details please visit our website http://peso.gov.in)

#### प्ररूप XV

#### (प्रथम अन्सूची का अन्च्छेद 6 देखिए)

FORM XV (see Article 6 of the First Schedule)

#### अधिष्ठापनों में पेट्रोलियम के आयात और भंडारकरण के लिए अनुज्ञप्ति LICENCE TO IMPORT AND STORE PETROLEUM IN AN INSTALLATION

अन्जप्ति सं. (Licence No.) : P/NC/DL/15/323(P179467)

फीस रूपए (Fee Rs.) 5500/- per year

M/s Select Infrastructure Pvt.Ltd., A-3, District Centre, Saket New Delhi-110017, A-3, District Centre, Saket New Delhi-110017, Saket, Taluka: Saket, District: DELHI, State: Delhi, PIN: 110017 को केवल इसमें यथा विनिर्दिष्टु वर्ग और मात्राओं में पेट्रोलियम 60.00 KL आयात करने के लिए और उसका, नीचे वर्णित और अनुमोदित नक्शा संख्या P/NC/DL/15/323(P179467) तारीख 12/09/2020 जो कि इससे उपाबद्ध हैं, में दिखाए गए स्थान पर भण्डारकरण के लिए पेट्रोलियम अधिनियम, 1934 के उपबंधों या उसके अधीन बनाए गए नियमों तथा इस अन्जप्ति की अतिरिक्त शर्तों के अधीन रहते हुए, यह अन्जप्ति अन्दत्त की जाती हैं।

Licence is hereby granted to M/s Select Infrastructure Pvt.Ltd., A-3, District Centre, Saket New Delhi-110017, A-3, District Centre, Saket New Delhi-110017, Saket, Taluka: Saket, District: DELHI, State: Delhi, PIN: 110017 valid only for the importation and storage of 60.00 KL Petroleum of the class and quantities as herein specified and storage thereof in the place described below and shown on the approved plan No P/NC/DL/15/323(P179467) dated 12/09/2020 attached hereto subject to the provisions of the Petroleum Act, 1934 and the rule made thereunder and to the further conditions of this Licence.

यह अनुज्ञप्ति 31st day of December 2023 तक प्रवृत रहेगी । The Licence shall remain in force till the 31st day of December 2023

NIL
IIIL
NIL
60.00 KL
NIL
NIL
NIL
60.00 KL

#### अन्ज्ञप्त परिसरों का विवरण और अवस्थान

#### DESCRIPTION AND LOCATION OF THE LICENSED PREMISES

अनुजप्त परिसर जिसकी विन्यास सीमाएं अन्य विशिष्टयां संलग्न अनुमोदित नक्शों में दिखाई गई हैं Plot No: Plot no.- A-3, Select City Walk, District Centre, Saket, District: DELHI, State: Delhi, PIN: 999999 स्थान पर अवस्थित है तथा उसमें निम्नलिखित Three underground tanks for storage of petroleum clas B connected together with another facilities. सिम्मिलित हैं | The licensed premises, the layout, boundaries and other particulars of which are shown in the attached approved plan are situated at Plot No: Plot no.- A-3, Select City Walk, District Centre, Saket, District: DELHI, State: Delhi, PIN: 999999 and consists of Three underground tanks for storage of petroleum clas B connected together with another facilities. together with connected facilities.

Note:-This is system generated document

does not require signature.

#### PESO Online Payment Receipt / Status

#### Details of the transaction

SUCCESS
576582
OIN576583
S1629214502040
12-09-2020 12:50:55
0119289422
Petroleum Rules
FORM-XV UG (License to import and store petroleum in
Underground tanks only)
P179467
Self Online Renewal
M/s. Select Infrastructure Pvt.Ltd.
16500.00
Sixteen Thousand Five Hundred Rupees
system generated hence No Signature is required.)

# MOU for E - waste and Hazardous Waste



#### INDIA NON JUDICIAL

#### Government of National Capital Territory of Delhi

#### e-Stamp

#### सत्यमेव जयते

Certificate No.

Certificate Issued Date

Account Reference

Unique Doc. Reference

Purchased by

Description of Document

Property Description

Consideration Price (Rs.)

First Party

Second Party

Stamp Duty Paid By

Stamp Duty Amount(Rs.)

IN-DL58400760117612P

: 29-Nov-2017 11:36 AM

: IMPACC (IV)/ dl853303/ DELHI/ DL-DLH

SUBIN-DLDL85330319377093714405P

SELECT INFRASTRUCTURE PVT LTD

Article 5 General Agreement

Not Applicable

0

(Zero)


SELECT INFRASTRUCTURE PVT LTD

Not Applicable

SELECT INFRASTRUCTURE PVT LTD

100

(One Hundred only)



.Plea AGREEMENT below this line.....

This Agreement is made at New Delhi on this day 2" January, 2018 by and between

M/s. Select Infrastructure Pvt. Ltd. (CIN: U74999DL1979PTC009494) a Company incorporated under the Companies Act, 1956 having its registered Office located at A – 3, District Centre, Saket, New Delhi – 110 017 (hereinafter called as "FIRST PARTY" which expression shall, unless repugnant to the context or meaning thereof, be deemed to mean and include its nominees and permitted assigns) represented through its authorized signatory, the party of the First Part.

For Bharet Oil & Waste Management Ltd.

Merren

Page 1

Authorised Signatory



The dutherity of this Spirity Contribute should be written in from a continuous contribution of the duthers within the forest and the contribution of the section and the contribution of the section and the section and the contribution of the section and the section of the section of the section and the section of the se

The times of thickery the legitimacy is on the laters of the fursion in

#### AND

M/s Bharat Oil and Waste Management Ltd (BOWML), (CIN:	) a Company
registered under the Companies Act 1956, having its registered office at B-5(GF), East of	f Kailash, New
Delhi – 110065 represented by its Director, as the case may be ( hereinafter called as "SEC	OND PARTY
which expression shall, unless repugnant to the context or meaning thereof, be deemed	to mean and
include its nominees and assigns), the party of the Second Party.	

WHEREAS First Party is engaged in business of mall management services and it is providing various services to a mixed-use commercial complex, known as Select CITYWALK, located at A – 3, District Centre, Saket, New Delhi – 110 017 and within Select CITYWALK premises, shopping mall, serviced apartment, multiplex and offices are operating their respective business.

AND WHEREAS the First Party desires that the Hazardous Waste being generated at Select CITYWALK, as mentioned above, to be lifted, transported, treated, stored and disposed of, by utilizing the services of SECOND PARTY, as per the Pollution Control Board Authorization, list of Hazardous Wastes and their tentative quantity is enclosed herewith marked as Annexure. Further, the SECOND PARTY's engineered common facility at Gata No. 672, Vill. Kumbi, NH-2, Ramabai Nagar, Kanpur(UP), duly authorized by the Uttar Pradesh Pollution Control Board and having another Facility at Mauza Mukimpur, Roorkee-Laksar Road, Roorkee-247664, (Uttarakhand), to treat, store and dispose of Hazardous Waste and/ or Bharat Oil Company (India) Registered (BOC) a partnership concern registered under the Partnership Act with its registered office at 169 Kailash Hills, New Delhi 110065, duly registered with Central Pollution Control Board, having its CHWTSDF at E-18, Site IV, Sahibabad Industrial Area, Ghaziabad, (UP), duly authorized by the UPPCB, under the Environment Protection Act 1986 (for short the 'Act')and the Hazardous & Other Waste (Management & Transboundary Movement ) Rules, 2016, and authorised for carrying out of the state the Hazardous Waste, generated in Delhi from Delhi Pollution Control Committee ("DPCC") and / or the E-Waste (Management) Rules 2016 (for short 'The Rules') as amended from time to time.

AND WHEREAS the SECOND PARTY has represented and assured to First Party that it's Facility in Kanpur/Roorkee/Sahibabad is duly authorized by the concerned State Pollution Control Board (including Delhi Pollution Control Committee "DPCC") and further capable of handling the Hazardous Waste generated at Select CITYWALK.

AND WHEREAS First Party has agreed to avail the services of Second Party for treating the Hazardous Wastes, in its above named facility/facilities.

Now, therefore, those present witnessed and it is hereby declared and agreed by and between the Parties as follows:-

For Bharat Oil & Waste Management Ltd.

Page 2

Authorised Signatory

Mest

- The FIRST PARTY will pay an amount of Rs. 25,000/-(Rs. Twenty Five Thousand Only) plus Applicable GST (total payable amount of Rs. 29,500/-) to SECOND PARTY towards Nonrefundable Lifetime Membership Deposit which will be applicable for lifetime from the date of signing of this Agreement and membership can be renewed per year without any extra charge.
- The scope of services to be provided by Second Party is limited to lift, transport through authorized vehicles, treat, store and dispose of Hazardous Waste of First Part as per the guidelines prescribed by Pollution Control Board or First Part can also send HW to SECOND Part's Plant directly at its own cost.
- Second Party, on receipt of written information from FIRST PARTY, will plan and schedule lifting logistics of the Hazardous Wastes from the premises of FIRST PARTY within 03 (Three) business days of receipt of such information. First Party shall ensure that Hazardous Wastes must be packed in proper & leak proof Bags or polythene Bags or containers for safe transportation.
- SECOND PARTY shall at all times comply with all the provisions of Hazardous & Other Wastes (Management & Transboundary Movement) Rules, 2016 as amended from time to time framed by MoEF/CPCB/DPCC.
- SECOND PARTY shall indemnify and keep indemnified FIRST PARTY from all losses, damages, and third party claims after taking out HW from Select CITYWALK, the premises of the First Party, in cases of non-compliance of statutory norms on the part of SECOND PARTY.
- 6. FIRST PARTY shall keep ready the Hazardous Waste as per the mandate given to SECOND PARTY for collection, as it is a common facility catering to diverse wastes. SECOND PARTY shall follow Ministry of Environment & Forest, Central Pollution Control Board and State Pollution Board guidelines, future amendments and latest disposal technologies.
- 7. FIRST PARTY shall ensure that the above Hazardous Waste must be packed in proper containers/bags so as to prevent any damage/spillage of the material, during transit to SECOND PARTY factory. Containers/Bags arranged by FIRST PARTY shall be of Metallic/PVC/Leak proof Bags and kept at the storage place under cover. Container/Bags' weight will also be added in the weight of the material.
- FIRST PARTY will provide labour and special Material Handling Equipments at its own cost to lift
  and load the containers at the FIRST PARTY premises, in the vehicles for the transportation.

For Bharat Oil & Waste Management Ltd.

Authorised Signatory

Page 3

MIL

- 9. FIRST PARTY has mandatory obligations to provide the entire process detail which leads to generation of Hazardous Waste and its tentative Quantity per month or year to SECOND PARTY for the purpose of determining the waste characteristics and to decide parameters for comprehensive analysis and process for disposal. However, it is specifically agreed between the parties that the process details provided by FIRST PARTY shall be kept confidential and Second Part shall not disclose it to any third party without the First Party's prior written consent. This clause shall survive termination for a period of 01 (One) year after the determination of this Agreement for any reason whatsoever.
- 10. FIRST PART shall provide comprehensive Laboratory Analysis Report from a CPCB approved Laboratory of each type of Hazardous Waste for Finger Print Analysis. In the event there are differences in the analysis results; FIRST PARTY may send its samples to a mutually agreed THIRD PARTY at their own cost. New Comprehensive Analysis Reports shall be provided by FIRST PARTY when there is a change in the Hazardous Waste characteristics, manufacturing process or change in the product mix etc. Reports must be provided to SECOND PARTY prior to scheduling pick-up of Hazardous Waste. Reports shall be sent via Electronic mail as well as by courier/speed post to SECOND PARTY.
- 11. The comprehensive Analysis Report shall determine the disposal Pathway based on the Waste Characteristics and as per Waste Acceptance Criteria given to the FIRST PARTY and any other condition/solution that would help in safe disposal of Hazardous Waste. Disposal Pathway is mutually agreed between FIRST PARTY and SECOND PARTY to finalize the disposal base or basic USER CHARGES. The base User Charges are defined in Annexure to this Agreement.
- 12. FIRST PARTY and the SECOND PARTY will maintain and provide details of the HW as per the provisions in various Forms prescribed in the Rules. These Forms can be provided by SECOND PARTY/ FIRST PARTY, as per the requirement at cost or be printed by FIRST PARTY as per the formats given by the SECOND PARTY.
- 13. If FIRST PARTY provides any false information/declarations or withholds information in relation to the provisions of Hazardous Waste rules and / or E-Waste rules any time during the term of this Agreement, all charges of Hazardous Waste during transportation, handling, treatment and disposal including post-disposal period shall remain vested at the responsibility of FIRST PARTY.
- 14. The charges for collection, treatment, storage, and disposal facility (hereinafter called as User Charges) will be applicable to FIRST PARTY/SECOND PARTY as per Annexure.

For Bharat Oil & Waste Management Ltd.

Authorised Signatory

Page 4

(37)

July

- 15. FIRST PARTY shall make payment for Waste management Services to SECOND PARTY and viceversa per User Charges and other terms and conditions as per payment terms outlined in Annexure.
- 16. FIRST PARTY is responsible to segregate/store/accumulate/fill/load the Hazardous Waste in the container provided by FIRST PARTY in a neat and proper manner and so also, the container area should be accessible to SECOND PARTY's vehicle, to come and lift the Waste. The Transporter/SECOND PARTY reserves the right to reject lifting of Hazardous Waste spilled over the ground and container whose exteriors are soiled by Hazardous Waste spillage due to leakage.
- 17. In case, for any reason, the SECOND PARTY's Vehicle is sent back without giving the Hazardous Waste even after being requisitioned by FIRST PARTY, FIRST PART will have to pay actual transport charges, which shall be Rs. 2,000/- per trip, to SECOND PART, for a minimum load of O1 (One) MT.
- 18. First Part shall at all times comply with all the provisions of the Acts and Rules from time to time in force and the Guidelines issued from time to time regarding handling of Waste involving the collection, storage, transportation and delivery thereof, and shall, without prejudice to the generality of the foregoing, also comply with all Environmental Protection Laws, Safety Laws and Regulations from time to time in force and the Rules, Regulations and Notifications made or issued thereunder from time to time. In the event of First Part committing any breach of the terms of this clause of Agreement, FIRST PARTY shall indemnify and keep indemnified to SECOND PARTY from and against all claims, payments, costs and actions of whatsoever nature brought against or sustained or incurred by SECOND PARTY arising from or as a result of such breach committed by FIRST PARTY in that behalf, provided these are proved.
- 19. Each PARTY shall indemnify and keep indemnified the other PARTY at all times from and against all actions, suits, proceedings, claims, third party claims, costs, payments and expenses of whatsoever nature made or suffered or incurred by the other PARTY whether by reason of or by virtue of non-performance or non-observance or non-compliance by either PARTY, of any terms and conditions of this Agreement or of the relevant Act, the Rules and the Guidelines.

#### IT IS FURTHER HEREBY AGREED BY AND BETWEEN THE PARTIES AS UNDER:

20. This Agreement is valid for a period of 05 years (from 02.01.2018 to 31.12.2022) and can be renewed thereafter on similar or revised terms and conditions as may be mutually agreed between the parties.

For Bharat Oil & Waste Management Ltd.

Western

Page 5

Authorised Signatory

grat

- 21. FIRST PARTY shall use the services of the SECOND PARTY during the period of this contract to dispose generated hazardous waste at agreed prices, while the agreement is in force. SECOND PARTY must legally and safely collect, transport, treat, dispose hazardous waste from FIRST PARTY during the agreed period per rates agreed while this Agreement is in force and payments made as per Agreement terms.
- 22. If all the terms and conditions as per the clauses of this Agreement are adhered to by FIRST PARTY, it shall be SECOND PARTY's responsibility to lift, transport, treat and dispose of the Hazardous Wastes generated by FIRST PARTY in accordance with prevailing Govt. Rules and FIRST PARTY shall not have any liability whatsoever in this regard.
- 23. The main mode of final disposal of HW shall be Incineration/Land-filling and ash would be cemented and landfilled. The modes of disposal are dependent on the Hazardous Wastes' characteristics and FIRST PARTY shall not have any liability whatsoever in this regard.
- 24. The User Charges are subject to Annual Revision on the basis of Govt. of India Wholesale Price Index [WPI], (Commodities Index-All India) and once a quarter in the event of escalation of fuel costs and on major price escalations, escalation of fuel costs viz., Power Tariff, change in Disposal Technologies/Method, Wage Hike etc., to name a few. For the purpose of escalation in fuel cost, 30% of freight rate will be considered as fuel element of the cost.
- 25. SECOND PARTY/ First Party reserves the right to cancel this Agreement if FIRST PARTY/ Second Party fails/refuses to pay the bills/dues as per the payment terms applicable to FIRST PARTY/ Second Party as mentioned herein and in Annexure. A Notice period of maximum Thirty (30) days will be allowed from the date of lifting of material. If FIRST PARTY/ Second Party fails to pay in settlement of the Invoice, it shall be liable to pay interest @ 18% per annum and this may also result in cancellation of First Party's Membership, forfeiture of deposit, and termination of this Agreement. Repeated defaults and violation of payment terms will also result in cancellation of Membership and forfeiture of Membership deposit.
- 26. Hazardous Wastes that require other alternate destruction technologies shall be handled at SECOND PARTY's facility. However, the prices for such treatment techniques shall be determined on a case-to-case basis on their characteristics.
- 27. Notwithstanding anything contained herein, neither Party hereto shall be liable for damages or have this Agreement terminated for any delay or default in the performance of such Party hereunder if such delay or default in performance derives from conditions beyond the reasonable control of such Party, including but not limited to, acts of God, fires, floods,

For Bharat Oil & Waste Management Ltd.

Western

Page 6

Authorised Signatory

91../

extreme drought, riots, work stoppages, embargoes, governmental actions or damage to the plant or facility or any cause unavoidable or beyond the control of either party including any arbitrary ruling by the Government prohibiting the handling of the Waste or continuing domestic or international problems such as wars or natural calamities.

- 28. This Agreement shall be deemed to represent the entire Agreement between the parties hereto regarding the subject matter hereof and shall supersede, cancel and replace all prior agreements or arrangements, if any, in this behalf, signed/entered into by and between the parties hereto.
- 29. This Agreement is on principal to principal basis and nothing contained herein shall be deemed to constitute a partnership, joint venture or agency by and between the parties hereto.
- This Agreement may be modified or amended only by writing, duly executed by or on behalf of the parties hereto.
- 31. Any terms and conditions of this Agreement may be waived at any time by the party that is entitled to the benefit thereof. Such waiver must be in writing and must be executed by an authorized officer of such party. A waiver on one occasion will not be deemed to be a waiver of a similar occasion or any other similar breach or non-fulfillment on a future occasion.
- 32. If any provision of this Agreement is held to be illegal, invalid or unenforceable under any present or future laws, such provisions shall be deemed terminable and the remaining parts and provisions of this Agreement shall remain in full force and effect.
- Either Party shall have the right to terminate this Agreement upon giving 30 days written notice to the other Party with a reasonable cause.
- 34. It is clearly and expressly understood by and between the parties that the activity of lifting, transportation, treatment, storage and disposal of Hazardous Wastes is an independent contract and it does not come within the purview of the FIRST PARTY's commercial complex activities. It is also clearly understood and confirmed by and between the parties that this contract is for performance of work and not for supply of Labour.
- 35. Nothing contained in these terms and conditions shall be construed as creating any relationship either direct or indirect of employer and employee between the FIRST PARTY and the persons engaged by SECOND PARTY. The FIRST PARTY shall have no liability towards such persons and such persons will not have any claim whatsoever against the FIRST PARTY for salary, wages,

For Bharat Oil & Waste Management Ltd.

weren

Authorised Signatory

grit

provident fund, gratuity, retrenchment compensation or any other compensation for accident or death or any other claim whatsoever.

- 36. Any dispute arising on any clause or clauses of this Agreement and the contents of the Annexure hereto between FIRST PARTY and SECOND PARTY shall be referred to an Arbitrator as mutually agreed between both parties. The Arbitration shall be conducted in accordance with the provisions of the Arbitration and Conciliation Act, 1996 with amendments thereof. The arbitration proceedings shall be conducted in English and shall take place at New Delhi, India. The arbitral award, including interim awards, if any, shall be final and binding upon both parties.
- Subject to the provisions of the foregoing clause, FIRST PARTY and SECOND PARTY mutually agree that the courts of Delhi alone, to the exclusion of any other, shall have the jurisdiction.

For Bharat Oli & Waste Management Ltd.

Authorised Signatory

and the same

IN WITHNESS WHEREOF, both the parties have signed this Agreement and a duplicate copy thereof at the place and the day, month and year first written hereinabove.

Select Infrastructure Pvt. Ltd.	Bharat Oil & Waste Management Ltd			
My mother 11	For Bharat Oil & Waste Management Ltd.			
Marian	Deven			
TEL 200 131	Authorised Signatory			
By its authorized Signatory	Director /Partner			
Name & Designation All MA	(Naresh Manglani)/BT Manglani			
SHASHI STAN	Anne			
Sx. V.1-	July 1			
Witnesses:	50. 1541			
1. Name & Designation)	1. Sanjiv S. Bhalings			
(Mobile:)	Sandeep			
2. Name & Designation	2. Sandeep Kumar (9717700119)			
(Mobile :)	sandeep.kumar@bharatoil.com			
GST No				
TIN No				
PAN No				
Phone No				



#### ANNEXURE

#### Waste Management & Handling Service Charge

This annexure is in conjunction with Agreement signed between FIRST PARTY (Select Infrastructure Pvt. Ltd.) and SECOND PARTY (Bharat Oil & Waste Management Limited) on 02.01.2018.

#### Disposal of Hazardous Waste: - Recycling/incineration/landfill Category – A- Recycling or refining:

S:N	Type Hazardous Waste	BOWML Rates in Rs.
	AND TRAVECOR TO REPORT OF	2000.00 per Barrel of 220 Lt.
1.	Used/ Waste Oil *	(Rupees Two Thousand only)
		120/- per barrel of 220 Liter
2.	Empty Container- 200-220 Liters	(Rupees One Hundred Twenty Only)
		Rs. 13.00 per Kg
3.	Batteries	(Rupees Thirteen per kg only)
	E-Waste- Laptop, Desktop, Monitor, UPC,	Rs. 11.00 per Kg
4.	CPU	(Rupees Eleven per kg only)
		And the state of t

- For Category A The Second Party shall pay the above said amount to the First Party within 15 days from the Invoice date. Quoted Rates are inclusive of all taxes.
- \* With container; Material should conform to specification in schedule V i.e. Without water & sludge and for fully filled drums.
- \* BOWML will pay for Min qty of 200 Liters otherwise used oil will come free of cost.
- The First Party shall not be liable to pay transportation charges for delivery of Hazardous Waste to the Second Party under Category A, except as specified in Clause 16 of the Agreement.

#### Category - B- Disposal:- Hazardous Waste

SR NO.	Type Hazardous Waste	Approx. Generation Frequency/ Annum	BOWML Rates in Rs.	
1.	Cotton Waste, plastic Waste, Oil Soaked cotton, paper, rubber waste, Hand gloves, Oily-Paint Sludge etc (Incinerable) Chemicals waste with	50kg	Rs. 25.00 per Kg (Rupees Twenty Five per kg only)	

For Bharat Oil & Waste Management Ltd. Page 10

Authorised Signatory

May

	water mix.		
2.	Air/Oil Filters (Incinerable)	5	Rs. 45.00 per Piece (Rupees Forty Five per PIECE only)
3.	CFL/Tube lights, Chokes, Capacitors, wires (E-waste & landfilable) Printers, Cartage, Mouse, Key board, CPU, Chargers,	10109	Rs.25.00 per kg (Rupees Twenty five Per kg Only)
4.	ETP Sludge (Landfilable waste)	100 Kg	Rs. 30.00 per Kg (Rupees Thirty per kg only)
5.	Discarded Containers below 200 liters capacity	awkg	Rs. 18.00 per Kg (Rupees Eighteen per kg only)
6.	Used Grease /Used Coolant	75 Kg	Rs. 14/- Kg (Rs. Fourteen Only)
7	Transport Charge		Rs. 2,000/- per trip

For Category B – the First Party shall pay to the Second Party within 15 days from the Invoice Date and all cost is inclusive of taxes.

#### Terms and conditions

- a) FIRST PARTY shall ensure that the above Hazardous Waste must be packed in proper containers/gunny bags so as to prevent any damage/spillage of the material, during transit at FIRST PARTY's commercial complex. Containers/Gunny bags arranged by FIRST PART shall be of metallic/PVC and kept at the storage place under cover. Containers' weight will also be added in the weight of total Hazardous Waste and those are not on returnable basis.
- b) FIRST PARTY, if intends to do so, however not obligatory, shall deliver their waste at our plant E-18, Sahibabad Industrial Area, Ghaziabad/Gata No.-672, village-Kumbhi NH-2, Kanpur Dehat-290101 UP at own cost. If SECOND PART lifts the material transportation cost shall be borne by FIRST PARTY as quoted above. Loading is in scope of FIRST PARTY. All documents shall provide by SECOND PARTY i.e.Form-6 for E-waste & Form- 8, 9, 10 (Hazardous Waste) & Form- 38 if required.
- c) As per Rule 8 of the Hazardous & Other Wastes (Management & Transboundary Movement) Rules, 2016 as amended FIRST PARTY (Hazardous Waste Generator) needs to send/dispose the

For Bharat Oil & Waste Management Ltd.

Page 11

Authorised Signatory

Nex

Hazardous Waste within 90 days from their Plant failing which agreement can be terminated without any notice.

- d) In accordance with the MoEF Memorandum No. 23-1/2008-HSMD dated 16th April 2009, an amount equivalent to 5% of the billed amount of landfillable hazardous waste towards maintaining of Escrow Fund with scheduled bank jointly operated by MoEF and UPPCB for postclosure monitoring of the Hazardous Waste landfill facility is additionally chargeable.
- e) For Category (A) Payment shall be made by SECOND PARTY in favour of FIRST PARTY by Cheque/DD within 15 days from the lifting/ transportation of the Hazardous Waste. (Used/ Waste Oil should meet parameters as per Schedule V (A) of H.W. (Management & Transboundary Movement) Rules 2016).
- f) For Category (B) FIRST PART shall pay to First Party within 15 days of receipt of SECOND PART's Invoice by cheque/Demand Draft. "NO CASH TRANSACTION WILL BE ENTERTAINED. However, besides cheque, we can accept payments under NEFT/ RTGS route also."
- g) <u>TAXES / LEVIES</u>:- All Government / Municipal Taxes / Duties/ Levies/ Octroi / Service Tax/ Tolls etc, as applicable from time to time, will be payable by FIRST PARTY.
- h) There shall be no goods other than mentioned in this Annexure. If FIRST PARTY sends goods which are not as agreed upon or unlawful, controlled substance or can't be disposed by SECOND PART, then the same shall be returned to FIRST PARTY. SECOND PART will not invoice the disposal charge, but full transport, handling fee will be invoiced and payable by FIRST PARTY in such case.

or Select infrastructure Pvt. Ltd.

(First Party)

For Bharat Oil & Waste Management Ltd.

For Bharat Oil & Waste Management Ltd.

(Second Ratty)sed Signatory

dos

# Annexure – 19

**ECBC** Report

## **ECBC COMPLIANCE REPORT**

SELECT CITY WALK EXPANSION, NEW DELHI

#### **ECBC COMPLIANCE REPORT**





#### Introduction

The proposed commercial project development "SELECT CITY WALK" is an expansion of existing mall by SELECT Group. This is an iconic luxurious complex having featuring restaurants and Retail for its customer. As a strong step towards the social corporate responsibility and commitment for protecting the environment, the company has taken an initiative to build this building as a "Green Building".

The objective of the Energy Analysis report is to evaluate Annual Energy usage and Energy Benefits associated with energy–efficient features. The report is prepared with the help of hourly simulation software which serves as an important tool to simulate various energy efficient measures particular to the building without being actually implementing. Energy efficiency measures in envelope, lighting and HVAC can be analyzed as well as thermal comfort of the occupants can be enhanced

#### **ECBC Compliance - General**

To comply with the Code, buildings shall -:

- (a) have an Energy Performance Index Ratio (EPI Ratio) as defined in §3.1.1 that is less than or equal to 1 and
- (b) meet all mandatory requirements mentioned under §4.2, §5.2, §6.2, and §7.2.

The Energy Performance Index (EPI) of a building is its annual energy consumption in kilowatt-hours per square meter of the building. While calculating the EPI of a building, the area of unconditioned basements shall not be included. EPI can be determined by

EPI = Annual energy consumption in kWh /Total Built Up Area (excluding Basement)

The EPI Ratio of a building is the ratio of the EPI of the Proposed Building to the EPI of the Standard Building:

EPI ratio = EPI of Proposed Building / EPI of Standard Building

Where, Proposed Building is consistent with the actual design of the building, and complies with all the mandatory requirements of ECBC.

Standard Building is a standardized building that has the same building floor area, gross wall area and gross roof area as the Proposed Building, complies with the mandatory requirements §4.2, §5.2, §6.2, and §7.2, and minimally complies with prescriptive requirements of §4.3, §5.3, and §6.3 for ECBC Buildings.

To comply with the Code, EPI shall be calculated based on one of the following:

- (a) Prescriptive Method including Building Envelope Trade-off Method (see §3.2.2)
- (b) Whole Building Performance Method (see §3.2.3)

ECBC Buildings that demonstrate compliance through Prescriptive Method (§3.2.2) shall be deemed to have an EPI equal to the Standard Building EPI, and therefore an EPI Ratio of 1. ECBC+ Buildings

and Super ECBC Buildings that demonstrate compliance through Prescriptive Method shall be deemed to have an EPI Ratio equal to the EPI Ratios listed in §9.5 under the applicable building type and climate zone.

#### **Whole Building Energy Performance Analysis**

A building complies with the Code using the Whole Building Performance (WBP) Method when the estimated annual energy use of the Proposed Design is less than that of the Standard Design, even though it may not comply with the specific provisions of the prescriptive requirements in §4 trough §7. The mandatory requirements of §4 through §7 (§4.2, §5.2, §6.2, and §7.2) shall be met when using the WBP Method.

SELECT CITY WALK EXPANSION project has been modeled using the e-QUEST energy simulation software which is able to model energy flows on hourly basis for the entire year. This simulation tool has the capability to model hourly variations, lighting, HVAC equipment, daylight control and thermal zones. e-QUEST uses the DOE 2.2 simulation engine. The SLD has been created so that the single line rests on the interior side of the external walls and in the middle of the interior walls. For representing the weather conditions, project has used the ISHRAE weather file database to represent the external weather conditions. Provided below the chart indicating the steps flow of 'Whole Building Energy Performance Process',


#### **ECBC Compliance – Proposed**

Project has proposed the following energy conservation or efficiency measures in compliance with ECBC requirement,


- 1. HVAC system design shall be planned with energy conservation features to reduce energy consumption and operating cost.
- 2. High efficient existing water cooled centrifugal chillers shall be used considering IPLV not to exceed 0.55 IKW/TR as per AHRI 550-590.
- 3. High efficient Water-cooled Screw chillers shall be used considering IPLV of 0.6 IKW/TR as per AHRI 550-590.
- 4. Chillers shall be used with ozone friendly HFC refrigerant
- 5. VFDs shall be used for secondary pumps, AHUs, bigger size ventilation fans and cooling towers.
- 6. Pressure independent control valve PICV/2-way valve shall be used in chilled water circuit
- 7. AHUs shall be selected area wise, so that some can be switched off during no occupancy periods and some can be used with lower speed during low occupancy period
- 8. USE of LED Luminaires.
- 9. Lighting controls to be done by Lux level sensors, Presence and occupancy detectors to minimise the energy requirement during low occupancy times in rest rooms.
- 10. Optimally sized water supply distribution piping.
- 11. Only common area lighting is under developer scope and thus the installation and controls will be provided accordingly.
- 12. Basement lighting is controlled by alternate circuit switch for reducing energy consumption during peak hours, by switching off the alternate lighting fixtures.

- 13. LED lighting for external areas and timer controlled feeder pillars are considered.
- 14. Voltage drop for feeders shall not exceed 2% at design load and voltage drop for branch circuit shall not exceed 3% at design load.
- 15. All 3 phases shall maintain 0.97 power factor at the point of connection.
- 16. EFF2 class energy efficient motors are considered for the plumbing system.
- 17. The power cabling shall be sized so that the distribution losses do not exceed 3% of the total power usage in Buildings.
- 18. Roof top SOLAR PV will be proposed to equivalent to 1% of total peak demand or connected load of the building. As per new expansion chart, the additional electrical load (KW) of new built up area will be 860 KW. Hence 10 KW of SOLAR PV will be installed on site

#### **Energy Model: 3 D Representation**

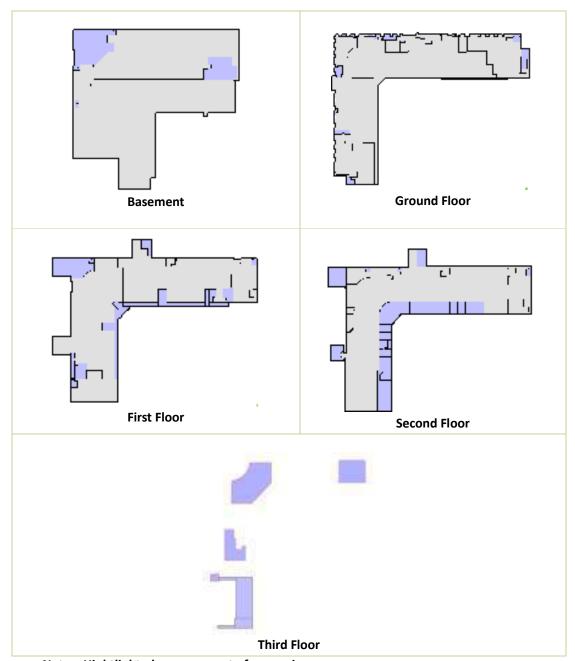


Note – Hightlighted area are part of expansion

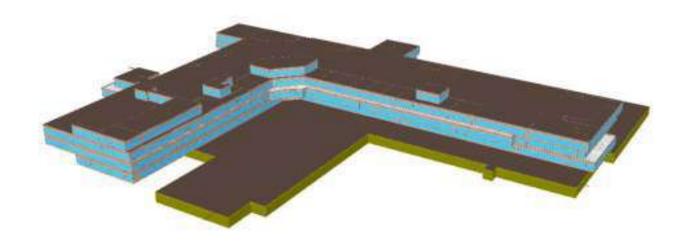

**3D View** 

#### **WEATHER DATA:**

The weather data file for city of NewDelhi.421820 was taken from ISHRAE with the following details:

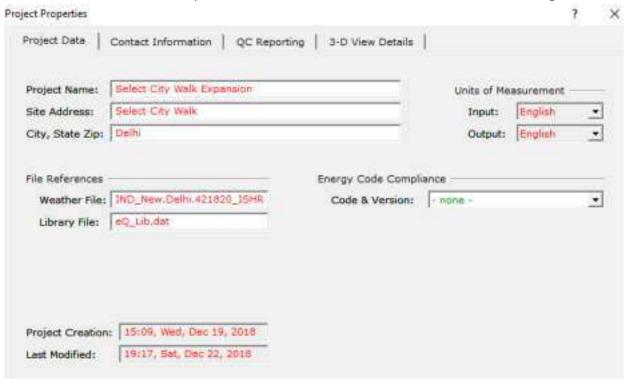

SNAP SHOT of Weather Data Selection

#### **Energy Performance Analysis**

Whole Building Performance Method has been used to show compliance of SELECT CITY WALK EXPANSION with ECBC. The retail building is considered as operating throughout the day respectively. Following table indicates the operating hours and diversity factor considered for the Retails, Restaurant, toilet and common areas.

#### PERFORMANCE RATING METHOD COMPLIANCE REPORT

Performance Rating Method Compliance Report					
Project Name	SELECT CITY WALK EXPANSION				
Project Address	NEW DELHI				
		Date: R0 25-12-2018			
Designer of Record	Godrej & Boyce	R1 02-01-2019			
		R2 08-07-2019			
City	NEW DELHI				
Weather Data: IND_NewDelhi.421820_ISHRAE.bin					
Climate Zone: Composite					

Advisory Messages					
Budget Building Proposed Case					
Number of hours heating loads not met (system/plant)	0				
Number of hours Cooling loads not met (system/plant)	0				
Number of warnings	-				

Number of errors	-					
Number of defaults overridden	-					
Description of differences between the budget building and proposed design not documented on other forms:						
Additional Building Information						
Quantity of Bldg.	1 Building Blocks					

eQUEST 3-65

**Simulation Program** 

Model Input Parameter	Model Input Parameter Baseline Design Input ECBC 2017		Proposed Case	Reference			
	Building Envelope						
Exterior Wall Construction	Exterior Wall Construction U-value as per ECBC 0.40 W/sq mtr K		U-value 0.20 W/sq mtr K	See U value calculation attached in Annexure			
Roof Construction	U-value as per ECBC - 0.33 W/sq mtr K	ECBC 2017 As Per Table 4.4	U-value 0.28 W/sq mtr K	75 MM XPS Insulation on Roof. See U value calculation attached in Annexure			
Fenestration Inputs							
WWR %	40%	ECBC 2017 As Per Table 4.4	40%	(As per Elevation)			
Solar Heat Gain Coefficient	0.27 Non-North Façade 0.50 North Façade	ECBC 2017 As Per Table 4.4	0.27	Proposed DGU			
U- Value (W/ sq. mtr K)	3	ECBC 2017 As Per Table 4.10	1.8	Proposed DGU			
		Lighting & Equipment					
Interior Lighting Power Density (W/sq. mtr)	Space by Space Area Method Retail- 18.3 W/sq mtr Restaurant- 10.9 W/sq mtr Rest rooms – 7.7 W/sq mtr	ECBC 2017 As Per Table 6.1	Space by Space Area Method Retail- 12 W/sq mtr Restaurant- 10 W/sq mtr Rest rooms – 5.5 W/sq mtr	Client will put LPD restriction value in lease agreement for all retail and restaurant tenants			
Equipment Power Density (W/sq. mtr)	Restaurant – 20 W/S0 mtr		Retail – 15 W/sq mtr Restaurant – 20 W/sq mtr	Same as in Baseline Case			

HVAC system						
Input Parameter	Reference					
Primary HVAC System Type	System Type C – Central cooling plant with variable volume AHU for each zone	ECBC 2017 As Per Table 9.2	Central cooling plant with FCU/CSU for each zone	Proposed as per DBR		
Cooling Type	Chilled Water with Water cooled Screw Chiller	ECBC 2017 As Per Table 9.2	New Water-Cooled screw chiller for 2 and 3 <sup>rd</sup> Floor Area	Proposed as per DBR		


			Existing Water cooled centrifugal chiller for Basement, Ground and 1 <sup>st</sup> Floor Area	
Chiller Size (TR)	2 Water Cooled Screw Chiller Equally Sized	Peak Cooling Load as per simulation is 463 TR Approx. ECBC 2017 Table as Per 9.3	1 Existing Water Cooled Centrifugal Chiller Loop 2 New Water-Cooled Screw Chiller equally sized	Proposed as per DBR
Chiller Water Design Supply Temp	Chilled water design supply temperature modeled at 6.7° C and return temperature at 13.3° C.	modeled at 6.7° C and ECBC 2017 As Per 9.4.2.7 temperature modeled at 7° C and P		Proposed as per DBR
AHU Fan Control	Variable Air Volume	ECBC 2017 As Per Table 9.2	Constant Volume	Proposed as per DBR
AHU Fan Load	0.0008 KW/CFM	ECBC 2017 As Per 9.4.2.3	0.0004 KW/CFM	Proposed as per DBR
And Fall Load	60% Efficiency	Table 5-12	60% Efficiency	
СОР	5.4	ECBC 2017 As Per Table 5.10	6.1 COP for existing Water Cooled Centrifugal Chiller 5.8 COP for new Water Cooled Screw Chiller	Proposed as per DBR
	Airside economizers are modeled		Dedicated Outdoor Air System has been provided to treat the fresh Air with demand control ventilation	
Economizers	air economizer capable of modulating outside-air and return-air dampers to supply 50% of the design supply air quantity as outside-air	ECBC 2017 As Per 9.4.2.5	Double Wheel Heat Recovery System has been modeled in Dedicated Outdoor Air System to supply fresh air in all the retails	Proposed as per DBR
Chilled Water Pumps	Modeled as primary-secondary with variable secondary flow. Power - 18.2 W/ kWr	ECBC 2017 As Per 9.4.2.9 and table 5.15	Modeled as primary-secondary with variable secondary flow.  Power = 18.2 W/kWr	Proposed as per DBR
	Pump Efficiency - 70%		Pump Efficiency = 70%	

Cooling Tower	open circuit axial flow tower  The fans modeled as two speeds.  Condenser water design supply temperature 29.4°C or 5.6°C approach to wet bulb temperature.  Efficiency = 0.017 kW/kWr.	ECBC 2017 As Per 9.4.2.10 and table 5.18	The fans modeled as two speed Fan Condenser water design supply temperature 25.7°C or 5.0°C approach to wet bulb temperature. Efficiency = 0.017 kW/kWr	Proposed as per DBR	
Condenser Water Pumps	Power - 17.7 W/ kWr	ECBC 2017 As Per 9.4.2.9 and	Power = 17.7 W/kWr	Proposed as per DBR.	
condenser water rumps	Pump Efficiency - 70%	table 5.15	Pump Efficiency = 70%	1 Toposed as per bbit.	

#### **Annual Energy End Use -**

kWh	Area Lights	Misc. Equip.	Space Cool	Heat Reject.	Pumps and Aux	Vent. Fans	Total
00 Deg	545128	294998	684121	73964	124982	250698	1973891
90 Deg	545128	294998	683641	74023	125138	250784	1973712
180 Deg	545128	294998	679552	73668	124826	245874	1964046
270 Deg	545128	294998	682713	74057	125207	249496	1971599
Avg. Baseline	545128	294998	682507	73928	125038	249213	1970812
<b>Proposed Case</b>	381014	294998	574442	64559	161304	216578	1692895
			Savings				14.10%

From the above table following parameters are analyzed, Proposed case energy consumption of the project is estimated to be 1692895 kWh, which is less than the base case energy consumption i.e., 1970812 kWh.

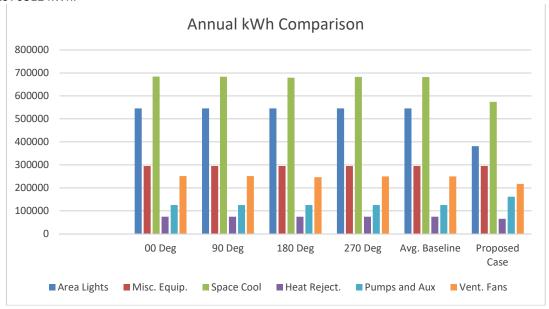


#### **EPI Calculation**


EPI Ration Calculation		
Total Built Up Area (Expansion)	7459.84	sq meter
<b>Total Proposed Building Consumption</b>	1692895	kWh/Year
<b>Total Baseline Building Consumption</b>	1970812	kWh/Year
EPI of Proposed Building	227	kWh/sq meter
EPI of Baseline Building	264	kWh/sq meter
EPI Ration of Project	0.86	Less than 1

Thereby, project is meeting the ECBC compliance by 'Whole Building Performance' approach.


#### **Building Operation Schedule -:**

Retail Occupancy Schedule Weekday and Weekend

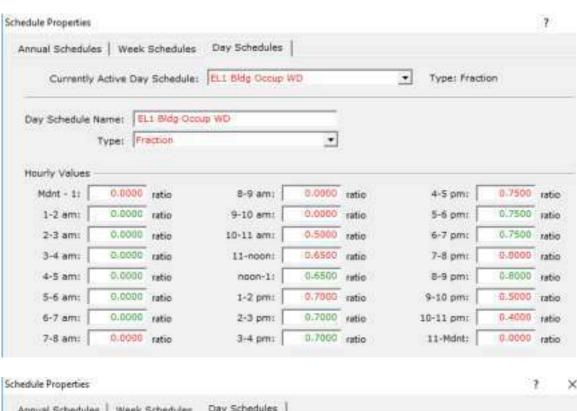


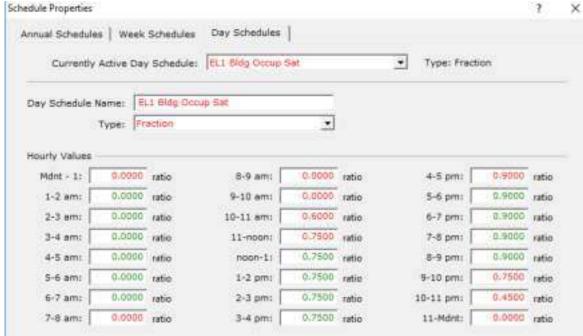


#### Retail Lighting Schedule Weekday and Weekend

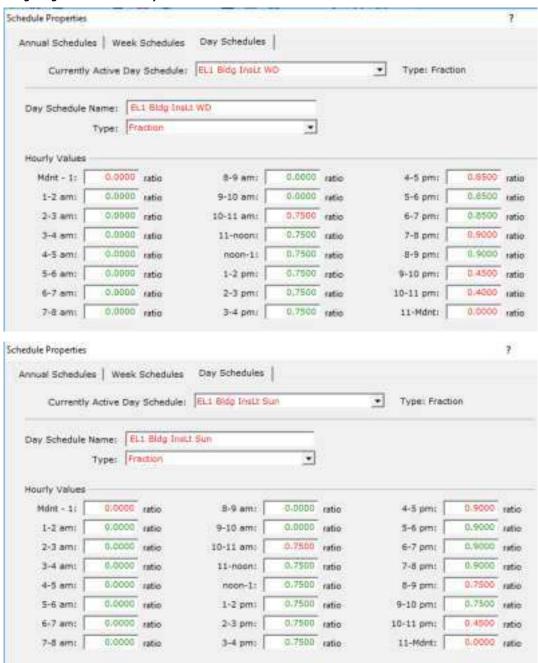


#### Retail Equipment Schedule Weekday and Weekend

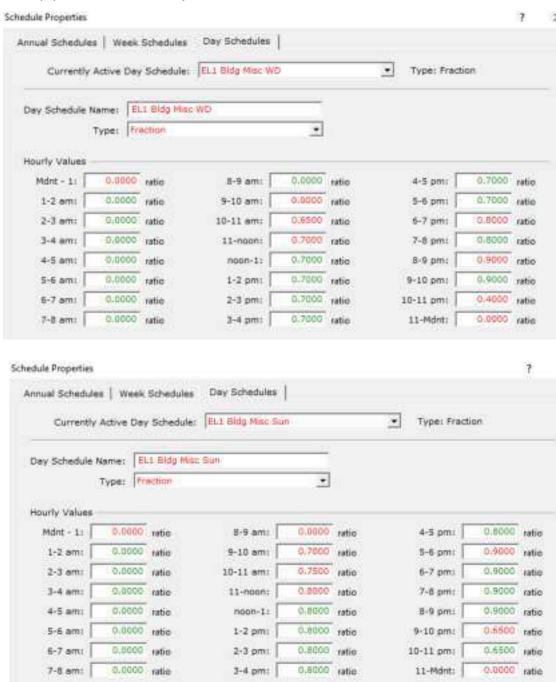

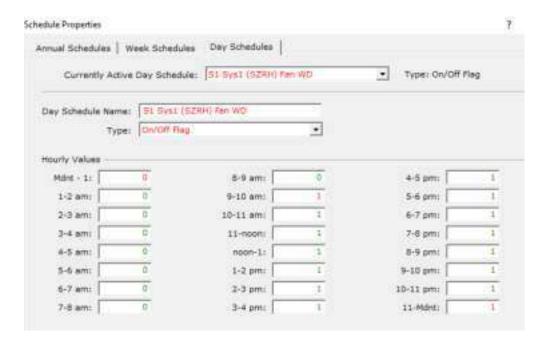

#### Retail Cooling Schedule Weekday and Weekend

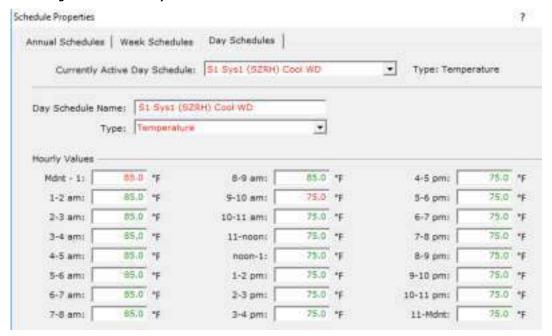

#### PROPOSED WALL AND ROOF U VALUE

#### Wall Section Details -:

External Concrete Wall U-Value Calculation					
	Conductivity	Thickness	R-Value		
	[W/m.K]	[Meter]	[sm.K/W]		
Outside Air Resistance			0.06		
Stone Cladding	0.84	0.030	0.04		
Air Gap (55 MM)			0.18		
Gypsum Board	0.098	0.030	0.31		
Insulation Mineral Wool	0.03	0.120	4.00		
Gypsum Board	0.098	0.030	0.31		
Internal Air Resistance			0.12		
	Combined R-Value		5.00	Sq.m. K/W	
	Combined U-Value		0.20	W/Sq.m. K	
			0.04	Btu/sq.	

#### Roof Section Details -:

Roof U-Value Calculation						
	Conductivity	Thickness	R-Value			
	[W/m.K]	[Meter]	[sm.K/W]			
Outside Air Resistance			0.06			
150mm Concrete Sla	1.7	0.15	0.09			
75mm PUF insulation	0.023	0.075	3.26			
Internal Air Resistance			0.12			
	Combined R-Value	9	3.53	Sq.m.K/W		
	Combined II Value	Combined II Value		W/Sq.m.K		
	Combined U-Value		0.050	Btu/sf.F		

# Annexure – 20

# Water Consumption Details

### Annexure 20

#### Average daily Water Consumption detail (October-22 to March-23)

Water meter 1 (outsourced recycled)	317 KLD
Water meter 2 (Fresh Water)	183 KLD
STP incoming water	156.5 KLD
Total Rainwater Harvesting (Source of data - IMD)	2923.37 KL

#### Breakup of utilisation of in-house produced recycled water through STP

Irrigation water	30 KLD
Cooling tower	71.5 KLD
Flushing	4.5 KLD
Backwash/Rinse	28.5 KLD
Evaporation Loses/recirculation through sludge holding tank	22 KLD

Julime

# Annexure – 21

# Adequacy Report of STP

No : Adequacy/Env/2012/[2]|8

Dated: |2 | 12 | 12 / 2012

#### ADEQUACY REPORT

ON

### SEWAGE TREATMENT PLANT

FOR

## SELECT CITY WALK, SAKET, NEW DELHI

DEVELOPERS: M/s SELECT INFRASTRUCTURE PVT LTD



DELHI TECHNOLOGICAL UNIVERSITY (FORMERLY DELHI COLLEGE OF ENGINEERING) BAWANA ROAD, DELHI - 110042

#### ADEQUACY REPORT ON SEWAGE TREATMENT PLANT FOR SELECT CITY WALK, SAKET, NEW DELHI DEVELOPERS: M/s SELECT INFRASTRUCTURE PVT LTD

#### 1.0 INTRODUCTION

SELECT CITY WALK, SAKET, New Delhi, DEVELOPERS M/s SELECT INFRASTRUCTURE PVT LTD operating the commercial complex provides various facilities for tourist, visitors and entrepreneurs. The mall also runs a Cineplex in the complex. The commercial complex provides space to retailers, manufactures and dealers to showcase and sell their product. The Mall Complex has restaurant facility which caters the needs of visitors/ guests who visit the Commercial Complex. The water requirement of the Complex is for domestic use of the Guests/ visitors, employees housed and process water for cooking and washing operation in the Complex. The Commercial Complex has the facilities of central air conditioning, so a part from this water is used for flushing and gardening.

A concerted effort has been made by the management to contain the wastewater discharge and treat the same to control the effluent quality in order to comply with the requirements of DPCC. A detailed analysis of the control system has been made in order to determine the effectiveness of the control system and the same was further checked by monitoring specific stream and analyzing the same.

The Mall Complex was visited on 06-12-2012 by a team of experts from Delhi Technological University, Delhi, to inspect the operations of the unit, and also check the sewage treatment facilities installed at the site. Detailed discussion with the plant personnel were held regarding the general concept of pollution control system, its operation and maintenance. The report is being submitted on the basis of the visit and study of the processing involved in plant, for effluent generation, its treatment system, sampling and analysis of

the treated and raw wastewater generated and previous experience on the treatment of such effluent stream.

#### 2.0 MANUFACTURING PROCESS

The Mall activities being a service-oriented unit do not have a specific manufacturing system. The major wastewater is expected to be produced from domestic use by the visitors/ guests, kitchen, laundry and the employee stationed therein.

#### 3.0 WASTEWATER QUANTITY AND CHARACTERISTICS

#### 3.1 Wastewater Quantity

Wastewater is generated mainly as domestic wastewater because of use by visitors/guests, occupants and maintenance personnel stationed in The Mall activities. Apart from this a small quantity of wastewater is expected to be generated from floor washing, laundry and kitchen as well. The total wastewater quantity from the process system has been estimated on the basis of the working of various washing systems and the amount of water used in various steps. The total water requirement for the Commercial Complex has been estimated to be about 530 KLD including the amount for domestic purpose, central cooling, flushing and hardening. The water requirement for cooling operation, flushing and gardening is met from the treated wastewater of Sewage Treatment Plant. The estimated amount of wastewater generated from the operation is about 300 Kilolitres per day. The Commercial Complex has installed effluent treatment plant with the capacity to treat about 300 KLD, which shall be recycled to the extent of 100%. The unit has

il

provided dual plumbing system and wastewater treatment facilities to the extent of tertiary treatment level so as to make it enable to use the treated wastewater for reuse. The STP operates on the basis of continuous operation. Domestic water consumption within the Mall activities is obtained from DDA Tanker.

#### 3.2 WASTEWATER CHARACTERISTICS

The wastewater discharged from the individual process steps depend on the material being used at the particular time. The major contaminants in the wastewater suspended solids, oil & grease, Biochemical Oxygen demand and COD.

#### 4.0 Wastewater Treatment

The Commercial Complex has a well designed and installed sewage treatment plant system for the combined effluent from the sources mentioned above at the premises. The sewage treatment plant has been designed and installed on the basis of physico-chemical treatment followed by secondary biological treatment. The treatment plant has been designed on the basis of continuous operation

Entire sewage generated is pumped to the inlet of bar screens and oil & Grease trap where extraneous & floating matter is removed. The treated sewage from oil & grease trap flows to the equalization tank. The equalized effluent from equalization tank is taken to Clarifier, for the removal of suspended solids. Clarified effluent is then taken to aeration tank for the biological treatment. Effluent from aeration tank goes to the secondary settling tank for the removal of suspended solids generated in the aeration tank. The treated effluent from secondary settling tank taken to the clear water tank from where it is pumped to dual media filter followed by

activated carbon filter for the removal of dissolved gases and odours. Treated effluent from activated carbon filter is passed through Ultraviolet system for disinfection. Sludge is collected from the bottom of the settling tank and is sent to the sludge holding tank and then passed through the filter press for its conditioning before its final disposal. Finally, treated effluent is reused depending upon requirements.

#### 5.0 TREATMENT PLANT PROCESS UNITS

The sewage treatment plant thus consists of the following process units:

- 1. Bar Screen
- 2. Oil & Grease trap
- 3. Equalization tank
- 4. Aeration Tank
- 5. Secondary Settling Tank
- 6. UV chamber
- 7. Sludge Holding Tank
- 8. Sand Filter
- 9. Filter Press
- 10. Activated carbon Filter

11.

Details of these process units are mentioned below:

#### 5.1.1. BAR SCREEN PIT

QUANTITY

: 1Nos.

SIZE

: 0.6m x 0.4 m

M.O.C

: 55



#### 5.1.2. OIL AND GREASE TRAP

QUANTITY : 1 Nos.

SIZE : 1.0m x 1.5m x 1.2 m

M.O.C · : RCC

#### 5.1.3. EQUALIZATION TANK

QUANTITY : 1 Nos.

SIZE : 6.1m x 1.4m x 3.0m

M.O.C. : RCC

#### 5.1.4. AERATION TANK

QUANTITY : 2 Nos.

SIZE : 2.4m x 1.5m x 2.4m

M.O.C. : MS FRP LINED

#### 5.1.5. SECONDARY SETTLING TANK

QUANTITY : 1 No.

SIZE : 1.0m x 1.0m x 0.75m

M.O.C : MS FRP LINED

#### 5.1.6. UV CHAMBER

QUANTITY : 1 No

CAPACITY : 600 1/min

M.O.C : SS

#### 5.1.7. SLUDGE HOLDING TANK

QUANTITY : 1 No SIZE : 500 I M.O.C : HDPE

#### 5.1.8. FILTER PRESS

QUANTITY : 7 No

SIZE : 0.45m x 0.45m

M.O.C : CI

rl

#### 5.1.9. SAND FILTER

QUANTITY

: 1 No

CAPACITY

: 4 m3/hr

#### 5.1.10. ACTIVATED CARBON FILTER

QUANTITY

: 1 No

CAPACITY

: 4 m3/hr

M.O.C

: MS

#### 6.0 CONCLUSIONS

The sewage treatment plant as designed and installed for treating the wastewater generated from the mall activities operations of SELECT CITY WALK, SAKET, NEW DELHI, DEVELOPERS: M/s SELECT INFRASTRUCTURE PVT LTD Is adequate for treating 300 KLD of wastewater and the treated wastewater comply with the requirements of DPCC as stipulated above. The unit has to take proper care in the operation of the system so that the treatment capacity matches with plant sewage generation.

(Principal Investigator)

Dr. S. K. Singh

Prof. & Head, Dept. of Environmental Engineering
Delhi Technological University
Govt. of NCT of Delai
(Formerly Delhi College of Engg.)
Bawana Road, Delhi-110042

#### SUMMARY OF ADEQUACY REPORT FOR SEWAGE TREATMENT PLANT OF SELECT CITY WALK, SAKET, NEW DELHI, DEVELOPERS: M/s SELECT INFRASTRUCTURE PVT LTD

Name of the Unit : SELECT CITY WALK

: SAKET, NEW DELHI Address of the Unit

DEVELOPERS: M/s SELECT INFRASTRUCTURE PVT LTD.

Activity/Process : Commercial Complex 3.

Production Capacity (max) 4.

Manufacturing Process 5.

Source of water : MCD/ Tankers 6.

Rate of Water Consumption 7.

Industrial/Catering

Domestic Others

: approx. 430 KLD

Rate of effluent discharged

Industrial Domestic

: 300 KLD

Others

Location of effluent discharge : Reuse (Flushing, Cooling & Gardening)

Source of trade effluent 10.

11. Whether effluent is treated

: Yes

Whether unit has installed ETP : Yes 12.

Details of ETP : It consists of bar screen, oil & grease 13.

> trap, equalization tank, aeration tank, secondary settling tank, UV chamber, sludge holding tank, sand filter, filter

press, activated carbon filter, etc.

Whether effluent discharge 14.

rate is monitored

: No

Whether manufacturing Process/: Yes 15. Characteristics of raw materials Have been studied thoroughly.

- Whether influent characteristics: No have been monitored
- 17. Whether any by pass : No arrangement
- Whether design aspects have : Yes been considered while evaluating performance of ETP
- If modifications have been : No suggested to upgrade ETP
- Whether existing ETP will be : Yes able to give effluent as per required parameters

(Principal Investigator)

Dr. S. K. Singh
Prof. & Head, Dept. of Environmental Engineering
Delhi Technological University
Govt. of NCT of Delhi
(Formerly Delhi College of Engg.)
Bawana Road, Delhi-110042

# Energy Conservation Measures

## **ENVIRONMENTAL MEASURES AT SELECT CITYWALK**

- Green power usage accounted for 71% of the total electrical energy consumption from February 2018 to September 2021. As a result, this contributed to saving the environment by reducing monthly emissions as below:
  - o Reduction in CO2 emission: 591.27 Tons
  - o Reduction in SO2 (Sulphur Dioxide) emission: 03.04 Tons
  - o Reduction in NO (Nitric Oxide) emission: 5.00 Tons
- Contribution to save Environment by installing roof top Solar Plant of capacity 102 KW thereby reducing emission on monthly basis:
  - o Reduction in CO2 emission: 8258.50 kg.
  - Reduction in SO2 (Sulphur Dioxide) emission: 69.83 kg.
  - Reduction in NO (Nitric Oxide) emission: 42.45 kg.
- Installed Chakr Shield (Retrofit Emission Control device) in all DG sets, leading reduction in 70% of emission. Impact created:
  - Capacity (2000 KVA x 03 Nos. & 1010 KVA x 02 Nos.), running hours considered: 30 min a day on average basis.
  - Emission Levels = </= 75 mg/Nm3 (as per CPCB Standards)</li>
     The impact values from this are as follows:-
    - PM Captured: 378 kg
    - Air Saved from getting polluted = 1260 billion litres
    - CO2 equivalents saved = 174 metric tonnes
    - Equivalent trees planted = 6,500 trees
- Environmental Management System -ISO 14001 :2015, certified Shopping Centre.
- Adoption, Development, Beautification & Maintenance of "Jamunwala Park" (Area: 1 Lac Sq.ft.).



- Adoption, Development, Beautification & Maintenance of "Gandhi Park".
- Adoption, Development, Beautification & Maintenance of "DDA Park" through SPDA.
- "Zero Discharge Policy" -All waste water recycled through Sewage Treatment Plant (300 cu mtr / day capacity) and used for Horticulture, Cooling Towers and Toilet flushing system.
- "Organic Waste Converter" Capacity 1200 kg / day Food waste recycled through Organic Waste Convertor to make organic manure. Production of organic manure approximately 2 metric ton per month utilized for horticulture and plantation.
- Segregation, Disposal and Re-cycling of wet and dry garbage in an Environment friendly manner through certified NGO by DPCC as per Municipal Solid Waste (Management & Handling) rules 2016 as amended to date.
- Disposal of Hazardous waste generated at premises through Authorized agency certified by DPCC as per hazardous waste (Management, handling and trans-boundary movement) rule 2016, as amended to date.
- Disposal of E Waste generated at premises through authorized agency certified by DPCC as per E waste (Management & Handling) Rules 2016, as amended to date.
- Rain Water Harvesting System having Seventeen pits constructed at premises, designed & duly certified by Central Ground Water Authority
   & Delhi Jal Board to recharge underground water table.
- Usage of Solar Energy:



- Solar water heating system through solar panel to tap on renewable energy converting to HOT WATER system of capacity 3000 LPD for food outlets.
- Conversion of conventional lights to LED lights for basements, staircases, common areas & Plaza area.
- Inducted "UV" treated system for water disinfection to eliminate the uses of liquid chlorine. The UV treated water used for washrooms and other domestic use.
- Sensor Operated Taps and Urinals have been installed in washrooms to reduce water consumption.
- Quarterly monitoring of Air (Ambient & Indoor), Water (Domestic & Waste Water) and Stack (DG sets & Hot Water Generator) as per Pollution Control Board Norms.
- Air conditioning Centralized Plants & stand alone Air conditioners equipped with CFC free refrigerants.
- Foam concrete light weight blocks made up of Fly ash used for partition walls.
- Using automated 3D Trasar Technology for proportionate Chemical Dozing and Automatic bleed off to conserve water.
- Reduction of Chemical Dozing in Cooling Towers by inducting ATC system for Air-conditioning Units.
- Cleaning chemicals used for Housekeeping services are Green seal 37 (GS 37) certified.



## **ENERGY MEASURES AT SELECT CITYWALK**

## **ENERGY SAVING MEASURES AT SELECT CITYWALK**

- Energy Management System -ISO 50001, certified Shopping Centre.
- Integrated Building Management System (IBMS) installed for controlling and monitoring of main Plants & Auxiliary Machineries.
- APFC equipped with passive tuned harmonic filters in capacitor bank to reduce harmonics and inductive losses to achieve P.F in the range of 0.99(1agging)- unity.
- Automatic Tube Cleaning System (ATCS) installed in Chiller plants for condenser cleaning thereby maintaining optimum approach temperature for better efficiency (1.F approach temperature is 3% of energy reduction).
- UV heat resistant transparent film applied over facade glasses to have 90% heat rejection.
- Maximum usage of Natural light by using tensile fabric toughened sandwiched facade glasses and Sky-lights to utilize sun light to optimize lux level.
- RCC slab at terraces have been provided with heat insulation membrane along with heat reflective tiles having 90% emittance and 75% reflectance.
- Centralized Chiller and Auxiliary Machineries are equipped with Variable Frequency Drive (VFD) for energy efficiency.

CITYWALK
Stay Safe

- Conversion of conventional lights to LED lights for Common area, Basements, staircases, Signages & plaza area.
- Motion sensor installed for lighting control and Escalators.
- Periodic Energy Audits conducted to upgrade the Plant & Machinery and to explore Energy saving opportunities.
- Solar water tapping for Hot water system designed at 3000 Litre per day.
- Installed 100 KW Roof Top Solar System.



# Form 4 and Form 10 DPCC





SIPL/Engg/23-24/003

To
The Member Secretary
DPCC
Dept. of Environment (Govt. of NCT of Delhi)

Sub: Submission of Form No. 04 with respect to Annual return of used lube oil for the year 2022-23.

Dear Sir,

Kindly find attached the Form No. 10 with respect to disposal of used Lube Oil. The details of the same are mentioned as below:-

- 1260 Ltrs used oil, disposed off to Bharat Oil and Waste Management Ltd., Plot no. 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 04.04.2022.
- 1260 Ltrs used oil & 55 Nos. filters (133.8 Kg including used soiled cloth) disposed off to Bharat Oil and Waste Management Ltd., Plot no. 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 20.12.2021.

Form 10 for the same have already been submitted to DPCC on regular intervals. However the copy of the same has been attached for your reference.

Thanking you,

Yours truly,

For Select Infrastructure-Pvt. Ltd

Director-Operations Project

Enclosures

1. Form - 4

Form – 10 (4th April 2022 and 20th December 2022)



SIPL/Engg/23-24/003

22<sup>nd</sup> June 2023

CONTRACTOR AND PERSONS

To
The Member Secretary
DPCC
Dept. of Environment (Govt. of NCT of Delhi)

Sub: Submission of Form No. 04 with respect to Annual return of used lube oil for the year 2022-23.

Dear Sir,

Kindly find attached the Form No. 10 with respect to disposal of used Lube Oil. The details of the same are mentioned as below:-

- 1. 1260 Ltrs used oil, disposed off to Bharat Oil and Waste Management Ltd., Plot no. 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 04.04.2022.
- 1260 Ltrs used oil & 55 Nos. filters (133.8 Kg including used soiled cloth) disposed off to Bharat Oil and Waste Management Ltd., Plot no. 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 20.12.2021.

Form 10 for the same have already been submitted to DPCC on regular intervals. However the copy of the same has been attached for your reference.

Thanking you,

Yours truly,

For Select Infrastructure Pvt. Ltd.

Shashi Sharma Director- Open

Enclosures

1. Form -4

Form – 10 (4th April 2022 and 20th December 2022)

#### FORM 4

[See rules 6(5), 13(8), 16(6) and 20 (2)]

## FORM FOR FILING ANNUAL RETURNS

To be submitted to State Pollution Control Board by 30th day of June of every year for the preceding period April to March]

- 1. Name and address of facility: GELECT INFRASTRUCTURE PYT LTD. C SELECT CITYWALK A-3 DISTRICT CENTRE SAKET, NEW DELHI - 110017
- 2. Authorisation No. and Date of issue: NI A
- 3. Name of the authorised person and full address with telephone, fax number and e-mail: \$\mu\_{\text{REPA}} \mathcal{E}\_{\text{PA}} \mathcal{E}\_{\text{PA}} Sharkis @ Scheekity walk. com
- 4. Production during the year (product wise), wherever applicable

## Part A. To be filled by hazardous waste generators

- 1. Total quantity of waste generated category wise 2520 LTRI
- 2. Quantity dispatched
  - to disposal facility USED LUBS OIL OF DE SETS CATEGORY 5.1
  - to recycler or co-processors or pre-processor = 2520 LTRS (a)
  - others (iii)
- 3. Quantity utilised in-house, if any -
- 4. Quantity in storage at the end of the year N/A

## Part B. To be filled by Treatment, storage and disposal facility operators

- 1. Total quantity received -
- 2. Quantity in stock at the beginning of the year -
- Quantity treated –
- Quantity disposed in landfills as such and after treatment —
- Quantity incinerated (if applicable) -
- 6. Quantity processed other than specified above -
- 7. Quantity in storage at the end of the year -

## Part C. To be filled by recyclers or co-processors or other users

- Quantity of waste received during the year
  - domestic sources
  - (0) imported (if applicable)
- 2. Quantity in stock at the beginning of the year -



- 3. Quantity recycled or co-processed or used -
- 4. Quantity of products dispatched (wherever applicable) -
- 5. Quantity of waste generated -
- 6. Quantity of waste disposed -
- 7. Quantity re-exported (wherever applicable)-
- 8. Quantity in storage at the end of the year -

Operator of the disposal facility

Date 72 10NE 2023

Place .. N.EH. AELHI





SIPL/Engg/22-23/002

6th April 2022

To
The Member Secretary
DPCC
Dept. of Environment (Govt. of NCT of Delhi)

DELHI POLLUTION CONTROL COMMITTEE DELINATMENT OF ENVIRONMENT GOVT. OF NOT OF DELHI 4TH FLOOR, ISBT BUILDING, KASHMERE GATE, DELHI-110000

Sub: Submission of Form No. 10 with respect to disposal of used lube oil.

Dear Sir,

Kindly find attached the Form No. 10 with respect to disposal of used Lube Oil, Oil filters and used cloth. The details of the same are mentioned as below:-

 1260 Ltrs used oil, disposed off to Bharat Oil and Waste Management Ltd., Piot no. 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 04.04.2022.

The firm to which we have disposed off the used lube oil is State Pollution Control board / Central Pollution control board authorized recyclers.

Thanking you,

Yours truly,

For Select Infrastructure Pvt. Ltd.

Director Operations & Projects

Enclosures

1. Form - 10

MANIFEST FOR HAZARI	le 19 (1)] DOUS AND (	OTHER W	AST	E	S.N		5	79	44
Occupier's Name & Mailing Address	SELTER	INTERNI	6 1 7	LINK	E	25/01/4	14	W 3	999
(including Phone No. and email)	Centi.	SPX (7.1	VIII.	201	FIRS	Niti I			W.
(including a morre visc	9,654	3345 "1	, 1	1/1	CJ	C 3.15 C	-	4	L
Sender's Authorization No.	-DI-	E-MC		-	七六	3 1	1.0	216	<u> </u>
Manifest Document No.	1241	1)	Ha	NO.	(1)	147	111		
COLOR DO COLOR DE COL	Div	BBIUS AT	4DEA						
Transporter's Name & Address (including Phone No. and email)	TAST	1			A		5869	7	1
Type of Vahicle	(Truck / Tr	anker / Sp	ecial	Vehic					1
Transporter's Registration	TOUR DESIGNATION		2766		A			100	1/3
Vehicle Registration No.		ACH				題		4	
Receiver's Name & Malling Address (Including Phone No. and email)	E-18, S Ghazia	AT OIL Co ite-IV, Sahi bad, UP-20 sales@bha	babac 11010	Tel:	istnai	Area.	24,		
(II) BHARAT OIL & WASTE MANAGEMENT LTD. Mauza Mukimpur, Roorkee-Lakshar Road. Roorkee - 247664 UK, Tel. 08874207664 e-mail:sales@bharatoil.com	Tehall / o-mail:	172, Sikand Vkbarpur, K sales@bha	ra Ro anpur ratoil.	ad, N Deha com	H-2, I	Tel:	0512	ge. 22857	296
Receiver's Authorization No.	(1) 1485/UPPCB								
(II) UEPPCB/HO/Con-B-84/2018/548 Volid upto: 31/03/2023	(HI) 1400 UPPOB	Kanpur Dehat (UF	PCBRO	унимк	ANPUR	DEHAT/20	ria Walid	upto:30	104/2
Waste Description A	1st / U	(2) 0	11	4			W.		
Total Quantity No, of Containers	1.26 m³ or MT (126-4 Nos.								
Physical Form	A CALL STREET, SALES	mi-Solid/S		100.00		200000			
Special Handling Instructions & Additional Information	Do not throw Drums from truck. In case of leakage/ seapage, use Washing soap at point of leak to stop its leakage.								
SENDER'S CERTIFICATE	I hereby declar	g that the con	lects o	(the o	onsigni	nont are	fully a	and acc	curat
	- described about	o he recover wh	Inning t	name a	and sea	categor	58C (10	CNBQ, I	TERSON N
Typed Name & Stamp Signature :	and labeled, ar	d are in all r	especis	e at bu	Jpin 320	KINGCH	O. Hill	1	200
	100	Mor	in.	D.	ay		Y	156	
		A FIGURE	4	0	4	2	0	2	T
1 10 100	X	0		2000	2000	-		1	100
Transporter Acknowledgement of Receipt of Waste	12/	Mor	ith	D.	зу	192	Y	ear.	
Typed Name & Stamp : Signatying		0	4	0	11	2	0	12	1
TWIS	18/		tal		1	118	His		
Receiver's Certificate for Receipt of Hazardous and other Waste		Mor	nth	D	ау		Y	ear	
		0	4	D	9	2	3	2	THE REAL PROPERTY.
Tuesd Nama & Stamp Signafuld		and the same	-		-	-	1	-	
Typed Name & Stamp : Signature :		SOFISSION			100	SUZE	1	No.	

[See rul	M 10  le 19 (1)  Occupier's Copy  5 7 9 4 4  OUS AND OTHER WASTE  OUS AND OTHER WASTE
Occupier's Name & Mailing Address (including Phone No. and email)	ELFCI IN FRASIKOE TOFF IN DOTHER SELECTION WITH AGS 433 99 41, ight Collection with
'Sender's Authorization No.	Cul. Prov
Manifest Document No.	0,000
(including Phone No. and email)	BOM ( )
5 Type of Vehicle	(Truck / Tanker / Special Vehicle)
> voteds Penistration	68607
	DL141c 4423
7 Vehicle Registration No.	(I) BHARAT OIL COMPANY (I) RE
8 Receiver's Name & Mailing Address (including Phone No. and email)	E-18, Site-IV, Sahibabad Industrial 74 Ghaziabad, UP-201010 Tel.: 0120-4167 e-mail:sales@bharatoil.com
(II) BHARAT OIL & WASTE MANAGEMENT LTD. Mauza Mukimpur, Roorkee-Lakshar Road, Roorkee - 247664 UK, Tel.: 08874207684 e-mail:seles@bharatoil.com	(III) EHARAT OIL & WASTE MANAGEMENT LTD. Plot # 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbsrpur, Kanpur Dehat, UP, Tel : 0512-2285296 e-mail:sales@bharatoll.com (I) 148E/LPPC8/Ghazabad/UPPC8RO/HWM/GHAZMBAD/2018 Valid upto: 63/95/26/23
= 1 to 4s Audhorization No.	(I) 1485/LPPCBIGhaziabad(LPPCBIC/ARINING GPD-CPD-CPD-CPD-CPD-CPD-CPD-CPD-CPD-CPD-C
9 Receiver's Authoritzation (II) UEPPCB/HO/Con-B-84/2018/548 Valid upto: 31/03/2023	HILIHADAUPPCBIKAnpurDehalijUPPCBROYHWBLKANPUR DEHATIDENS Vand upto:38794/2023
10 Waste Description	oned of Ore Mil
11 Total Quantity No. of Containers	1 - 2 6
12 Physical Form	(Solid/Semi-Solid/Sludge/Oily/Tarry/Slurry/Liquid)  Do not throw Drums from truck. In case of leakage/
13 Special Handling Instructions & Additional Information	seapage, use Washing soap at joint of the leakage.
The state of the s	I hereby declare that the contents of the consignment are fully and accurately described above by proper shipping name and are categorised packed, marked, described above by proper shipping name and are categorised packed, marked,
14 SENDER'S CERTIFICATE	described above by peoper shipping name and are condition for transport by made and fatheled, and are in all reapports in proper condition for transport by made
Typed Name & Stamp : Highature :	Month, Day 4 2 Year 2 2
180 mile of Morett	Month Day Year
15 Transporter Acknowledgement of Receipt of Waste	04042026
Typed Name & Stamp : Signature Cur	
16 Receiver's Certificate for Receipt of Hazardous and	Month u Day 4 2 Year 2
other Waste	
Typed Name & Stamp : Signature	





SIPL/Engg/22-23/0017

26th December 2022

To The Member Secretary DPCC

Dept. of Environment (Govt. of NCT of Delhi)

Sub: Submission of Form No. 10 with respect to disposal of used lube oil.

Dear Sir,

Kindly find attached the Form No. 10 with respect to disposal of used Lube Oil, Oil filters and used cloth. The details of the same are mentioned as below:-

 1260 Ltrs used oil & 55 Nos. filters (133.8 Kg including used soiled cloth) disposed off to Bharat Oil and Waste Management Ltd., Plot no. 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 20.12.2021.

The firm to which we have disposed off the used lube oil is State Pollution Control board / Central Pollution control board authorized recyclers.

Thanking you,

Yours truly,

For Select Infrastructure Pvt. Ltd.

Director Operations & Projects

FORM 10

Thru: - Nor 12 529 Occupier's Copy 68256 [See rule 19 (1)] MANIFEST FOR HAZARDOUS AND OTHER WASTE S.No.: Occupier's Name & Mailing Address District Center, SAKE T, N. DEHA (including Phone No. and email) DI-ILAC 4925 Sender's Authorization No. Manifest Document No. Transporter's Name & Address BOM Kanpin Dehad (including Phone No. and email) (WEST (Truck / Tanker / Special Vehicle) Type of Vehicle Transporter's Registration AC422 Vehicle Registration No. BHARAT OIL COMPANY (I) REG Receiver's Name & Mailing Address E-18, Site-IV, Sahibabad Industrial Ali (including Phone No. and email) Ghaziabad, UP-201010 Tel.: 0120-416 mall:sales@bharatoil.com BHARAT OIL & WASTE MANAGEMENT LT (II) BHARAT OIL & WASTE MANAGEMENT LTD. Plot # 672, Sikandra Road, NH-2, Kumbhi Village, Mauza Muldmpur, Roorkee-Lakshar Road, Tehsil Akbarpur, Kanpur Dehat, UP, Tel: 0512-2285296 Roorkee - 247654 UK, Tel.: 08874207664 e-mail:sales@bharatoil.com e-mall:sales@bharatoil.com (I) 1486/UPPCB/Ghzziabad/UPPCBRO)HWM/GHAZIABAD/2016 Vulki upto: 63/05/2023 Receiver's Authorization No. (HT)1403UPPCBIKaspurDehallUPPCERO)/HWM/KANPUR DEHATOUS Valid uptp:2004/2023 (H) UEPPCB/HO/Con-B-84/2018/548 Valid upto: 31/03/2023 10 Waste Description 11 Total Quantity No. of Containers Nos. (Solid/Semi-Solid/Sludge/Oily/Tarry/Slurry/Liquid) 12 Physical Form Do not throw Drums from truck. In case of leakage/ 13 Special Handling Instructions & Additional seapage, use Washing soap at point of leak to stop its Informetion leakage. hereby declare that the contents of the consignment are fully and accurately 14 SENDER'S CERTIFICATE described above by proper shipping name and are categorised packed, marked, and labeled, and are in all respects in proper condition for transport by road Signature Typed Name & S Year Month Day Month Day Year 15 Transporter Acknowledgement of Receipt of Waste Signature : Typed Name & Stamp : 16 Receiver's Certificate for Reg dous and Day Year Month other Waste

Typed Name & Stamp:

Signature

FORM 10

[See rule 19 (1)] S.No.: 68266 MANIFEST FOR HAZARDOUS AND OTHER WASTE Select CITYLY ALK ( SI OL) Occupier's Name & Mailing Address (Including Phone No. and email) District Contre, SAKE TINDELHI Sender's Authorization No. Manifest Document No. Transporter's Name & Address (including Phone No. and email) (Truck / Tanker / Special Vehicle) Type of Vehicle Transporter's Registration Vehicle Registration No. 8 Receiver's Name & Mailing Address BHARAT OIL COMPANY (I) REC E-18, Site-IV, Sahibabad Industrial Area (including Phone No, and email) Ghaziabad, UP-201010 Tel.: 0120-4167924, e-mail:sales@bharatoil.com BHARAT OIL & WASTE MANAGEMENT LTD. (III) BHARAT OIL & WASTE MANAGEMENT LTD. Mauza Mukimpur, Roorkee-Lakshar Road, Roorkee - 247664 UK, Tel.: 08874207664 Plot # 572, Sikandra Road, NH-2, Kumbhi Village Tehsil Akbarpur, Kanpur Dehat, UP, Tel : 0512-2285296 e-mail.sales@bharatoil.com e-mail:sales@bharatoil.com (I) \$485/UPPCBIGHttfiebed(UPPCBRO)HWM/GHAZIAEADGD18 Valid upto: 05/05/2023 Receiver's Authorization No. (JRF) \$403/UPPCB/KampurDehat/UPPCBROSHWMMKANPUR DEHAT/2018 Valid #100/31/04/2021 (ii) UEPPCB/HO/Con-B-84/2018/548 Valid upto: 31/03/2023 10 Waste Description 11 Total Quantity OF MT No. of Containers (Solid/Semi-Solid/Sludge/Oily/Tarry/Slurry/Liquid) 12 Physical Form Do not throw Drums from truck, in case of leakage/ 13 Special Handling Instructions & Additional seapage, use Washing soap at point of leak to stop its Information leakage. hereby declare that the contents of the consignment are fully and accountely 14 SENDER'S CERTIFICATE described above by proper shipping name and are categorised packed, marked. Typed Name & Sta Signature: and labeled, and are in all respects in proper condition for transport by road Month Day Year Year Month Day 15 Transporter Acknowledgement of Receipt of Waste Signature Typed Name & Stamp: 100 W 650 16 Receiver's Certificate for Receipt of Mazardous and Day Year Month other Waste Typed Name & Stamp: onature

Company Policy



## **POLICY**

To create a unique shopping experience through excellence & continual improvement approach thereby striving to achieve customer delight and creating a responsible socio-economic environment.

## Select CITYWALK, is committed to achieve Multi-Stakeholders Requirements

We shall strive to achieve operational excellence by framing, reviewing and continually improving on Qualitative, Energy Efficiency, Environmental, and Health & Safety performance by:

- 1. Complying and endeavor to exceed all applicable national legislations, guidelines, code of practices and all other requirements applicable to our **operations**, health and **safety, environmental** & Energy aspects in letter and in spirit.
- 2. Ensuring **best in class shopping experience**, safe and secure facilities at Select CITYWALK to meet expectations of our Multi Stakeholders.
- 3. Providing **niche platform to new and/or recognized National & International brands** to showcase their unique products & services to consumers.
- 4. To ensure **RESPECT** for dignity of human life. Further ensuring **safe and healthy environment** and achieving an **injury-free and illness-free** center by eliminating hazards and reducing OH&S risks.
- 5. Promoting waste avoidance & reduction, recycling and reusing waste and finally disposal of inevitable waste by following environment-friendly processes. Further, reducing and controlling all types of wastages/losses, pollutants, optimizing resource utilization; initiating energy and water conservation measures and increasing use of green energy thereby reducing carbon footprints.
- 6. Creating an atmosphere of IMS System awareness for **Quality, EHS** & Energy by providing adequate resources, training, educating and ensuring participation and consultation of our employees, contracted personnel and other **interested parties**.
- 7. Ensuring that **Qualitative**, EHS, and Energy criteria and objectives are framed, monitored, measured analyzed and continually improved in all our processes.
- 8. Taking measures in Energy Management System by being proactive, innovative, cost effective for procurement of energy and sourcing energy-efficient product & services.

The management and colleagues of Select CITYWALK are committed to implement the policy & maintain Policy by setting new best industry practices.

Sph short was

Yogeshwar Sharma
Executive Director & CEO
15th December 2020

# **EMP** Expenditure

### Annexure - 25

	ure - 25			T	1 1 11 1		
SL.No	Items	Expenditu	ure till date(31/3/23)		udget estimates	Basis of recurring Cost	
		Recurring in Non-recurring in Rs.		for next two years  Recurring in Non-Recurring			
		Rs.	Non-recurring in Ks.	Rs.	in Rs.		
a)	Air pollution control measures	12.942 Lacs	440.68 lacs	115.5 lac	Nill	2.5 lack Monitoring cost, 113 lacs for indoor air purification system)	
b)	Water Pollution control measures	271.312 lacs	38.144 Lacs	125.6 lacs	5 lac	Manpower / operation & maintenance cost of STP, oil & grease traps	
c)	Noise pollution control measures	5.192 Lacs	25 Lacs ( Accoustic enclousre DG set)	0.94 Lacs	Nil	Monitoring & maintenance of accoustic enclosure	
d)	Monitoring	31.418 Lacs	Nil	3.8 Lacs	Nil	Monitoring cost of air, water, noise, soil, stack & STP	
e)	Rain Water Harvesting	56.23 Lacs	73.5 Lacs	11.32 Lacs	Nill	Maintenance of harvesting pits, upkeep / maintenance of storm water channels	
f)	Green Belt	314 Lacs	253.73 Lacs	122 Lacs	5 Lacs	Upkeep & maintenance of Green Belt and addition of plantation in plaza and DDA park, development of Jamunwala park and Gandhi wala park. Saket, New Delhi	
g)	Fire Management	721.116 Lacs	991.639 Lacs	182.13 Lacs	62 lacs	Manpower , operation & maintenance and upgradtion of Fire Management System	
h) -1	Miscellaneous (a)- Audits and training -Energy , Fire & Safety, IMS (ISO-9001, ISO 14001 & ISO 45001,ISO50001 .	84.67 Lacs	8 lakh	11.858 Lacs	2 lacs	Audit Expense	
h)-2	Miscellaneous-Solar Lighting /Solar water heating system	10.04 Lacs	75.6 Lacs	2.4 Lac	Nill	Maintenance of solar lighting and solar water heating system and For adding 120 KW of solar lightining system	
h)-3	Miscellaneous - Solid Waste Management	51.4 lacs	20.99 lacs	21.88 lacs	nil	Procurement of OWC and Manpower and electricity cost (Whereas this has been operational since 2010 we are calculating cost from june-18)	

Advertisement in Newspapers for Environment Clearance

दादरा स गाव लाट का या। जल जा वा आरोप में एफ आईआर दर्ज की गई है।

## सार्वजनिक सूचना

मैसर्स सेलेक्ट इन्फ्रास्ट्रक्चर प्रा. लिमिटेड आपको यह सूचित करते है कि A-3 & P-1B जिला केंद्र, साकेत, नई दिल्ली - 110017 में "कमिशियल कॉम्प्लेक्स सेलेक्ट सिटी वॉक (शॉपिंग मॉल) का विस्तार" पर्यावरण, वन और जलवायु परिवर्तन मंत्रालय, भारत सरकार के हारा पर्यावरणीय मंजूरी Ref-21-45/2019-IA-III, दिनांक 1 नवंबर 2019 में हुआ है। मंजूरी पत्र की प्रतियां पर्यावरण, वन और जलवायु परिवर्तन मंत्रालय के पास उपलब्ध हैं, और जिसको आप वेबसाइट www.envfor.nic.in पर भी देख सकते हैं।

मैसर्स सेलेक्ट इन्फ्रास्ट्रक्बर प्रा. लिमिटेड

strengthened," he said.

村府市

मत

नस

रोपी

Besides its 105 MLAs, the BJP

Edi

and

K

Sc

## **PUBLIC NOTICE**

M/s Select Infrastructure Pvt. Ltd. is pleased to inform that the "Expansion of Commercial Complex SELECT CITYWALK (Shopping Mall)" at A-3 & P-1B District Centre, Saket, New Delhi - 110017 has been accorded with Environmental Clearance vide Ref. No. 21-45/2019-IA-III dated 1st November 2019 from Ministry of Environment, Forest and Climate Change, Govt. of India. The copies of the clearance letters are available with the Ministry of Environment, Forest and Climate Change and can also be seen on their website www.envfor.nic.in M/s Select Infrastructure Pvt. Ltd.

Himachal Pradesh State Electricity Board Ltd

Extension for Consent to Establish for Project Expansion for 1 more year (till October 2022)



## DELHI POLLUTION CONTROL COMMITTEE

(Government of N.C.T. of Delhi)

4th & 5th Floor, ISBT Building Kashmere Gate, Delhi 110006

## (Visit us at https://www.dpccocmms.nic.in) CONSENT ORDER

Certificate No.: G-20571

Name of the unit : M/s Select Infrastructure Pvt. Ltd.

Address : "COMMERCIAL COMPLEX SELECT

CITY WALK (SHOPPING MALL)" at A-3 & P1B, District Centre, Saket, New Delhi-110017, Housing Complexes, Commercial Complexes (including shopping malls), office complexes including IT and Infrastructual and Town Development Projects (Built Up Area 20000 sq. meters

and above), Delhi - 110017

Consent Order No : DPCC/CMC/2021/6590549

**Date of issue** : 28/10/2021

Product/Activity : Shopping Malls, Housing / Commercial/

Office Complexes having built up area

20,000 sqm and above

Manufacturing Activities : Expansion/Additional Construction of

"Commercial Complex Select City

Walk(Shopping Mall)".

Category Name : [RED]

**Prouct Capacity** : 0 Metric Tonnes/Day

This Consent to **Establish** is hereby granted under section 21 of the Air (Prevention & Control of Pollution) Act, 1981 and under section 25/26 of the Water (Prevention & Control of Pollution) Act, 1974 under **RED** Category. This consent is subjected to terms and conditions specified overleaf. **This is being issued with reference to your application id 6590549 valid from 09/10/2021 to 08/10/2022.** 

PANKAJ Digitally signed by PANKAJ KAPIL Date: 2021.10.28 12:04:08+05:30 Date: 2021.02 Date: 2021.02

#### Terms and Conditions

- 1. The Consented shall meet the effluent standards i.e. pH= 5.5-9, Total Suspended Solids (TSS) 30, Biochemical Oxygen Demand (3days at 27degree Cent.) 20, COD 250, Oil and Grease10, Ammonical Nitrogen (as N) 50, Nitrate Nitrogen 10, Dissolved Phosphate (as P) 5. #All effluent parameters are in mg/I expect pH value. Parameters are in mg/I expect pH value.
- 2. The Consent is activity specific and based on the information provided in the consent application along with the documents/ subsequent documents/information submitted to Delhi Pollution control Committee (DPCC). The Consentee shall apply for fresh consent in case of any change in the activity /manufacturing process.
- 3. The Consentee shall display the Name of the unit along with its Address, name of the proprietor/ Directors/ partners etc., Contact Phone No(s) and its Activities Processes/ Product etc., on a Display Board be placed/ fixed at the main gate of the unit.
- 4. The Consentee/unit shall have/take separate Electricity/ Power connection in its name and shall have/install separate meter in this regard.
- 5. The Consentee shall provide and maintain separate drainage system for collection of trade and sewage effluents. Terminal manholes shall be provided at the end of collection system and shall be connected to the conveyance system/ sewerage system of the area leading to common Effluent Treatment Plant of the Industrial Area/ Sewage Treatment Plant of the catchment area.
- 6. The Consentee shall obtain permission from Delhi Jal Board for ground water extraction, if any, as per the various orders/Notification of Govt. of NCT of Delhi.
- 7. The Consentee shall ensure proper channelization/ control system for fugitive emissions generated from the various activities/ processes of the unit and maintain good housekeeping practices so as to maintain clean & safe environment in and around the premises of the unit.
- 8. The Consentee shall comply with the noise standards laid down vide Gazette Notification of Ministry of Environment and Forest (MOEF), Government of India Dated 17.05.2002 & 12.07.2004, as amended to date, for the Diesel Generator Set(s) and shall also comply with the Emission Standards prescribed for Diesel Engines [(Engine rating more than 0.8 MW) for Power Plant, Generator Set applications and other Requirements], if any, as per the Gazette Notification of MOEF, Dated 09.07.2002, as amended to date. Stack Height (Engine rating more than 0.8 MW) commissioned after 01.07.2003 shall be maximum of following (i) Minimum 6 meter above the building where generator set is installed (ii) 30 meter (iii) 14Q°'3(Q Total so2 emission from the plant in kglhr) and for otter DG Set(s) (upto 0.8 MW) stack height shall be as per the following formula, H = h + 0.2?KVA( H-Total Height of stack in meter, h = Height of the building in meters where the Generator Set is installed, KVA -Total Generator capacity of the set in KVA).
- 9. The Consentee shall comply with the provisions of the Hazardous and Other Wastes (Management and Transboundary Movement) Rules, 2016, as amended to date, the Batteries (Management and Handling) Rules, 2001 as amended to date, Solid Waste Management Rules, 2016 and E-Waste (Management) Rules, 2016, the Manufacture, Storage and Import of Hazardous Chemicals Rules, 1989, as amended to date, wherever applicable. All such wastes generated from the unit will be managed and handled as per the provisions of the said Rules and will be disposed only through the Recycler/Reprocessor/Authorized Agencies for such wastes, authorized by MOEF/Central Pollution Control Board/State Pollution Control Board/Committee/DPCC as per details available on their websites.
- 10. The Consentee shall comply with the provisions of the Plastic Waste Management Rules, 2016, as amended to date, if applicable.
- 11. The Consentee shall comply the other prescribed standards of Effluent/Emissions as prescribed and as applicable under the provisions of the Environment (Protection) Act, 1986, as amended to date and the various Rules made there under including the Noise Pollution (Regulation and Control) Rules, 2000 as amended to date.

- 12. The Consentee shall promote the use of CFL and recovery of mercury from CFL Lamps and should create a system of replacing of old bulbs for new to enable recovery of mercury after the bulbs are fused.
- 13. The Consentee shall not carry out any activity falling under the Prohibited/ Negative list of Industries (Annexure III of MPD -2021) which are prohibited in National Capital Territory of Delhi, as per Master Plan of Delhi.
- 14. Quantity of Sewage/ trade effluent discharge from the unit shall not exceed Nillitre/Day (100 % waste water recycling and zero waste water discharge).
- 15. The Consentee shall treat the waste water generated from labour in existing STP.
- 16. The total waste water after expansion will be 245 KLD which shall be treated in to sewage treatment of total capacity 300 KLD (already installed).
- 17. The zero waste water discharge condition to be achieved with installation of onsite sewage treatment plant. Trade effluent shall confirm to the norms and standards prescribed by Delhi Pollution Control Committee. The STP should be certified by an independent expert and report in this regard should be submitted to Delhi Pollution Control Committee before the project is commissioned for operation. Necessary measures should be made to mitigate the dour problem from STP.
- 18. The treated wastewater shall be recycled and reused for Horticulture/ landscape/cooling/flushing purposes to reduce the demand of fresh water as committed.
- 19. The project proponent shall provide electromagnetic flow meter at the inlet and outlet of the water supply, Inlet and outlet of the STP and any pipeline to be used for re-using the treated wastewater back into the system for cooling, flushing and for horticulture purpose/green etc. and shall maintain a record of readings of each such meter on daily basis.
- 20. The quantity of fresh water usage and water recycling shall be measured and recorded to monitor the water balance as projected by the project proponent. The record shall be submitted to the Delhi Pollution Control Committee on six monthly basis.
- 21. Capacity of the Diesel Generator Set (s) proposed to install in the unit shall be 4X 1500 KVA. The Consentee shall provide and maintain the Acoustic Enclosure/ Acoustic Treated room for DG Set(s) in good condition and provide the adequate stack height for DG Set(s) to meet the prescribed standards/ norms. The Consentee shall not operate the DG Set(s) till compliance of the prescribed norms/standards for DG Sets. The D.G. Sets install for construction purposes shall also comply with the prescribed norms/standards.
- 22. The Consentee shall comply with the applicable provisions / Directions given vide Gazette Notification of Department of Environment, Govt. of NCT of Delhi, dated 23.10.2012 including the directions that no person shall manufacture, import, store, sell or transport any kind of plastic carry bags (including that of Poly Propylene, Non-woven fabric type carry bags) in the whole of National Capital Territory of Delhi.
- 23. The Consentee shall provide wide spread Green Cover and the use of Fly Ash as per Fly Ash notification dated 14.09.1999 shall be mandatory.
- 24. Project proponent will ensure use of Ozone depletion substances (ODS) free appliances so that no toxic gases in air conditioning / refrigeration / fire extinguishers are created.
- 25. During construction Phase for control of dust pollution all precautionary measure should be ensured in compliance of Honble National Green Tribunal order dated 04.12.2014 and 10.04.2015 in O.A. No. 21 of 2014 and O.A. No. 95 of 2014 in the matter of VardhmanKaushikVs,. Union India and other and Sanjay KulshreshthaVs. Union of India and Ors. , notified by MOEF and CC, GOI vide Notification no. G.S.R. 94(E) dated 25.01.2018 and Hon'ble Supreme Court orders dated 13.01.2020 in WPC No. 13029/1985 titled M.C. Mehta Vs Union of India & others making the use of anti-smog gun compulsory in the projects that require Environmental Clearance from the State/ Central level on site having built-up area of more than 20,000 sqm including excavation, material handling and other dust generating activities.
- 26. It will be the responsibility of the project proponent to obtain prior clearances/approval and ensure compliances under all other relevant Acts/ Rules/ Regulations/ guidelines/ instructions/ Court Orders/Tribunal Orders as applicable to this project before starting of the project.

- 27. The Consentee shall comply with the provisions of Solid Waste Management Rules, 2016.
- 28. Unit shall implement the environmental safeguards as per stipulations in Environmental Clearance issued by SEIAA Delhi and shall submit half yearly compliance report in respect of the terms and conditions of Environmental Clearance to Regional Office of MoEF and simultaneously to DPCC on the prescribed date.
- 29. The Consentee shall not extract the Ground Water without obtaining prior permission in this regard from DJB / CGWA. The Consentee shall ensure that there is no bore well in the premises and if exist, same shall be close / sealed with immediate effect till permission received from DJB / CGWA.
- 30. The Consentee shall submit application for extension of the Consent / Consent to Operate, one month in advance of the expiry date of this Consent Order.
- 31. This consent is being granted focusing only on the Water Act 1974/ Air Act 1981. The project will be regulated by the concerned local Civic Authorities under the provisions of the relevant provisions of the extant MPD2021, Building Control Regulations and Safety Regulations. The investment made in the project, if any, based on Consent so granted, in anticipation of the clearance from other statuary authorities shall be entirely at the cost and risk of the project proponent DPCC shall not be responsible in this regard in any manner.
- 32. Project Proponent is allowed to run the pollution control devices and collect and test the data. The trial for three aforesaid purpose is permitted within the period of maximum three months from the date of completion. The Consentee shall give prior intimation, to DPCC, of the dates on which trial would starts and end. Thereafter Project Proponent shall apply for Consent to Operate along with requisite details and test reports to DPCC.
- 33. The Consentee shall abide by the Guideline on Environmental Management of Construction and Demolition (C and D) Waste and Guidelines on Dust Mitigation Measure in Handling Construction Material and C and D waste developed and published by CPCB available at www.cpcb.nic.in.
- 34. The Consentee shall display the enclosed template of Notice for Construction and Demolition WasteManagement at the site.
- 35. The Consentee shall ensure the compliance of policy to be followed regarding operation of Ready MixConcrete Plants (RMC Plants) issued vide office order No. DPCC/CMC I/RMC/2017/2596 to 2614 dated27.12.2017 (available at DPCC website).
- 36. In the event of any information furnished by the Consentee found to be false OR in case of failure to comply with any of the above mentioned consent conditions, consent granted through this Consent Order shall be deemed to be revoked without any notice and necessary action as per law shall be taken, which may include closure of the unit and prosecution for wrong declaration.
- 37. Notwithstanding anything contained in this consent order. Delhi Pollution Control Committee, reserves its right to review any / or all the conditions imposed herein above and to make such variations as deemed fit for the purpose of enforcement of the Air (Prevention and Control of Pollution)Act, 1981, as amended to date and the Water(Prevention and Control of Pollution)Act, 1974, as amended to date.
- 38. The Consent granted to the Consentee is to ensure control of pollution from the premises of the unit in accordance with various Pollution Control Laws and in no way confers the right to the Consentee / unit to exist in violation of other laws and statutory provisions including the Master Plan of Delhi.
- 39. The Consent granted to the Consentee is to ensure control of pollution from the premises of the unit in accordance with various Pollution Control Laws and in no way confers the right to the Consentee / unit to exist in violation of other laws and statutory provisions including the Master Plan of Delhi.

This issues in view of the Office Order dated 12.04.2016 regarding processing of the Consent to Establishcases.

Template for displaying notice w.r.t. condition no 33 to be displayed on board of size 6 feet X 4 feet. Background color- Yellow, Letters- Black

#### **NOTICE**

(Construction and demolition waste management rule 2016)

The construction/Demolition site is authorized by... Vide file no... Dated.....

- 1. Name and Address with contact number of contractor/developer
- 2. Address of the site
- 3. Area/length
- 4. Date of initiation of the project (dd/mm/yy)
- 5. Scheduled completion date of the project (dd/mm/yy)
- 6. Details date of completion/disposal/clearing of the site (dd/mm/yy)
- 7. Estimated waste (TPD)
- 8. Total estimated waste (MT) for the entire project
- 9. Nature of waste (concrete/iron/plastic/soil) (TPD)

Material Generated Recycled Reused Disposed

Sand
Concrete

- 10. Identified waste disposal site
- 11. Mode of utilization of waste (reuse/recycle/converting to construction material)
- 12. Mode of disposal
- 13. Mode of handling and transportation (manual/mechanical/pneumatic) (by road/rail)
- 14. Dust mitigation measures at the site (water sprinkling/curtain/barriers etc.)
- 15. Reason of delay in disposing waste (in any)
- 16. Accidents reported (in any)

Name of Agency Owner

Telephone number

Form and Challan of fees paid for Renewal of Consent to Operate and Consent to operate for new Area

11/4/22, 12:31 PM **Untitled Document** 



**Name of Regional Office** 

## Online Consent Management & Monitoring System

Delhi Pollution Control Committee 41H Ploor, ISBT Indiding, Endouve Cate Delhi-Looni visit us at https://dpecocions.nie.in



#### FEE RECEIPT

486347695 Receipt No. **Depositor Name** SHASHI SHARMA

Bank Name. Bank Id. **Application No.** 

SELECT CITYWALK (SHOPPING MALL), Plot A-3 and P1B, District Centre, Saket, Housing Complexes, Commercial Complexes (including shopping malls), office complexes including IT and Infrastructual and Town Development Projects (Built Up Area 20000 sq. meters and above), SOUTH Name and Address of Industry

CMC II

ICICI

8706964

NA

**Applied For** CTO - BOTH - RENEW **Payment Date** 

02-11-2022

**Payment Details** 

**Payment GateWay Name** EASYPAY\_ICICI **Total Amount Paid (Rs.)** 3000000 **Transaction Status** Successfully Completed

Print

FORM NO: 8706964 DATE: 31/10/2022

RECEIVED BY: DPCC



## DELHI POLLUTION CONTROL COMMITTEE 4th Floor, ISBT Building Kashmere Gate, Delhi 110006

## Common Application for Consent Under Water(Prevention and Control of Pollution)Act,1974 and Under Air (Prevention and Control of Pollution)Act, 1981, as amended

## RED

From

SELECT CITYWALK (SHOPPING MALL) Plot A-3 and P1B, District Centre, Saket

To,

The Member Secretary,
Delhi Pollution Control Committee,
4th Floor, ISBT Building Kashmere Gate, Delhi 110006.

### Sir/Madam,

I/We hereby apply for\*

- (i) Consent to operate of consent under section 25 & 26 of the Water (Prevention and Control of Pollution) Act,1974 as amended.
- (ii) Consent to operate of consent under section 21 of the Air(Prevention and Control of Pollution) Act,1981 as amended.

## **PART A: GENERAL**

1. Name : SHASHI SHARMA

Designation : Director Ops and project

Office Address : Delhi, Plot A-3 and P1B, District Centre,

Saket,South

Telephone/Fax and : 9540339933

Email Address of the applicant : shashis@selectcitywalk.com

Bank Name ·

Bank Address :

Account Number :

IFSC Code :

GSTN Number :

2. (a) Name and address of the Industrial SELECT CITYWALK (SHOPPING Unit/Project/Premises for which the MALL) application is made. (with telephone No. and Plot A-3 and P1B, District Centre, Saket, Delhi e-mail) 91-9540339933 (b) Manufacturing activity Commercial Complex (Shopping Mall) (c) Status of the unit Owned Premises SHASHI SHARMA, Plot A-3 and P1B, (d) Name and address of the premises owner District Centre, Saket, Delhi SHASHI SHARMA, Director Operations (e) Name & Designation of the person authorized to sign this application form and Project (f) Latitude/longgitude of the premises of 28.3144,77.1310 the unit 3. Names, residence address with telephone SHASHI SHARMA, Plot A-3 and P1B, and fax number of Managing District Centre, Saket, Delhi Director/Managing Partner and officer responsible for matters connected with pollution control. 4. If registered as a small-scale industrial -N/A unit, give Number and Date of registraion. 5. Gross capital investment (in Lakh.) of the 47563.0 unit without depriciation till date of application (cost of building, land, plant and machinery)(To be supported by an Affidavit and: Certificate form a Charted Accountant. For proposed unit(s), give estimated figure). Housing Complexes, Commercial 6. (a) Location of the Unit. Complexes (including shopping malls), office complexes including IT and Infrastructual and Town Development Projects (Built Up Area 20000 sq. meters and above) (b) If situated in industrial Area, details of ,Attached CETP Society membership thereof. (c) Whether total effluent / sewage from the No unit is discharged into conveyance system leading to CETP (d) Whether a copy of certificate for Attached connection for discharge of total effluent / sewage into conveyance system is enclosed. 7. (a) Total plot area of unit(in sq. meter). 24174.66 (b) Built-up area of the unit (in sq. meter) 118079 (c) Sanction Power Load (in KW) (Details 5660 of electric meter number and name of the person be indicated (i) Electric Meter Number XH413006 (ii) Name of the Person Select Infrastructure Pvt Ltd (d) Date of Possession of the land 04/10/2004 (e) Date of Commissioning of Construction 22/02/2005 (f) Date of completion / proposed date of 12/10/2007 Completion of construction. (g) Status of Environment Clearance, under Yes EIA notification(if applicable)

12/10/2007

0

8.

9.

Date of Commencement of Production.

(a) Number of workers

(b) Number of employees (including	:	10567
workers and office staff)		

10. List of products manufactured in tones/month, Kl/month or numbers/month

Product	Quantity	Unit	Maximum Installed Production Capacity
It is a Commercial Complex	0	Metric Tonnes/Day	0

List of by-products manufactured in tones/month, Kl/month or numbers/month.

Byproduct	Quantity	Unit	Maximum Installed Production Capacity
It is a Commercial Complex	0	Metric Tonnes/Day	0

11. List of raw materials and process chemicals with annual consumption corresponding to above stated production figures, in tones/month or kl/month or numbers/month.

Raw Materials Name	Quantity	Unit
It is a Commercial Complex	0	Metric Tonnes/Day

**12.** Description of process of manufacture for each of the products(showing input,output quality and quantity of solid,liquid and gaseous wastes,if any from each unit process)

Flow of manufacturing process	Description of manufacturing process
It is a Commercial Complex	It is a Commercial Complex

## **Part - B Waste Water Aspects**

13. Water consumption for different uses (litres/day)

(a) Domestic purpose : 264000

(b) Industrial cooling or boiling feeds : 300000

(c) Processing whereby water gets : 0 polluted and the pollutants are easily bio-degradable.

(d) Processing whereby water gets : 0 polluted and the polluted and the polluted and the polluted and the pollutants are not easily bio-degradable and are toxic.

(e) Others such as agriculture, : 135000 Gardening etc. (specify)

14. Source of water supply

(a) Municipal Authority : 354000 Litres/Day

(details of water meter and name of the Person be indicated)

(b) Ground Water : 0 Litres/Day

(details of CGWA/DJB/DC permission/registration)

15. Quantity of waste water (effluent) generated

(i) **Domestic** : 234000

	(ii) Industrial/Trade Effluent			
	(a) Process	:		0
	(b) Washings	:		0
	(c) Cooling Water Blowdown	:		0
	(d) Boiler Blowdown	:		0
	(e) DM Plant/Softening Plant washings	:		0
	(f) Other	:		11000
	Total Industries/Trade Effluent (litres/day):	:		11000
16.	Present treatment of trade effluent (G schematic diagram of the treatment s opetation/process is to be provided. I sludges)	cheme	with inle	t/outlet characteristics of each unit
	Type of treatment Plant for trade efflu	uent	Design	Capacity
	Oil & Grease Trap		0	
17.	Mode of disposal of treated effluents,	with Re	espective	e quantity. Litres/Day
	(i) Into public sewer/open drain/land for irrigation/inland surface water.	:		0
	(ii) Quantitiy of treated effluent Reused/Recycled,(litres/day).Details of reuse / recycle in cooling / flushing / gardening / manufacturing	:		220000
	(iii) Provide a location map of disposal arrangement clearly indicating the outlet(s) for sampling	:		to be enclosed
18.	(a) Quality of Untreated/treated effluent (the industry. Refer Schedule-I for industry standards of Environment Protection			
	(b) Enclose a copy of the latest Report of Pollution Control Committee. For propos Untreated/treated effluent.			
Part -	C Air Emission Aspects			
19.	Details of Stack (Process & Fuel Stack	cks)		
	(a) Stack number(s)	:		5
	(b) Attached to	:		DG set (more than $800~KW$ ),
	(c) Capacity	:		2,2,2,1.01,1.01,

(d) Fuel Type

(e) Fuel Quantity (Kg/hr or lit/hr) 250, 250, 250, 130, 130,

High Speed Diesel , High Speed Diesel , High Speed Diesel , High Speed Diesel , High Speed Diesel ,

(f) Material of construction : MS, MS, MS, MS, MS,

(g) Shape (round/rectangular) : Round, Round, Round,

Round,

(h) Height,m(above ground level) : 44, 44, 44, 44, 44,

(i) Height,m(above roof level) : 6,6,6,4,6,

(j) Sampling facility provided : Yes, Yes, Yes, Yes, Yes,

(k) Diameter/size, in meters : 0.45, 0.45, 0.45, 0.45,

(1) Gas quantity, Nm/hr, 0, 0, 0, 0, 0,

(m) Gas temprature, C : 0, 0, 0, 0, 0,

(n) Exit gas velocity, m/sec. 0, 0, 0, 0, 0

(o) Control equipment :

Other
Other
Other
Other
Other

# 20. Details of D.G. Set(s)

Capacity (in KVA)	Stack Height above Ground Level (in meters)	Stack Height above roof of the building where D.G. Set installed (in meters)	Manufactur ing Date	Acoustic enclosure installed	Noise Monitoring report submitted	Noise Level within the limit
2000	44	6	After Jan 1, 2005	Yes	Yes	Yes
2000	44	6	After Jan 1, 2005	Yes	Yes	Yes
2000	44	6	After Jan 1, 2005	Yes	Yes	Yes
1010	44	6	After Jan 1, 2005	Yes	Yes	Yes
1010	44	6	After Jan 1, 2005	Yes	Yes	Yes

21. Quantity of treated flue gas emmissions and process emissions (Enclose a copy of the latest + report of analysis form the approved labaoratory by Delhi Pollution Control Committee. For proposed units furnish the expected characteristics of the emission).

# Part - D Hazardous Waste Aspects

22. (a) Whether the unit is generating : No hazardous waste as defined in the Hazardous Waste (Management and

Handling) Rules, 1989, as amended.

(b) If Yes, Select type of hazardous : [] waste generated

(c) Whether authorization granted, if : , N/A yes, indicate the authorization no. and

date

23. Quantity of hazardous waste generated (kg/day) or (MT/month).

Category	r	Types		Quantity of Waste Generated	
----------	---	-------	--	--------------------------------	--

- 24. I/We further declare that the information furnished above is correct to the best of my/our knowledge.
- 25. I/We hereby submit that in case of any change from what is stated in this application in respect of raw materials, products, process of manufacturing and treatment and/or disposal of effluent,emmissions / hazardous waste etc. in quality and quantity; a fresh application for Consent / Authorization is granted, no change shall be made.
- 26. I/We undertake to furnish any other information with one month of its being called by the committee.
- 27. I/We agree to submit to the Committee an application for renewal of consent/authorization in two months in advance before the date of the expiry of the consent/Authorization validity period.
- 28. I/We hereby declare that the provision of Master Plan of Delhi shall not be violated at any stage.

Signature.....

Name: SHASHI SHARMA

Designation: Director Ops and project

# <u>Annexure – 29</u>

Installation certificate of retrofit pollution control device Chakra Shield in DG sets.



Tel: +91-124-4084599

URL: www.chakr.in Email: info@chakr.in

Date: 24 December 2020

# **Work Completion Report**

This is to inform you that as per PO Number "SCW/RGPO/ENGG/VS/FY19-20/0287", Chakr Innovation Pvt. Ltd. has successfully installed Chakr shield (Retrofit emission control device) on different rating's Diesel Generator (3 nos. 2000KVA and 2 nos. 1010 KVA) at Select Infrastructure Private Limited (Select CITYWALK), A-3, Saket District Centre, New Delhi - 110017, and achieved minimum of 70% efficiency in all 5 DG Sets (3 nos. 2000KVA and 2 nos. 1010 KVA).

Customer Name	Select Infrastructure Private. Limited.(Select CITYWALK)
Site Address	A-3, Saket District Centre, New Delhi -110017
Invoice Number	CHK/20-21/0018, CHK/20-21/0017
Purchase Order Number	SCW/RGPO/ENGG/VS/FY19-20/0287
Purchase Order Date	20/09/2019
POC (Chakr Innovation Pvt. Ltd.)	Mr. Vinod Bhoir
POC (Select Infrastructure Private Limited - Select City Walk)	Mr. Vidyanand Srivastava

# Intervention Points:

20 September 2019	PO Generation Date	
18th February 2020	Device Shipment Date	
20 February 2020	Installation Started	
5 November 2020	Installation Completed	

Contact Details:

Vinod Bhoir vinod.bhoir@chakr.in

Chakr Innovation Pvt. Ltd.

UNA REPORTED TO THE PARTY OF TH

Select Infrastructure Pvt. Ltd.

# Annexure – 30

Test report of Chakra
Shield as approved
by CPCB approved
laboratory



# INTERNATIONAL CENTRE FOR AUTOMOTIVE TECHNOLOGY

[A Division of NATRIP Implementation Society (NATIS), Govt. of India]

ULR No-TC536021060000140F

CDOEQ 0251

22/07/2021

			DEVELOPME	ENT TEST				
Test Sponsored	by:	AND DEV	P. S. W. S.	DVA DE N	Objective of the	Test:	Contract of	
M/s Chakr Innovat 102-9/54, First Fk Namdhari Chambi Delhi-110005 New	oor, D.B. Gupta er, Karol Bagh,	Road,			To carry cul develo		ISO 8178 D2 5	
Test Date:	13/07/20	21 & 14/07/2021	Test Site	ETC-11	IQCS No. : 14895	10		
Engine receipt d	ate	01/07/2021	Condition of English	10 01	Any deviation fro	m test method	None	
Engine	100	Make	Ws Caterpillar		Tested Model	C32		
TO RES	100 TH	ALBERT STEEL	Brief Specification	of Engine				
Bare (mm)		145	Stroke (mm)	162	No. of Cylinders	12		
Working Principle 4-Stroke			Туре	v	Swept Volume (II	L) 32:101		
Cooling System	HARRY.	Liquid Cooled	Aspiration / Injecti	TCICIDI	Fuel Type	Diesel		
		Make	M/s Chakr In toward	7	W. 120 (0)	1		
After treatment a	yacem	Model No.	DOFF/V C. H. V. N	100/750-1000	No. of devices			
Turbocharger		Make	Min Calegoliar	1	Part No.	445-1674		
Ter	t Equipments	used		Make:	200	Model	1000	
Er	gine Dynamom	oter innovatio	In Our ICE so	сновене Пелсе		D-41238		
Exhaus	st Gas Analysis	System	HOR	BA,JAPAN	2	MEXA-740	00	
A	rflow measuren	tent		ABB		SENSYFLO	W-P	
Part	iculate Measure	ement	HORI	BA,JAPAN		MDLT-1303	TM	
7,000	Smoke Meter	84		AVL		4158		
	Weighing Balan	00	Sa	ertorious		MSU2.78		
Fue	Consumption I	Moter	CP En	JUK, grinsering				
Cor	nditioned Air Sy	stem	CP En	gineering ,UK		CAHU-2500		



Office Address: Centre-I: Plot No.-26, Sector-3, HSIDC, IMT-Manesar, Gurugram-122050. Haryana (India) Centre-II: Plot No.-01, Sector-M-11, HSIIDC, IMT-Manesar, Gurugram-122050. Haryana (India) Phone: 0124-4586111, Fax: +91-124-2290005. E-mail: team@icat.in, Website: www.icat.in (An ISO 9001, ISO 14001 and ISO 45001 certified, scope wise NABL accredited and BIS recognised Test House).



## ULR NO-TC536021060000140F

### CDOE Q 0251


Date - 22/07/2021

Summary	of Test Ro	sults :	Test result	are given in	Annexure	D Sain	14.1	■ Sample 2		
Mass Brits lone In 194 Whi	Bample No.	Observed Rated Power(kW)	co	нс	NOx	HC+NOx	PM	0		
		799.80 (With After treatment system)	0.03	0.01	9.27	9,28	0.007	Vicwh O		
	2	799.63 (Without After treatment system)	0.93	0.08	9.22	0.30	0.095	η ω,	HC NOX	HC+MOx
Conch	noisu	As per Annexure t & II			_	_				
Rem	irk to	Test was carried out with com-	mercial dies	et.						

- 1. CAT issues Developmental Test Reports for vehicles toamponents/parts/ assembles etc. based on the documents pro prototype / vehicle(s) or sample(s) submitted by the applican end teating thereof
- 2. ICAT is sum: Test Reports/Extension Reports/ Developmental Test Reports in compliance to Multir Vehicle Act/ Com Motor Vorsite Nuise and their provisions as prended from line to line or an ther statutory orders under which ICAT is watherized. Other Rales/Acts are outside the purview (scope of the last Rec. Extension Reports/ Developmental Test Reports
- specifical requested by the applicant. Results of such tests are property Test(s) on prototype /vehicle(s) or earque(s) inlaw carried out on the basis of standard procedures as notified to of boarer of Test Reports/ Extension Reports/ Developmental Test Reports. These results cannot be disclosed unless as cally ordered so by Government, Court, etc.
- E. Unless ethors he supported by a separate Certificate, this Test Reporte? Extension Reports/ Developmental Test Reports Trust not be considered in solution as weld Type approval for any vehicles.

  6. ICAT is not responsible for testing such vehicles/components/parts/assentities etc. for which Test reports Extension reports/ Developmental test reports is fasued. Further, ICAT is not responsible for ensuring manufacturing quality of the vehicles/components/parts/assentities etc. for which the responsible for ensuring manufacturing quality of the vehicles/components/parts/assentities etc. for which
- 6. CAT is in no way responsible for any misuse or copying of any design/lype/system in connect the vehicle/ components/parts and assembles covered under the Tiest Reports Extension reports/ Developmental test reports, is have sessed.
- 7. Breach of any statutory provisions, of Viden laws or laws of other countries, will be sole resp on and shall undertake to inderently CAT in this regard. warer of Test Reports/ Extension Reports / Developmental reports lafare seased and CAT shell not be liable for any claims or damages, whatevever. The bearer shall alone be liable for the
- 8. Further, CAT has the right, but not under obligation to indiate curtostation / withdraw at of to at Reports/ Extension Reports/ Developmental Yest Reports is/are as used in case of any freud microprocentation, when it surfaces and comes in the two lodge of EAT
- or product without the written consent of the Director, CAT, who reserves the absolute right to 9. No extract, absidgment or abstraction from this text report may be published or used to adve agree or reject all or any of the detals of any items of publicity for which operant may be a 10. ICAT has not verified any physical directions, observed properties, build quality, con-
- 11. Considering the confidentiality and pending patents of After treatment system. is are about it is CAT.

The appropriate local court at Gurugram shall have the jurisdiction in respect or tability wising out of this report





# ULR NO-TC536021060000140F

C D 0 E Q 0251

Date - 22 07/2021

									An	nex	ure	1							
						Emis	sion	Per	forma	ance	Tes	t: 5	Mo	de cyc	le		J		
																Modes	THE REAL PROPERTY.		
															Engine	81	JP 10737		
	_	-							_										
Mode	Speed	Torque	Power	Fuel Flave	BSFG	fuelling	Ally In Temp	пн	Baro Pross	Air Flow	AIF	Fa	AID	ISSP at attendend location as per ISC 6176	100	O	SBP at inist of ATS*	BBP at Dutlet of ATS**	Delta auros the A1
····	rpm	Nes	kW	kgiti	pawa	mm3/str/	90	*	NP4	kgrit	*****		ethar	man	91	40	rebar	mbar	mba
-1	1490	5005,1	790.80																
2	5498	1820.9	599.79																
3	1499	2547.0	300.81																
4	1498	1223.0	189.83																
- 5	14899	509.4	79.86										1						
	2						2			0.00	3 1 1 1						1111224		11
Mede	*NOs	60	*THC	002	OE.	Smoke	Dry-Wei		Hern ears, t	ofity tector	N	OX.	co.	на	W	WWOK	wco	WHO	m# OWE
*****	ppm	ppm	ppm	16.	-	ENN	-			-		•	gin	gh		gh	gh	gth	1.W
											1	•							
2																			
3																			
4											<b>N</b> , , ,								
. 5																			
These	valves	are base	nd on W	et Basis	s Measu	ement				Q	7			Tel		3604.11	11,21	3,71	377.83
We is	gisted M sion Res	ese ulta	Unit					4							Particul	ole Mans			mg
10			gkWh					_							Missen T				Ag.
10		ı	gAWh					7								righted Avg			- Right
POK.			gRWH;						-						La Marchaela Laboratoria	er Temp	ion I		Deg C
C+Nox			gkWh gkWh						- 3						Power l	Weighted A	VB.		WW.
Te.	_		Agents:					-											
Rema		YOUP at in	at of ATS	was to	en at a di	with One a tance of 540 distance of	S I Stan	that wo	stere. gitte exitu										





## ULR NO-TC536021060000140F

C D 0 E Q 0251

Date - 22/07/2031

							Ar	nexu	ire II	Į.						
					Emis	sion P	erforn	nance	Test	: 5 Mod	ie cy	- Personal Property and Propert				
												Engin	e Model	Cas		
												Engin	P No	JFE00737		
Aode	Speed	Torque	Power	Fuel Flow	BSFC	Fuelling	Air In Temp	RH	Baro Press	Air Flow	AF		AID	EBP at standard legation as per ISO 8178	BEP	тмт
	rpm.	Nn	xw	kgh	pkWh	mm3/str/c	*0	%	MPa	kgftr			mbar	mbar	mber	10
1	1499	5005.1	799.80													
2	1400	3821.0	599.00							1						
3	1499	2547,0	399.81													
4	1409	1273.0	199.83													
5	1409	500.5	79.98									-				
fode	*NOx	co	*THG	CO2	02	Smoke	Dry-Wet corr, factor	Humidity corr. factor	No.	co	нс	WF	WNOK	wco	WHC	WPOWE
	ppm	ppm	ppm	%	2000	FSN		(*****	jih i	għ	gfh		gth	gth	gh	kW
1																
2																
3									27							
4																
5																
These v	alues are	based on	WM Basis	Measuren	eri						To	otal	3484.77	352.40	29.16	377,83
	d Mass Results	Baission	Unit										Particulat	Mann .		mg
0	2.75 V. 75 V.		gWWh:			X							Msam Tol			Pα
2			g8Wh										Gest! Weig			kgft
			gNVAh				-						Max. Filter	And the second second second		Dag C
DX D+Max			gRWh:										LOMB AND	righted Avg.		KWV .



# <u>Annexure – 31</u>

Occupancy – cum completion certificate
issued by Delhi
Development
Authority

# FORM- D-1 (Chapter 2, Para 2.7.1/2.7.3)



# OCCUPANCY-CUM-COMPLETION CERTIFICATE

# Delhi Development Authority

**BUILDING SECTION** 

File No.: SZ/0110/19-20 OCC

Dated.

: 26 August, 2022

Plan No. :

To,

Shri/ Miss/Smt. Shashi Sharma

Select Infrastructure Pvt Ltd A-3 District Centre Saket, Newdelhi.

With reference to your notice of completion dated 16 June, 2022. I hereby certify that the building as per description below and certified plans of SZ/0110/19-20 whose LOP & Bldg. plans were sanctioned vide letter No. CA/BP/0111/19-20 dated 17 January, 2020 and completion certificate as approved by DUAC/DFS and other statutory bodies, the NOC has been approved on 26 August, 2022 .The site has been inspected with reference to Building Bye-Laws, MPD provisions, hygienic and sanitary conditions inside and in the surroundings and is declared fit for occupation.

The sanctioning authority approves Architectural Drawings/Development Control norms with respect to the Building Bye Laws and MPD provisions only. The technical drawings/documents submitted by the owner/consultant/Architect/Engineer/Structural Engineer/Landscape Architect /Urban Designer/Engineer for Utility Services are considered as part of the records/information supporting the building permit only. The responsibility of the correctness of information/application of technical provisions fully vests with the owner/consultant/ Architect/Engineer/Structural Engineer/Landscape Architect /Urban Designer/Engineer for Utility Services and shall be liable as per laws.

The structural stability of the building is based on the certificate given jointly by the Owner/Architect/Structural Engineer along with one set of Structural Drawings, incorporating therein the provisions of Structural Safety as specified in the relevant prevailing IS Codes/Standards/Guidelines stated in the Government of India Notification bearing No.SO-248(E) dated 21.3.2001 and clause 9.1, 9.2.1, 9.2.2 and Annexure VII of this Bye Laws. For the fire-safety the same has been based on the Fire Safety Certificate given by the Delhi Fire Services, Government of NCT of Delhi. The sanctioning authority shall not have any responsibility for any loss caused to the building from any natural hazard / calamity.

Completion Certificate is issued for Plot No. Building No.: SELECT CITY WALK, Plot No :A3 & P1B, Ward: DISTRICT CENTER, Situated at:SAKET, NEW DELHI as per enclosed drawings.

Encl. One set of Completion Plan

Your Faithfully

Name: PARVEEN KUMAR Designation : Assistant

Engineer

Organization: DELHI **DEVELOPMENT AUTHORITY** 

Date: 26-Aug-2022 16: 32:56

For Vice Chairman

Delhi Development Authority

# Annexure – 32

# CER expense (April 22- March 23) with details

# Report on CER expense (April 22 to March 23) – Select Infrastructure Private Limited (Select CITYWALK)

Select CITYWALK, India's most admired shopping and entertainment destination that has won accolades for its CSR initiatives joined hands with South Delhi Municipal Corporation towards making a contribution to the promotion of the Prime Minister's widely acclaimed "Swachh Bharat Abhiyaan".

A firm believer of "charity begins at home", Select CITYWALK took responsibility for neglected lands which were a dumping ground earlier and converted it into a beautiful parks which are called, Jamun Wala Park and Gandhi Wala Park.

Both these parks are maintained by Select CITYWALK with horticulture and landscaping, disabled – friendly ramps to access the park, energy saving LED lights, surveillance and security systems. The parks also consists of an Open Gymnasium, Badminton Court, Kids Play Area, Yoga and Meditation area, Elder sitting area, Butterfly Sculpture Garden, Pergola Walk, Gazebo, Bamboo Cluster Walk and Joggers Trail. Both these parks are open to public and the facilities are thoroughly enjoyed by the community.

As per EC condition issued, Select CITYWALK was to draw up and implement corporate social Responsibility plan as per the Company's Act of 2013. As per the Ministry's Office Memorandum F.No. 22- 65/2017-IA. III dated 1 May, 2018, and proposed by the project proponent, an amount of Rs. 0.32 Crore (@ 1.00% of Project Cost) was earmarked under Corporate Environment Responsibility (CER) for the activities such as drinking water supply, plantation and horticulture and skill development & computer education. The activities proposed under CER shall be restricted to the affected area around the project.

Accordingly, Select CITYWALK has developed and is maintaining Jamunwala park and Gandhiwala park. Both these are parks are in near vicinity of the Mall and are playing significant role in providing clean environment to the residents of Hauz Rani and Khirki village.

During the period of 1/04/22 to 31/03/23 Select CITYWALK has spent Rs. 89,78,424 for developing and maintaining Gandhiwala park and maintaining Jamunwala park. The details of expense and photographs of both the parks are attached below.

# SDMC Park






















# **DDA PARK**





























		CER Expense Details 1st April 2022 to 31st March 2023							
Month	Amount	Details of Expenses							
July	130276.03	Landscape maintinance services for the m/o juy'22							
July	440452	towards deployment charges for PSO July '22							
		Vendor - 360 INFRATECH AND WASTE SOLUTIONS, Event Name- Azadi Ka Amrit mahotsav SDMC campaign,							
		total wall painting area - 1100sqft, total amount - 154000+taxes, Based On Purchase Request 281. Based On							
August	154000	Purchase Orders 40261.							
A	1000	alactricity, charges in recursively morely (Newsonder Charges (Congr. Dyscod))							
August	1900 440452	electricity charges jamunwala park (Narender Sharma/Ganga Prasad) towards deployment charges for month of Aug'22							
August August	26710	towards deployment charges for NH payment 15th Aug'2022							
August	131399.62	Landscape maintinance services for the m/o Aug'22							
August	25510	towards electricity charges for the m/o 05.08.22 to 03.09.22							
	78300.61	Housekeeping Dceployment for the month of Aug-22 (Jamunwala Park)							
August	1								
September	7130	electricity charges jamunwala park (Narender Sharma/Ganga Prasad)							
September	1760 1596078	electricity charges jamunwala park (Narender Sharma/Ganga Prasad) 20.08.22 to 17.09.22  Devlopment cost of gandhi wala park							
September		towards electricity charges for the m/o 04.09.22 to 04.10.22							
September September	35410 3619	Water Charges from 01-09.22 to 30-09-22							
-		towards deployment charges for month of Sep'22							
September	405351 115774	Landscape maintenance charges for Sep'22							
September	92216	Housekeeping Dceployment for the month of Sep-22 jamunwala park							
September									
September	113494.68	Landscape maintenance charges for Oct'22 Gandhi park							
September	69162	Housekeeping Dceployment for the month of July-22 jamunwala park							
September	1890	electricity charges jamunwala park (Narender Sharma/Ganga Prasad/Narender Sharma) 31.08.22 to 30.09.22							
October	5236	Water Charges from 01-10.22 to 31-10-22							
October	654755	Grass Carpet, Plant - Bodelia 4 Inch Pot, Plant - Song Of India 8 Inch Pot							
October	36050	towards electricity charges for the m/o 05.10.22 to 03.11.22							
October	442807	towards deployment charges for month of Oct'22 & NH 2nd oct(JAmunwala park)							
October	442007	towards deployment charges for month of occ 22 & 1111 2nd occ(s/andhwald park)							
October	1780	electricity charges jamunwala park (Narender Sharma/Ganga Prasad/Narender Sharma) 01.10.22 to 31.10.22							
October	98223.5	Housekeeping Dceployment for the month of Oct-22 Jamunwala Park							
November	50000	maintenance cost including plantation at SDMC ghandhi park							
November	3560	electricity charges jamunwala park (Narender Sharma/Ganga Prasad/Narender Sharma) 18.10.22 to 16.11.22							
November	50000	Maintinance cost including plantation & Maintinace at SDMC Gandhi Park							
November	438150	towards deployment charges for month of Nov'22 (Gandhi park)							
November	2583	Water Charges from 01-11.22 to 30-11-22 (Gandhi Park)							
November	128880.07	Landscape maintenance charges for Nov'22 Gandhi park							
November	93644	Housekeeping Dceployment for the month of Nov-22 Jamunwala park							
November	41350	towards electricity charges for the m/o 04.11.22 to 03.12.22							
December	50000	Maintinance cost including plantation & Maintinace at SDMC Gandhi Park m/o Dec'22							
December	442803	towards deployment charges for month of Dec'22 (Gandhi park)							
December	126945.87	Landscape maintenance charges for Dec'22 Gandhi park							
December	93644	Housekeeping Dceployment for the month of Dec-22 Jamunwala Park							
December	45310	towards electricity charges for the m/o 04.12.22 to 04.01.23							
December	3490	towards electricity charges for the m/o 01.12.22 to 29.12.22							
December	3239	Water Charges from 01-12.22 to 31-12-22 (Gandhi Park)							
January	3530	towards electricity charges for the m/o 17.12.22 to 16.01.23							
	1	, · · · · · · · · · · · · · · · · · · ·							

January	469448	towards deployment charges for month of Jan'23 (Gandhi park)							
January	191412.05	Landscape maintenance charges for Jan'23 Gandhi park							
January	98978.69	Housekeeping Dceployment for the month of Jan-23 Jamunwala Park							
January	22500	Consultancy Services Gandhi Park							
January	36540	towards electricity charges for the m/o 05.01.23 to 02.02.23							
January	1880	, 0							
February	441822	towards deployment charges for month of Feb'23 (Gandhi park)							
February	155706.24	Landscape maintenance charges for Feb'23 Gandhi park							
February	93644	Housekeeping Dceployment for the month of Feb-23 Jamunwala Park							
February	2130	towards electricity charges for the m/o 16.02.23 to 20.03.23							
February	46000	towards electricity charges for the m/o 03.02.23 to 3.03.23 Jamunwala park)							
March	1640	Water Charges from 01-02.23 to 28-02-23 (Gandhi Park)							
March	158892.55	Landscape maintenance charges for March'23 Gandhi park							
March	76274.55	Housekeeping Dceployment for the month of March-23 Jamunwala Park							
March	442803	towards deployment charges for month of March'23 (Gandhi park)							
March	10572.71	Housekeeping Dceployment for the month of March-23 Jamunwala Park							
March	1681	Water Charges from 01-03.23 to 31-03-23 (Gandhi Park)							
March	37994								
	8978424.17								

# Annexure – 33

# Form V for FY 2021-22



SIPL/Engg/22-23/0011

DELHI POLLUTICA CONTROL COMMITTEE
DEPARTMENT OF ENVIRONMENT
GOVT OF NOT OF DELHI
4TH FLOOR, ISBT BUILDING,
KASMHERE GATE, DELHI-110008

22<sup>nd</sup> September 2022

To

The Member Secretary DPCC Dept. of Environment (Govt. of NCT of Delhi)

Sub: Submission of Environment Statement for the financial year 2021- 22.

Dear Sir,

Kindly find attached the Submission of Environment Statement for the financial year 2021-22.

Thanks & Regards

For Select Infrastructure Pvt Ltd.

Shashi Sharma Director- Operations & Projects

Form No. : V

# FORM-V ENVIRONMENTAL STATEMENT FORM-V

(See Rule 14)

From:

Select CITYWALK,
Select Infrastructure Private Limited,
A-3 & P I B, District Centre,
Saket,
New Delhi.

To.

Delhi Pollution Control Committee, Government of N.C.T. Delhi, 4th Floor, ISBT Building, Kashmere Gate, Delhi-110006

ENVIRONMENTAL STATEMENT for the financial year ending the 31st March, 2022.

### PART-A

(i)	Name and address of the owner/ occupier of the industry operation or process	M/s. Select Infrastructure Pvt. Ltd. A-3, District Centre, Saket, New Delhi, India-110017
(ii)	Industry category- Primary – (STC Code) Secondary – (STC Code)	Mixed occupancy
(iii)	Production capacity Units	Not Applicable
(v)	Year of establishment	2007
(vi)	Date of the last Environmental Statement submitted	06.07.2021

Submissions of Environmental Statement is in accordance with the provisions of Rule – 14 of the Environment (Protection) Amendment Rules, 1993 of the Environment (Protection) Act, 1986 (29 of 1986) published vide Notification dated 22 04.1993 G.S.R. 386 (E) in the Gazette of India- Extraordinary – Part \_ II Section 3 Subsection (i), No. 155 dated 28-4-1993 by the Ministry of Environment & Forests, Govt. of India; read with the Notification dated 13-2-1993 G.S.R. 386 (E) in the Gazette of India- Extraordinary – Part \_ II Section 3 Subsection (i) No.120 dated 13-3-1993.

Every person carrying on an industry, operation or process requiring consent under Section-25 of the water (Prevention & Control of pollution) Act,1974 (6 of 1974) or under Section 21 of the Air (Prevention & Control of Pollution) Act,1981 (14 of 1981) or both or authorization under the Hazardous wastes (Management and handling) rules,1989 published under the environment protection act 1986 (29 of

1986) shall submit an Environmental Statement for the financial year ending the 31st March in form-V to the consent state pollution control board on or before the Thirtieth day of September every year, beginning 1993.

### PART-B

Water and Raw Material Consumption:

### Water Consumption m3/d (Annual average of financial year 2021 -22) (i)

Fresh water

: 153.67 m3/day

Recycled tanker water: 184.9 m3/day

STP incoming water : 161.3 m3/day

### Breakup of utilization of STP recycled water m3/day (Annual average of financial year 2021 -(ii) 22)

Irrigation

: 36.2 m3/day

Cooling Tower

: 68.65 m3/day

Flushing

: 11.05 m3/day

Backwash/rinse/loses: 23.725 m3/day

Evaporation loses/ recirculation through sludge holding tank: 42.1 m3/day

Name of Products	Process water consumption per unit of product output			
	During the Previous Financial year	During the current Financial year		
	(1)	(2)		
	NOT APPLICABLE			

# (ii) Raw material consumption

* Name of raw materials	Name of Products	Consumption of per unit of	
		During the previous Financial year	During the current Financial year
	NOT AF	PLICABLE	

<sup>\*</sup> Industry may use codes if disclosing details of raw material would violate contractual obligations, otherwise all industries have to name the raw materials used.

PART-C

Pollution discharged to environment/unit of output (Parameter as specified in the consent issued)

Pollutants	Quantity of pollutants discharged (mass/day)	Concentration of Pollutants in discharges (mass/volume)	Percentage of variation from prescribed standards with reasons
(a) Water	The domestic waste water (Annual average of 161.3 m3/day) is treated and reused for irrigation, cooling tower and flushing.	Refer Annexure- I	All results are well within limit.
(b) Air		Refer Annexure - II	All results are well within limit.

PART- D

HAZARDOUS WASTES (As specified under Hazardous Wastes (Management & Handling and Transboundary Rules, 2016)

	Total Quantity (Litres)			
Hazardous Wastes	During the previous Financial year	During the current Financial year		
1. From Process	Not Applicable	Not Applicable		
<ol> <li>From Pollution Control Facilities</li> <li>At select CITYWALK we generate only lube oil as hazardous waste and the same is disposed off as per DPCC norms to authorized recycler Bharat Oil and waste management limited).</li> </ol>	2860 L used lube oil (Volvo line Cummins LA-SAE-15W-40) for the financial year 2020-21.	1260 L used lube oil (Volvo line Cummins LA-SAE-15W-40) for the financial year 2021-22. Form –IV for annual return of lube oil and Form 10 is attached as Annexure 3		

# PART – E Solid Wastes

	Total Quantity (Tons)		
Solid Wastes	During the previous financial year(20-21)	During the current financial year(21-22)  Not Applicable	
a. From process	Not Applicable		
b. From Pollution Control Facility			
c. (1) Quantity recycled or re - utilized within the unit	Dry garbage generated at Select Citywa handed over to Chintan Enviro rese group which gets it recycled and wet gar is treated and converted into organic maby processing it through Organic V Convertor.		
(2) Solid (Dry waste) (Total generated in tons)	31.426 ton	49.799 ton	
(3) Wet waste	104.812 ton	124.352 ton	

Please specify the characteristics (in terms of concentration and quantum) of hazardous as well as solid wastes and indicate disposal practice adopted for both these categories of wastes.

There is no generation of hazardous waste.

The used oil generated is disposed off to Pollution control board approved vendor Bharat oil and waste management limited and Form 10 and Form 4 are submitted timely to DPCC.

The solid waste generated during operational phase is segregated at source and is taken for recycling by an NGO M/s Chintan Enviro and Research group, a leading NGO in environmental field in Delhi NCR.

All of Wet biodegradable waste (124.352 tons) for the year 2021-2022 was converted into organic manure by processing it through Organic Waste Convertor at Select CITYWALK itself and the manure produced 14.571 ton was used for horticulture purpose within Select CITYWALK.

All e waste generated was handed over to authorized e waste collector M/s Bharat oil and waste management limited. Form 1 for annual return of e waste is submitted to DPCC.

All battery generated is handed over to authorized vendors and half yearly return is submitted to DPCC.

# PART - G

Impact of the pollution control measures taken on conservation of natural resources and or the cost of production.

Rain water harvesting is being done at select CITYWALK. The entire rainwater of the Roof top area and the runoff water from open paved and unpaved area is recharged into the underground aquifer through (17 Nos.) of recharging pits.

### PART - H

Additional measures/ investment proposal for environmental protection including abatement of pollution.

Concentration of pollutant discharge from DG sets and Hot water generator is below standard limit. The test reports from MoEF approved laboratory has been attached.

DG sets are provided at basement with acoustic enclosures with height of chimney 6 m above roof level or as specified by PCC and Pollution control device has been installed thereby reducing 75% of emissions.

The waste water generated is of domestic and is been treated and reused in cooling, irrigation and flushing purposes. The test reports from MoEF approved laboratory has been attached.

# Up-to-date expenditure(till March 2022) on different items of EMP and plan for next two years is mentioned as below

л.	-	ne	347	 -	
-				 8.5	

SL.No	Items	Expenditure till date		Proposed Budget estimates for next two years		Basis of recurring Cost
		Recurrin g in Rs.	Non- recurring in Rs.	Recurring in Rs.	Non- Recurri ng in Rs.	
a)	Air pollution control measures	11.722 Lacs	115,68 lacs	2.5 lac	325 lacs	Monitoring cost
b)	Water Pollution control measures	211.312 lacs	38.144 Lacs	43 Lacs	nil	Manpower / operation & maintenance cost of STP, oil & grease traps
c)	Noise pollution control measures	4.732 Lacs	25 Lacs ( Accoustic enclousre DG set)	0.94 Lacs	Nil	Monitoring & maintenance of accoustic enclosure
d)	Monitoring	29.518 Lacs	Nil	3.8 Lacs	Nil	Monitoring cost of air, water, noise, soil, stack & STP
e)	Rain Water Harvesting	53.40 Lacs	61 Lacs	11.32 Lacs	12.5 lacs	Maintenance of harvesting pits, upkeep / maintenance of storm water channels
n	Green Belt	262.68 Lacs	204.43 Lacs	80 Lacs	40 Lacs	Upkeep & maintenance of Green Belt and addition of plantation, development of Jamunwala park, Saket, New Delhi

g) .	Fire Management	632.156 Lacs	853.63 Lacs	148.89 Lacs	150 lacs	Manpower , operation & maintenance and upgradtion of Fire Management System
h) -1	Miscellaneous (a)- Audits and training - Energy , Fire & Safety, IMS (ISO- 9001, ISO 14001 & OHSAS - 18001, ISO50001 .	78.75 Lacs	8 lakh	11.858 Lacs	nil	Audit Expense
h)-2	Miscellaneous-Solar Lighting /Solar water heating system	8.84 Lacs	19.6 Lacs	2 Lac	65 lakh	Maintenance of solar lighting and solar water heating system
h)-3	Miscellaneous - Solid Waste Management	40.46 lacs	20,99 lacs	21.88 lacs	nil	Procurement of OWC, Waste to energy plant

#### PART-1

Miscellaneous: Any other particulars in respect of environmental protection and abatement of pollution.

### GREEN BELT DEVELOPMENT(Till March 2022):

S.No.	Year	Area Covered	No. of plants planted	Species of plants planted
1	2008-10	Indoor Plants	600 plants	Arica palm, jed plant, dry cina, royal palm, luca, pansatia, rafish palm, ascodium, zanadu etc etc
2	2008-10	8290 Sq Mtr, Open plaza area	328 plants of different varietes & varoius others ground coverage plants	Ficus Benjamina
				Magnolia champaca ( champa )
				Date Palm ( khajoor )
				Foxtail Palm
				Fishtail Palm
				Rubber Tree
				Bottle brush plant
				Herbaceous plant (Banana Tree )
				Ficus
3	2008-10	Complete Development of DDA	168 plants of different varietes	Magnolia champaca ( champa )

		park		
				Ficus Benjamina
				Bottle brush Plant
				Hyophorbe lagenicaulis ( Bottle Palm )
				Azadirachta Indica (Neem )
4	Aug-10	DDA Park	600 Plants	Black Ficus
7	riug-10	DUATEIN	OUU Flamo	Didon 11000
5	Mar-11	Drop Off Point Open Plaza	55 Plants	Bamboo
6	Mar-11	Drop Off Point Open Plaza	50 Plants	Ficus Panda
7	May-11	Rear Side of Mail	grass cover in 168m2 area	Grass
	- All	I FACCACIO	2	West-today to grown
8	Aug-11	Plaza	4	Washingtonian 5' - 6.' Ashoka Tree 6' - 7'
9	Aug-11	Rear side of Mall	50	
10	Aug-11	DDA Park	350	Ficus 8' - 10' Golden Panda 4' - 5'
11	Nov-11	Rear Side of Mall & DDA Park	20000	Enermy 12"
13	Nov-11	DDA Park	25	Neem 4' - 5'
14	May-12	Front side of the mall	800 Plants	Ficus 4' - 8'
15	May-12	Front side of the mall	20000 sq ft of grass cover	Grass
16	Sep-12	DDA Park/Plaza	300	Ficus Panda
17	Sep-12	Plaza	22	Ficus Starlike
18	Sep-12	Mail area/Plaza	175	Ficus
19	Sep-12	Mall area/ Basement	150	Arika Palm
20	Sep-12	DDA Park	1000	Rose
21	Sep-12	DDA Park/Plaza	100	Raat Ki Rani
22	Sep-12	DDA Park/Plaza	1000	Hibiscus
23	Oct-12	DDA Park	1000	Bougenvilla
24	Oct-12	DDA Park	500	Enermy 12"
25	Jul-13	DDA Park	200	Ficus 3' - 4'
26	Jul-13	DDA Park	25	Azadirachta Indica 5' - 6"
27	Jul-13	DDA Park	500	Tikoma Gaudi Chaudi 4' - 5'
28	Jul-13	DDA Park	500	Hibicus 2' 3'
29	Jul-13	DDA Park	500	Bougenvilia 2' - 3'
30	Jul-13	DDA Park	10000	Enermy 12"
31	May-14	DDA Park/Plaza	200	Bougainvillea-2'
32	May-14	Plaza	800	Denali-8"
33	Dec-14	Terrace area	10	Ficus Reginald-9'-10'
34	Dec-14	Terrace area	6	Bougainvillea-6'-8'
35	Dec-14	Terrace area	30	Bougainvillea-2'-3'
36	Dec-14	Rear Side of Mall/Terrace area	61	Plumeria alba (Champa)-10'-12'
37	Dec-14	DDA Park/Plaza	11	Washington Philiphons-8'-10'

38	Jan-15	DDA Park/Plaza	23	Ficus 9'-10'	
9	Jan-15	Open Terrace area	6	Bougenvilla 4' - 5'	
40	Jan-15	DDA Park	1	Bottle brush plant-6'-8'	
41	Jan-15	Open Terrace area/DDA Park	15	Plumeria alba (Champa)-10'-12'	
42	Jan-15	DDA Park	1	Hibiaus 3-4'	
43	Jan-15	Rear Side of Mall	2	Rafish palm-2'-3'	
44	Jan-15	Rear Side of Mall/DDA Park	2	Drycina(Green)6	
45	Jan-15	Open Terrace area/DDA Park	5	chinese palm	
46	Jan-15	Rear Side of Mail/DDA Park	5	Jed plant	
47	Jan-15	DDA Park	1	Arica palm	
48	Jan-15	Open Terrace area/Plaza	17	Phoenix plant	
49	Jan-15	Open Terrace area	1	Pedilanthus plant-6"-8"	
50	Jan-15	Open Terrace area/DDA Park	9	Spray grass-2"-3"	
51	Dec-15	Back side of the mall	100	Ficus 4'-5'	
52	Dec-15	DDA Park	30	Ficus 5'-6'	
53	Mar-16	Mall staircase area	200	Arika Palm	
54	Sep-16	DDA Park	70	Bougainvillea-2'-3'	
55	Sep-16	DDA Park	200	Ficus Panda 9"-12"	
56	Sep-16	DDA Park/1st Floor	400	Enermy 12"	
00	3ep-10	SDMC( JAMUN	5	Plumeria alba (dwarf) 18" pot (10' Ht. 150mm Girth- 2 Mts	
57	Mar-17	WALA PARK)		canopy)	
		SDMC( JAMUN	15	Bottle palm 6' 7' ht stem (6'-7' stem Ht. 450mm	
58	Mar-17	WALA PARK)	4.5	Girth- 2 Mts canopy)	
59	Mar-17	SDMC( JAMUN WALA PARK)	15	Cycus palm	
60	Mar-17	SDMC( JAMUN WALA PARK)	21	Fish tail palm	
61	Mar-17	SDMC( JAMUN WALA PARK)	35	Pheorix palm 1' - 2' ht stem (Phoenix roebelleni 1'-6" stem Ht. 150mm Girth- 1.5 Mts canopy)	
0.1	IVIDS-17	SDMC( JAMUN	5	Cycus Cersanalasis	
62	Mar-17	WALA PARK)	2	( Ravina Palm)	
63	Mar-17	SDMC( JAMUN WALA PARK)	7	Caryota Mitis	
64	Mar-17	SDMC( JAMUN WALA PARK)	50	Leropetnun	
65	Mar-17	SDMC( JAMUN WALA PARK)	30	Rapis Palm ( 2.5 ft ht)	
66	Mar-17	SDMC( JAMUN WALA PARK)	30	Rapis Palm ( 4 ft ht)	
67	Mar-17	SDMC( JAMUN WALA PARK)	5	Nolina	
68	Mar-17	SDMC( JAMUN WALA PARK)	5	Adenium	
69	Mar-17	SDMC( JAMUN	6	Yuca Elegance	

		WALA PARK)			
70	Mar-17	SDMC( JAMUN WALA PARK)	12	Silver yucca 14" pot (2' Ht.)	
10	Mat-17	VVALA PARK)	30	Juniperous orientalis	
		SDMC(JAMUN	220	4' to 5' ht (4'-5' Ht. well	
71	Mar-17	WALA PARK)		shaped)	
-	111395 1.1	SDMC( JAMUN	12	Furcuria 14" pot	
72	Mar-17	WALA PARK)	NAME OF THE PARTY	(Furcaerea 2"-6" dia.)	
		SDMC( JAMUN	20	Ficus Panda	
73	Mar-17	WALA PARK)	2000	130000000000000000000000000000000000000	
1.11	200000000	SDMC( JAMUN	15	Podo carpus	
74	Mar-17	WALA PARK)			
	West 25%	SDMC(JAMUN	200	Ixora	
75	Mar-17	WALA PARK)	557001	11-1,000	
	1284 600	SDMC( JAMUN	300	chandni	
76	Mar-17	WALA PARK)	3.060		
	WAR BOW	SDMC( JAMUN	500	boxes	
77	Mar-17	WALA PARK)	-	WAR BUILDING STREET	
20257	92250526	SDMC( JAMUN	50	chinese caronda	
78	Mar-17	WALA PARK)		Town do	
70	19925039000	SDMC(JAMUN	100	kevada	
79	Mar-17	WALA PARK)	20	umberalla palm	
P.C	1800 670	SDMC(JAMUN	20	umperana pam	
80	Mar-17	WALA PARK) SDMC( JAMUN	600	dynella	
04 14 17	WALA PARK)	000	dynesia		
81	Mar-17	SDMC( JAMUN	100	pittospera	
82	Mar-17	WALA PARK)	100	phtospere	
02	Tright-17	SDMC( JAMUN	15	Topiary Casurina/ficus	
83	Mar-17	WALA PARK)	100	panda/	
99	100001512	SDMC( JAMUN	15	Weeping willow	
84	Mar-17	WALA PARK)	0/75		
-		SDMC( JAMUN	15	Bottle brush	
85	Mar-17	WALA PARK)		100000000000000000000000000000000000000	
	A14000111011	SDMC( JAMUN	5	Kathal Champa	
86	Mar-17	WALA PARK)			
and the same	The second	SDMC( JAMUN	15	Lyrata compacta	
87	Mar-17	WALA PARK)	991	FeWares Allega	
	The second store	SDMC( JAMUN	15	Plumerai Alba	
88	Mar-17	WALA PARK)	-	Control of the contro	
	40	SDMC( JAMUN	5	Brachichitan	
89	Mar-17	WALA PARK)	40	Accacia auriculiformis 5'	
			10	to 6' ht (Acacia	
				auriculiformis 5'-6' Ht.	
		SDMC( JAMUN		Girth 60mm Canopy	
90	Mar-17	WALA PARK)		1 Mt.)	
20	mpt-17	SDMC(JAMUN	5	Michalia Champa	
91	Mar-17	WALA PARK)	177		
21	Tital Street	7.77,786.3.7.12.753.30	10	Ficus nerifolia 4' to 5' ht	
		SDMC(JAMUN	11 2075	(4'-5' Ht. Girth 50mm	
92	Mar-17	WALA PARK)		Canopy 0.6 Mt.)	
	1 - 10 - 20 -		15	Alstonia scholoris 7' to 8'	
			1.083	ht (Alastonia scholaris	
	TOUGH SHEET	SDMC( JAMUN		7'-8' Ht. Girth 100mm	
93	Mar-17	WALA PARK)		Canopy 1.5 Mt.)	

94	Mar-17	SDMC( JAMUN WALA PARK)	5	Neem	
95	Mar-17	SDMC( JAMUN WALA PARK)	235	F.Benjamina (dark green leaf) 5' to 6' ht (5'-6' Ht. Girth 60mm Canopy 1 Mt.)	
96	Mar-17	SDMC( JAMUN WALA PARK)	5	Ficus decora	
97	Mar-17	SDMC( JAMUN WALA PARK)	12	F.retusa 5' to 6' ht (Ficus retusa5'-6' Ht. Girth 100mm Canopy 1.5 Mt.)	
98	Mar-17	SDMC( JAMUN WALA PARK)	12	Ashok (desi) 7' to 8' ht (7'-8' Ht. Girth 60mm Canopy 1 Mt.)	
99	Mar-17	SDMC( JAMUN WALA PARK)	30	Bamboo multiplea	
100	Mar-17	SDMC( JAMUN WALA PARK)	50	Bamboo yellow 8' to 10' ht (8'-10' Ht.)	
101	Mar-17	SDMC( JAMUN WALA PARK)	15	Buddha bally bamboo 6' to 7' ht (6'-7' Ht.)	
102	Mar-17	SDMC( JAMUN WALA PARK)	15	Giant bamboo	
103	Mar-17	SDMC( JAMUN WALA PARK)	4000	Shrubs	
104	Mar-17	SDMC( JAMUN WALA PARK)	14000	Ground cover	
105	Apr-17	Rear Side of Mall	90	RAPHIS PALM 3'-4'	
106	Apr-17	Rear Side of Mall	70	ARECA PALM 4'-5'	
107	Apr-17	Rear Side of Mall	500	DINAELIA VARIEGATED	
108	Apr-17	Rear Side of Mall	200	Brassisa	
109	Apr-17	Rear Side of Mall	200	sefhlera	
110	Apr-17	Rear Side of Mall	200	sefnlera green	
111	Apr-17	Rear Side of Mall	200	Drenna rosay	
112	Dec-17	Rear Side of Mall	150	RAPHIS PALM 3' -4'	
113	Jan-18	Plaza area	250	RAPHIS PALM 3'-4'	
114	May-18	Plaza area	100	Bougainvillea 3-4 ft in 16" pot	
115	May-18	Plaza area	200	Ixoag Singapuria Red flower , 1.5" height	
116	May-18	Plaza area	200	Hybrid Roses bunch flower, with 8" pot	
117	May-18	Plaza area	5000	Elorodendan Enermy	
118	May-18	Plaza area	2000	Erenthemum	
119	May-18	Rear Side of Mall	125	RAPHIS PALM 3' -4'	
120	Jul-18	SDMC( JAMUN WALA PARK)	4500sqft	Grass (selection No.1)	
121	Jul-18	SDMC( JAMUN WALA PARK)	100	Hybrid Roses bunch flower, with 8" pot	
122	Jul-18	SDMC( JAMUN WALA PARK)	600	Green wall plants	
123	Aug-18	DDA Park	50	Golden Panda 1'-2'	
124	Nov-18	Distribution	150	Herbal (indoor air purifying)	

125	Nov-18	DDA park	500	Rose with 1 feet height
126	Nov-18	Plaza	100	Poinsettia with 8" pot
127	Nov-18	Plaza	400	Earthern Pot (clay ) 8" Dia
128	Nov-18	Opposite Gate no 2	3000	Good Earth (one truck having 600 cfeet)
129	Jan-19	DDA park	500	Rose plant
130	Jan-19	Plaza	600	Earthern Pot (clay ) 8" Dia
131	Jan-19	Opposite Gate no 2	3000	Good Earth
132	Jul-19	Plaza area	200	Tikoma Gwaraf 1'.5"-'2'.5"
133	Sep-19	SDMC( JAMUN WALA PARK)	105	Tikoma Gaudi Chaudi 1'
134	Sep-19	SDMC( JAMUN WALA PARK)	17	Neem 1-'2'
135	Sep-19	SDMC( JAMUN WALA PARK)	7	Aam Tree 2' - 3'
136	Sep-19	SDMC( JAMUN WALA PARK)	6	Jamun Tree 2' - 3'
137	Oct-19	SDMC( JAMUN WALA PARK)	16	Hibicus 3'-4'
138	Oct-19	SDMC( JAMUN WALA PARK)	200	Bougenvilia 2' - 3'
139	Oct-19	Rear Side of Mall ( Gate No.02)	170	Tikoma Gaudi Chaudi 1'
	CALL PROPERTY.	Plaza area (water		Tikoma Gaudi Chaudi 1'
140	Oct-19	body)	150	(In the latest and lat
141	Nov-19	DDA Park	25	Hibiscus-1'-2'
142	Nov-19	DDA Park	30	Ficus Panda-1'-2'
143	Dec-19 to Feb-2020	Plaza area and DDA Park	1390	Calendula
144	Dec-19 to Feb-2020	Plaza area and DDA Park	1470	Salvia
145	Dec-19 to Feb-2020	Plaza area and DDA Park	2000	Babuna
146	Dec-19 to Feb-2020	Plaza area and DDA Park	800	Cinneneria
147	Dec-19 to Feb-2020	Plaza area and DDA Park	707	Dianthus
148	Dec-19 to Feb-2020	Plaza area and DDA Park	1280	Ice flower
149	Dec-19 to Feb-2020	Plaza area and DDA Park	1150	Phlox
150	Dec-19 to Feb-2020	Plaza area and DDA Park	421	Stock
151	Dec-19 to Feb-2020	Plaza area and DDA Park	430	Marigold
152	Dec-19 to Feb-2020	Plaza area and DDA Park	250	Hollyhocks (alcea rosea)
153	Dec-19 to Feb-2020	Plaza area and DDA Park	452	Dahlia double
154	Dec-19 to Feb-2020	Plaza area and DDA Park	1150	Dahlia single
155	Dec-19 to	Plaza area and DDA	4000	Alyssum

	Feb-2020	Park		
156	Dec-19 to Feb-2020	Plaza area and DDA Park	200	Kale
157	Dec-19 to Feb-2020	Plaza area and DDA Park	180	Marigold jafri
158	Dec-19 to Feb-2020	Plaza area and DDA Park	400	Guldavri single
159	Dec-19 to Feb-2020	Plaza area and DDA Park	125	Guldavri double
160	Dec-19 to Feb-2020	Plaza area and DDA Park	320	Straw
161	Dec-19 to Feb-2020	Plaza area and DDA Park	841	Gazania
	Dec-19 to	Plaza area and DDA Park	134	Sweet William
162	Feb-2020 Dec-19 to	Plaza area and DDA	150	kalanchoe
163	Feb-2020 Dec-19 to	Park Plaza area and DDA	800	Antirrhinum (dog flower)
164	Feb-2020 Dec-19 to	Park Plaza area and DDA	525	Pansy
165	Feb-2020 Dec-19 to	Park Plaza area and DDA	2740	Petunia
166	Feb-2020	Park		Poinsettia with 6" pot
167	Dec-19	Inside mall	200	The state of the s
168	Feb-20	Plaza area	500	Dahlia double hybrid
169	Apr-20	Plaza area and DDA Park	500	Sadabahar
170	Apr-20 to July -20	Plaza area and DDA Park	1700	Kochia
171	Apr-20 to June -20	Plaza area and DDA Park	1200	Zinia
172	Apr-20 to June -20	Plaza area and DDA Park	900	Sunflower
173	Apr-20 to June -20	Plaza area and DDA Park	700	Cosmos
174	Jun-20	Plaza area	115	Acalypha
175	Jul-20	DDA Park	120	Ficus
176	Aug-20	Plaza area	500	Tikoma Gaudi Chaudi 1'
177	Aug-20	DDA Park	40	Money plant
178	Aug-20	DDA Park	35	Hibiscus-1'-2'
179	Sep-20	DDA Park	110	Jatropha
180	Nov-20	SDMC( JAMUN WALA PARK)	500	Tikoma Gaudi Chaudi 1'
181	Nov-20	DDA Park	200	Tikoma Gaudi Chaudi 1'
182	Nov-20	DDA Park	240	Ficus Panda
	Nov-20 to	Plaza area and DDA	136500	Guldwari flower
183	Mar 21	Park	600	DOOR CARDING ADMINISTRA
184	Nov-20 to Mar 21	Plaza area and DDA Park	4500	Elasium flower
185	Nov-20 to Mar 21	Plaza area and DDA Park	2600	Calendula
186	Nov-20 to Mar 21	Plaza area and DDA Park	550	Gazania
187	Nov-20 to Mar 21	Plaza area and DDA Park	1400	Salvia

188	Nov-20 to Mar 21	Plaza area and DDA Park	1000	Stock	
- 66	Nov-20 to	Plaza area and DDA	2220	Marigold	
189	Mar 21 Nov-20 to	Park Plaza area and DDA	300	Dahlia double	
190	Mar 21 Nov-20 to	Park Plaza area and DDA	700	Dania dodole	
191	Mar 21	Park	2000	Pitonia	
192	Nov-20 to Mar 21	Plaza area and DDA Park	500	Antirrhinum (dog flower)	
5020	Nov-20 to	Plaza area and DDA	SEXTE	Babuna	
193	Mar 21	Park	200		
194	Nov-20 to Mar 21	Plaza area and DDA Park	600	Cinneneria	
195	Nov-20 to Mar 21	Plaza area and DDA Park	800	Sweet William	
196	Nov-20 to Mar 21	Plaza area and DDA Park	500	Dianthus	
197	Nov-20 to Mar 21	Plaza area and DDA Park	1500	Ice flower	
198	Nov-20 to Mar 21	Plaza area and DDA Park	200	Pansy	
199	Nov-20	Inside mall	200	Poinsettia with 8" pot	
200	Dec-20	Inside mall	200	Poinsettia with 8" pot	
201	Feb-21	plaza area	400	Dahlia double	
202	Mar-21	DDA Park	200	Pansy	
203	Mar-21	DDA Park	375	Bimca	
204	Mar-21	plaza area	400	Celosia	
205	Mar-21	plaza area	350	Tikoma hybrid	
206	Apr-21	Plaza area and DDA Park	2500	Kochia	
207	Apr-21	Plaza area and DDA Park	400	Zinia	
208	Apr-21	Plaza area and DDA Park	600	Sunflower	
209	Apr-21	Plaza area and DDA Park	300	Cosmos	
210	Apr-21	Plaza area and DDA Park	200	Porttaloca	
211	Apr-21	Plaza area and DDA Park	100	Caladium	
212	Apr-21	Plaza area and DDA Park	150	Gumfrina	
2002	1 3 30	Plaza area and DDA		22.12	
213	Apr-21	Park	500	Gladia	
214	Apr-21	Plaza area and DDA Park	300	Sadabhar	
215	Apr-21 to July-21	Plaza area and DDA Park	80	Aglonima	
216	Apr-21 to July-21	Plaza area and DDA Park	170	Aklifa	
217	Apr-21 to July-21	Plaza area and DDA Park	120	Enermy	
218	Apr-21 to July-21	Plaza area and DDA Park	500	Desi Ticoma	

219	Apr-21 to July-21	Plaza area and DDA Park	100	Panda
220	Apr-21 to July-21	Plaza area and DDA Park	51	Hibiscus
221	Apr-21 to July-21	Plaza area and DDA Park	200	Laisa
222	Apr-21 to July-21	Plaza area and DDA Park	150	Tulsi plant
223	Apr-21 to July-21	Plaza area and DDA Park	50	Money plant
224	Jun-21	Green wall	70	Money plant
225	Jun-21	Green wall	160	Clorofythem
226	Jun-21	Green wall	50	Dry sena compatta
227	Jun-21	Green wall	108	Song of india green
228	Jun-21	Green wall	155	Song of india berygrater
229	Jun-21	Green wall	51	Money plant
230	Jun-21	Green wall	80	synghoniyam
231	Jul-21	Green wall	102	Money plant
232	Jul-21	Green wall	253	Song of india Green
233	Jul-21	Green wall	200	Song of india berigate
234	Sep-21	Green wall	32	Song of india Green
235	Sep-21	Green wall	114	Song of india berigate
236	Sep-21	Green wall	27	Safrela
237	Sep-21	Green wall	6	Money plant
238	Sep-21	Green wall	4	Caclore faidam
239	Sep-21	Green wall	3	Shewlam
240	Sep-21	Green wall	26	Faran
241	Sep-21	Green wall	150	Money plant
242	Oct-21	Green wall	110	Song of india Green
243	Oct-21	Green wall	135	Song of india berigate
244	Oct-21	Green wall	50	Shewlam
245	Oct-21	Green wall	100	Money plant
246	Oct-21	Green wall	50	synghoniyam
247	Oct-21	Green wall	210	Money plant

(Signature of a posse) danying out an Industry - operation or process)

Name: Mr. Shashi Sharma

Designation: Director - Operations & Projects

Address: A-3, District Center, Saket, New Delhi-110017

PH NO.: +91 4114211 4211 FAX: +91 11 42114222

Mob. +91 9654339933

EMAIL: shashis@selectcitywalk.com





SIPL/Engg/22-23/001

To

The Member Secretary

DPCC

Dept. of Environment (Govt. of NCT of Delhi)

6th April 2022

(ENQUIRY COUNTER)

DELHI POLLUTION CONTROL COMMITTEE
DEPARTMENT OF ENVIRONMENT
GOVT. OF NOT OF DELHI
4TH PLOOR, ISBT BUILDING,
KASHMERE GATE, DELHI-110006

Sub: Submission of Form No. 04 with respect to Annual return of used lube oil for the year 2021-22.

Dear Sir,

Kindly find attached the Form No. 10 with respect to disposal of used Lube Oil. The details of the same are mentioned as below:-

1260 L disposed off to Bharat Oil and Waste Management Ltd., Plot no. 672.
 Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 08.10.2021.

Form 10 for the same have already been submitted to DPCC on regular intervals. However the copy of the same has been attached for your reference.

Thanking you,

Yours truly,

For Select Infrastructure Pvt. Ltd.

Shashi Sharma

Director- Operations & Projects

Enclosures

1. Form - 4

2. Form - 10 (8th October 2021)

#### FORM 4

[See rules 6(5), 13(8), 16(6) and 20 (2)]

#### FORM FOR FILING ANNUAL RETURNS

[To be submitted to State Poliution Control Board by 30<sup>th</sup> day of June of every year for the preceding period April to March)

- 1. Name and address of facility: \_ [LECT\_INFRASTRUCTURE\_PVT\_LTD. ( SELECT\_C177\*\*\*\*\* ) A-3, DISTRICT CEMBE SAKET, NEW BELLI - 110017
- 2. Authorisation No. and Date of issue: NIA
- 3. Name of the authorised person and full address with telephone, fax number and e-mail SHACH? CHACHER shashis Cocketerty walk som

# -1:563391

4. Production during the year (product wise), wherever applicable

#### Part A. To be filled by hazardous waste generators

- 1 Total quantity of waste generated category wise . 12.60 LTRS
- Quantity dispatched
  - to disposal facility USED LUBE OIL OF DG SETS CATEGORY 5.1
  - to recycler or co-processors or pre-processor 12.60 LTRS
  - (111)
- 3. Quantity utilised in-house, if any N/A
- 4. Quantity in storage at the end of the year A/A

### Part B. To be filled by Treatment, storage and disposal facility operators

- Total quantity received -
- Quantity in stock at the beginning of the year -
- Quantity treated —
- Quantity disposed in landfills as such and after treatment —
- Quantity incinerated (if applicable) -
- Quantity processed other than specified above -
- 7. Quantity in storage at the end of the year -

#### Part C. To be filled by recyclers or co-processors or other users

- Quantity of waste received during the year N/A
  - (i) domestic sources
  - imported (if applicable) (ii)
- Quantity in stock at the beginning of the year -

- 3. Quantity recycled or co-processed or used -
- 4. Quantity of products dispatched (wherever applicable) -
- 5. Quantity of waste generated -
- 6. Quantity of waste disposed -
- 7. Quantity re-exported (wherever applicable)-
- 8. Quantity in storage at the end of the year -

Signature of the Occupier

Operator of the disposal facility

Date 6. APRIL 2022

Place MEH. ACLUI







SIPL/Engg/21-22/027

To
The Member Secretary
DPCC
Dept. of Environment (Govt. of NCT of Delhi)

13th October 2021

DELHI POLLUTION CONTROL COMMITTEE

DEPAITMENT OF NOT OF DELHI

4111 FLOOR, ISBN BURDING,
KASHMERE GATE, DELHI 110008

Sub: Submission of Form No. 10 with respect to disposal of used lube oil.

Dear Sir,

Kindly find attached the Form No. 10 with respect to disposal of used Lube Oil, Oil filters and used cloth. The details of the same are mentioned as below:-

 1260 Ltrs used oil, 106 Nos. filters and 1 Kg used solled cloth disposed off to Bharat Oil and Waste Management Ltd., Plot no. 672, Sikandra Road, NH-2, Kumbhi Village, Tehsil Akbarpur, Kanpur- Dehat (UP) on 08.10.2021.

The firm to which we have disposed off the used lube oil is State Pollution Control board / Central Pollution control board authorized recyclers.

Thanking you,

Yours truly,

For Select Infrastructure Pvt. Ltd.

Shashi Sharitia Director- Operations & Projects

12/1-14 13/1-14



(See rule 19 (1))

Occupier's Copy

5.No.: 55007 MANIFEST FOR HAZARDOUS AND OTHER WASTE Occupier's Name & Mailing Address (including Phone No. and email) 2 Sender's Authorization No. Manifest Document No. Transporter's Name & Address (including Phone No. and email) (Truck / Tanker / Special Vehicle) Type of Vehicle Transporter's Registration Vehicle Registration No. BHARAT OIL COMPANY (I) REGD. Receiver's Name & Mailing Address E-18, Site-IV, Sahibabad Industrial Area. (including Phone No. and email) Ghazlabad, UP-201010 Tel.: 0120-4107824. e-mail:seles@bharatoil.com BHARAT OIL & WASTE MANAGEMENT LTD. (II) BHARAT OIL & WASTE MANAGEMENT LTD. Plot # 672, Sikandra Road, NH-2: Kumphi Visage. Mauza Mukimpur, Roorkee-Lakshar Road, Tehsil Akbarpur, Kanpur Dehat, UP, Tel: 0512-2285298 Roorkee - 247864 UK, Tel.: 08874207664 o-mail:sales@bharatoil.com e-mail:sales@bharatoll.com (I) 1485/UPPCB/Ghasisbas/UPPCBROJHWM/GHAZ/ABAD/2018 Volid upto: 83/05/2013 9 Receiver's Authorization No. (FR)1662/UPPCIXKaspurDehat/UPPCBROykWAN/CAMPUR DENAT/(616 Valid upto:3664/2023 (ii) UEPPCB/HO/Con-B-\$4/2018/548 Valid upto: 31/03/2023 10 Waste Description 11 Total Quantity No. of Containers (Solid/Semi-Solid/Sludge/Qily/Tarry/Slurry/Lightil) 12 Physical Form Do not throw Drums from truck, in case of leakage/ 13 Special Handling Instructions & Additional scapege, use Washing soap at point of leak to stop its Information leekege. hereby declare that the contents of the consignment are fully and accurately 14 SENDER'S CERTIFICATE described above by proper shipping name and are categorised packed, marked, and tabeled, and are in all respects in proper condition for transport by road Typed Name & Stamp: Signature: MJ. MASHOODVE JOBAL Year Month Day Vear Month Day 15 Transporter Acknowledgement of Receipt of Waste Typed Name & Stamp : Signature: 16 Receiver's Certificate for Receipt of Hazardou other Waste Day Year Month Typed Name & Stamp : Signature:

WTS - 458/0

Date & Rev F-23-7502 Page, 1 of 1	18.12.08 & 00	G	ATE PASS		File .
Lice, _oe's Unit No.:_		17 Nove: 09,	AA <c58781d12< td=""><td>2 185460</td><td>CITYWALK</td></c58781d12<>	2 185460	CITYWALK
To . Vendor Nar Address : _	ne: Blaratoil 4 Khaniki Villy	Date Mary	neur Lth Dúthar	Time : Non-Returna	_13-0 krr ible ⊅Returnable □
PER PROPERTY.	Used oil	126-		Modern	Tale sert
L	VACE diecord	The second secon	the state of the s		to DPCC
	LA Air Filter	And the second of the latest designation of			autorised
	DCANT			H WE HOU	vendorfor
0	Use L Chap	t. Ly			Links org.
4	All gate Passes Should Copy of DC to be depo Attach Separate list for	alted Milhi security of additional Jacos.	linery Challaris duly Signer	SEC S. NO.1 S. NO.1 DATE	222

101 901



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognized By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1988) (No. Q - 1508 / 32 / 2007 - CPW)

(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September - 2022)

Client De	talls		Sample Details	
Name	M/s. Select Citywalk Mall a unit of Select Infrastructure Pvt. Limited Select Infrastructure Pvt. Ltd., Select Citywalk, A-3, District Centre, Saket, New Delhi – 110017		Sample Code	GCI/22/I20/WW2
Address			Batch/Location	STP Outlet
Sampling	Done By	Operator	Quantity	1000 ml
Analysis :	Starts on	18/09/2022	Date of Sampling	16/09/2022
Analysis (	Completion On	21/09/2022	Sampling Instrument	Manual Sampler
Sampling	Method	APHA 1060	Sample Received Date	18/09/2022

#### WASTE WATER ANALYSIS RESULTS

Sr. No.	Parameters	Unit	Results	DPCC Standard	Reference Method
1.	рН	8	7.69	5.5 - 9.0	APHA 4500
2.	Total Suspended Solids	mg/L	19	30	APHA 2540 D
3.	Chemical Oxygen Demand	mg/L	43	250	APHA 5220
4.	Biochemical Oxygen Demand (3 days at 27 °C)	mg/L	.6	20	APHA 5210
5	Oil & Grease	mg/L	1.1	10	APHA 5520
6.	Phosphate	mg/L	0.58	5.0	APHA 4500 - P
7,	Nitrate Nitrogen	mg/L	2.4	10	APHA 4500 - NORG-E
8.	Fecal Coliforns	MPN/100 ml	110	<230	APHA 9221 - E
9)	Ammonical Nitrogen	mg/L	2.8	50	APHA 4500 - NH <sub>3</sub>

**BDL: Below Detectable Level** 

ND: Not Detectable



#### **Authorized Signatory**

Analysis is subject to the condition in Which the Sample is received at our Laboratory.

Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.

Sample will be retained till 15 days from the date of sampling.





(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/21/5P/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Details			Sample Details		
Name	M/s. Select Citywalk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/22/I20/AA1 & AA2	
Select Infrastructure Pvt. Ltd., Select		Location	As PerTable		
Address	Citywak, A-3, District Centre, Saket,		Quantity	NA.	
	New Delhi - 1	10017	Date of Sampling	15/09/2022	
Sampling	Done By	Mr. Kartik	Sampling Instrument	RDS, FPS	
Analysis Starts on		17/09/2022	Sampling Method	IS 5182 ; Part 5 : 1975	
Analysis C	Completion On	21/09/2022	Sample Received Date	17/09/2022	

#### AMBIENT AIR MONITORING RESULTS

			Res	ults	60 HOLES TO	
Sr. No.	Parameters	Unit	Near Main Gate	Back Side (Near STP)	Permissible Limit as per NAAQS	Reference Method
1.	Particulate Matter (PM10)	µg/m³	62.6	64.6	100	IS 5182 : Port 23 : 2006
2.	Particulate Matter (PM2.5)	µg/m³	24.9	26.9	60	IS 5182 : Part 24 : 2019
3.	Sulfur Dioxide (SO <sub>2</sub> )	µg/m³	7.6	8.2	80	IS 5182 : Part 2 : 2001
4.	Oxides of Nitrogen(NOx)	µg/m³	12.1	13.1	80	IS 5182 : Part 6 : 2006
5.	Carbon Monoxide CO	mg/m³	0.26	0.34	2.0	IS 5182 : Part 10 : 1999
6.	Ozone as O <sub>3</sub>	µg/m³	<20	<20	100	NAAQS Guidelines
7.	Lead as Pb	µg/m³	<0.05	<0.05	1.0	NAAQS Guidelines
8.	Nickel as Ni	ng/m³	<1.0	<1.0	20	NAAQS Guidelines
9,	Arsenic as As	ng/m³	<0.5	<0.5	6.0	NAAQS Guidelines
10.	Ammonia as NH3	µg/m³	<20	<20	400	NAAQS Guidelines
11.	Benzene , C₀H₅	µg/m³	<0.5	<0.5	5.0	IS 5182 (Part 11):2006
12.	Benzo (a) Pyrene	ng/m³	<0.05	<0.05	1.0	Gas Chromatography



- Analysis is subject to the condition in Which the Sample is received at our Laboratory.
- Reports cannot be used as evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.





(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/21/5P/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

#### (For the Month of September-2022)

Client Dete	alls		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/22/I20/AA3
	Select Infrastr	ructure Pvt. Ltd.,	Location	As PerTable
Address	Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Quantity	NA .
			Date of Sampling	15/09/2022
Sampling	Done By	Mr. Kortik	Sampling Instrument	RDS, FPS
Analysis St	tarts on	17/09/2022	Sampling Method	IS 5182 : Part 5 : 1975
Analysis C	ompletion On	21/09/2022	Sample Received Date	17/09/2022
and the second second second second	the first term and the second	The state of the s	A CONTRACTOR OF THE PROPERTY O	

#### AMBIENT AIR MONITORING RESULTS

			Results	Permissible	
Sr. No.	Parameters	Unit	New construction area 3rd floor	Limit as per NAAQS	Reference Method
1,	Particulate Matter (PM10)	µg/m³	68.9	100	IS 5182 : Part 23 : 2006
2.	Particulate Matter (PM2.5)	µg/m³	32.6	60	IS 5182 : Part 24 : 2019
3.	Sulfur Dioxide (SO <sub>2</sub> )	µg/m³	8.6	80	IS 5182 : Part 2 : 2001
4.	Oxides of Nitrogen (NOx)	µg/m³	14.8	80	IS 5182 : Part 6 : 2006
5.	Carbon Monoxide CO	mg/m³	0.27	2.0	IS 5182 : Part 10 : 1999
6.	Ozone as Os	µg/m³	<20	100	NAAQS Guidelines
7.	Lead as Pb	µg/m³	<0.05	1.0	NAAQS Guidelines
8.	Nickel as Ni	ng/m <sup>3</sup>	<1.0	20	NAAQS Guidelines
9.	Arsenic as As	ng/m <sup>3</sup>	<0.5	6.0	NAAQS Guidelines
10.	Ammonia as NH <sub>3</sub>	µg/m³	<20	400	NAAQS Guidelines
11.	Benzene , CaHa	µg/m³	<0.5	5.0	IS 5182 (Part 11):2006
12.	Benzo (a) Pyrene	ng/m³	< 0.05	1.0	Gas Chromatography



- Analysis is subject to the condition in Which the Sample is received at our Laboratory.
- Reports cannot be used as evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.



GREEN CIRCLE, INC. Integrated HSEQR Consulting Engineers, Scientists & Trainers

(No. Q - 1508 / 32 / 2007 - CPW) (ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/5P/22-23/5eptember-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Details		Sample Details			
Name	mme M/s. Select City walk Mall a unit of Select Intrastructure Pvt. Limited		Sample Code	GCI/22/I20/ST1	
Select Infrastructure Pvt. Ltd., Select		Batch/Location	As per Table		
Address	The second secon	District Centre, Saket,	Nature of Sample	Stack	
	New Delhi - 1	0017	Sampling Instrument	Stack Manitoring Kill	
Sampling	Done By	Mr. Karfik	Date of Sampling	16/09/2022	
Analysis Starts on Analysis Completion On		17/09/2022	Sampling Method	Isokinetic Sampling, IS:11255, PART	
		na u propinsia	Julia Melliou	1,2,3	
		21/09/2022	Sample Received Date	17/09/2022	

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 1	-
2	Rated Capacity	2000	KVA
3	Date of Manufacturing	09/2007	Month /Yea
(4)	Make	Cummins	19
5	Engine Sr. No.	33161054	19
6	Name of the Plant/Section	DG Room	- 14
7	Normal Operating schedule of the Plant(Hrs/Day)	As & When Required	22
В	Capacity on Sampling Day	980	kW
9	Stack Identification	Stack attached to D.G. Set No. 1	
10	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14:	Fuel Type	H.S.D.	77
15	fuel Consumption	250	Liter/Hr.
16:	Flue Gas Temperature	299	*C
17	Velocity	16.2	m/s
18	Gas Volume	4850	Nm <sup>3</sup> /Hr;
19	Sampling Duration	30	Min.





(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### ANALYSIS REPORT

(For the Month of September- 2022)

Client Details		Sample Defails		
Name	M/s. Select City walk Mall a unit of     Select Infrastructure Pvf. Limited		Sample Code	GCI/22/I20/ST1
Select infrastructure Pvt. Ltd., Select		Batch/Location	As per Table	
Address	City walk, A-3, District Centre, Saket,		Nature of Sample	Stack
	New Delhi - 1	10017	Sampling Instrument	Stack Monitoring Kit
Sampling	Done By	Mr. Kartik	Date of Sampling	16/09/2022
Analysis Starts on 17/09/2022		17/09/2022	Sampling Method	Isokinetic Sampling.IS:11255.PART
		Dim	Sampling manica	1.2.3
		21/09/2022	Sample Received Date	17/09/2022

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	19.5	75	IS 11255: Part 1
2	NOx (as NOz)	ppmv	106.8	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	24.6	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm³	8,9	100	Gas Chromatograph— Flame Ionization Detector

Note: Generator sets commissioning Date – after 01, 07, 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Tried Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thSeptember, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



- Analysis is subject to the condition in Which the Sample is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our pror permission.
- Sample will be retained till 15 days from the date of sampling.





(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: -GCI/V/LAB/G0137/22/5F/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Deta	nils		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/22/I20/S12
was and server	Select infrastructure Pvt, Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 110017		Batch/Location	As per Table
Address			Nature of Sample	Stack
	THE COURT OF	10017	Sampling Instrument	Stack Monitoring Kit
Sampling (	Done By	Mr. Kartik	Date of Sampling	16/09/2022
Analysis Starts on		18/09/2022	Sampling Method	Isokinetic Sampling. IS:11255.PART-1.2.3
Analysis Completion On		21/09/2022		10.11233,73901-1,23
Ariuly als C	21/09/2022		Sample Received Date	18/09/2022

Sr. No.	Particulars	Details	Unit
1	Name Of Emission	D.G. Set 2	
2	Rated Capacity	1010	EVA
3	Date of Manufacturing	09/2007	Month /Yea
4:	Make	Cummins	
5	Engine Sr. No.	25311742	- 6
6	Name of the Plant/Section	DG Room	(6)
7	Normal Operating schedule of the Plant(Hrs/Day)	As & When Required	-
8	Capacity on Sampling Day	534	kW
9	Stack Identification	Stack attached to D.G. Set No. 2	**
10	Material of Stack	Metal	723
11	Stack Height from G.L.	34	Mfr.
12	Diameter of Stack	45	cm
13	Type of Stack	Round	
14	Fuel Type	H.S.D.	
15	Fuel Consumption	130	Liter/Hz
16	Flue Gas Temperature	266	*C
12	Velocity	14.8	m/s
18	Gas Volume	4290	Nm <sup>3</sup> /Hr.
19	Sampling Duration	30	Min



(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: -GCI/V/LAB/G0137/22/5P/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Deto	rils		Sample Details	
Name	M/s. Select City walk Mall a unit of Select Infrastructure Pvt, Limited		Sample Code	GCI/22/I20/S12
\$0£950005	Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket, New Delhi – 170017		Batch/Location	As per Table
Address			Nature of Sample	Stack
			Sampling Instrument	Stack Monitoring Kit
Sampling (	Done By	Mr. Kartik	Date of Sampling	16/09/2022
Analysis Starts on		18/09/2022	Sampling Method	Isokinetic Sampling, IS:11255.PART-1.2.3

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm <sup>3</sup>	14.6	75	IS 11255: Part 1
2	NOx (as NO <sub>2</sub> )	ppmv	88.6	710	IS 11255: Port 7
3.	Carban Monoxide	mg/nm²	29.7	150	Non Dispersive Infrared
4	NMHC (as C)	mg/Nm³	12.6	100	Gas Chromatograph- Flame Ionization Detector

Note: Generator sets commissioning Date – after 01, 07, 2005 [Emission Standards for Diesel Engines [Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9th September, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



- Analysis is subject to the condition in Which the Sample is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained fill 15 days from the date of sampling.





(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LA5/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Deta	ills		Sample Details	
Name		y walk Mall a unit of icture Pvt. Limited	Sample Code	GCI/22/120/513
Select Infrastructure Pvt. Ltd., Select		Batch/Location	As per Table	
Address	City wak, A-3, District Centre, Saket,		Nature of Sample	Stack
	New Delhi - 11	0017	Sampling Instrument	Stack Monitoring Kit
Sampling I	Done By	Mr. Karfik	Date of Sampling	16/09/2022
Analysis \$1	arts on	18/09/2022		Isokinetic Sampling.
Analysis Completion On			Sampling Method	IS:11255,PART-1,2,3
		21/09/2022	Sample Received Date	18/09/2022
7/50		. 2.2	Sample Received Date	18/09/2022

Sr. No.	Particulars	Details	Unit
31	Name Of Emission	D.G. Set 3	100
2	Rated Capacity	1010	KVA
3	Date of Manufacturing	09/2007	Month /Yea
4	Make	Cummins	1.85
5	Engine Sr. No.	25311741	(6)
6	Name of the Plant/Section	DG Room	
7	Normal Operating schedule of the	As & When Required	
8	Capacity on Sampling Day	520	kW
9	Stack Identification	Stack attached to D.G. Set No. 3	-
10	Material of Stack	Metal	
TE	Stock Height from G.L.	34	Mfr.
12	Diameter of Stock	45	cm
13	Type of Stack	Round	i je
14	Fuel Type	H.5.D.	155
15	Fuel Consumption	125	Liter/Hr.
16	Flue Gas Temperature	206	*C
17	Velocity	13.4	m/s
18	Gas Volume	4690	Nm³/Hr.
19	Sampling Duration	30	Min.



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognized By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (No. Q - 1508 / 32 / 2007 - CPW)

(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### ANALYSIS REPORT

(For the Month of September- 2022)

Client Deta	alls		Sample Details	
Name M/s. Select City walk Mall a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/22/120/513	
		icture Pvt. Ltd., Select	Batch/Location	As per Table
Address	City walk, A-3, District Centre, Soket,		Nature of Sample	Stack
	New Delhi - 1	10017	Sampling Instrument	Stack Monitoring Kit
Sampling I	Done By	Mr. Kartik	Date of Sampling	16/09/2022
Analysis St	arts on	18/09/2022	- Contract C	Isokinetic Sampling.
Analysis Completion On		EMALES MANUAL CONTRACTOR OF THE PARTY OF THE	Sampling Method	IS:11255.PART-1,2,3
		21/09/2022	Sample Received Date	18/09/2022

### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1.	Particulate Matter (PM)	mg/nm³	16,7	75	IS 11255: Part 1
2	NOx (as NO <sub>2</sub> )	ppmv	115.6	710	IS 11255; Part 7
3.	Carbon Monoxide	mg/nm³	26.8	150	Non Dispersive Infrared
4.	NMHC (as C)	mg/Nm <sup>3</sup>	8.9	100	Gas Chromatograph- Flame Ionization Detector

Note: Generator sets commissioning Date – after 01, 07, 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9th September, 2002 at serial no. 94, under the Environment (Protection) Act, 1986.)



- Analysis is subject to the condition in Which the Sample is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognized By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (No. Q - 1508 / 32 / 2007 - CPW)

(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Deta	ills		Sample Details	
Name:	M/s. Select City walk Mall a unit of Select infrastructure Pvt, Limited.		Sample Code	GCI/22/I20/S14
Address City walk, A-3, Dist	cture Pvt. Ltd., Select	Batch/Location	As per Table	
	City walk, A-3, District Centre, Saket.		Nature of Sample	Stack
	New Delhi - 1	10017	Sampling Instrument	Stack Monitoring Kit
Sampling I	Done By	Mr. Kartik	Date of Sampling	16/09/2022
Analysis St	arts on	18/09/2022	Policia de California de la companya del companya del companya de la companya de	tsokinetic Sompling.
CONTROL OF STREET		2425340 255 G.S	Sampling Method	IS:11255,PART-1,2,3
Analysis Completion On	ompletion On	21/09/2022	Sample Received Date	18/09/2022

Sr. No.	Particulars	Details	Unit
11:	Name Of Emission	D.G. Set 4	-
2	Rated Capacity	2000	KVA
3	Date of Manufacturing	09/2007	Month /Year
4	Make	Cummins	6
5	Engine Sr. No.	33163864	100
6	Name of the Plant/Section	DG Room	263
7	Normal Operating schedule of the Plant(Hrs/Day)	As & When Required	5.50
8	Capacity on Sampling Day	1260	kW
9	Stack Identification	Stack attached to D.G. Set No. 4	46
10	Material of Stack	Metal	(4)
11	Stack Height from G.L.	34	Mtr.
12	Diameter of Stack	45	cm
13:	Type of Stack	Round	**.
14	Fuel Type	H.S.D.	.#/
15	Fuel Consumption	360	Liter/Hr.
16	Flue Gas Temperature	288	*C
17	Velocity	17.6	m/s
18	Gas Volume	5006	Nm <sup>3</sup> /Hr.
19	Sampling Duration	30	Min.



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognized By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (No. Q - 1508 / 32 / 2007 - CPW) (ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### ANALYSIS REPORT

(For the Month of September- 2022)

Client Deta	ills		Sample Details	
Name	H. A.C. Develop Committee Co. Fr. St.	City walk Mall a unit of structure Pvt. Limited	Sample Code	GCI/22/I20/514
- 500 m m m m m m m m m m m m m m m m m m		structure Pvt. Ltd., Select	Batch/Location	As per Table
Address		-3. District Centre, Saket,	Nature of Sample	Stack
	New Delni-	110017	Sampling Instrument	Stack Monitoring Kit
Sampling I	ng Done By Mr. Kartik		Date of Sampling	16/09/2022
Analysis Starts on	18/09/2022	Sampling Method	Isokinetic Sampling, IS:11255.PART-1,2,3	

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Resulf	Emission Standard	Reference Method
1,	Particulate Matter (PM)	mg/nm³	19.4	75	IS 11255: Part I
2	NOx (as NO <sub>2</sub> )	ppmv	125.1	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	29.4	150	Non Dispersive Infrared
4,	NMHC (as C)	mg/Nm³	16.9	100	Gas Chromatograph- Flame Ionization Detector

Note: Generator sets commissioning Date – after 01, 07, 2005 (Emission Standards for Diesel Engines (Engine Rating more than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9th September, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



- Analysis is subject to the condition in Which the Sample is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.



0

Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognized By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1986) (No. Q - 1508 / 32 / 2007 - CPW)

(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Deta	alls		Sample Details	
Name	M/s. Select City walk Mail a unit of Select Infrastructure Pvt. Limited		Sample Code	GCI/22/I20/575
* 1.1.		octure Pvt. Ltd., Select	Batch/Location	As per l'able
Address	City walk, A-3, District Centre, Saket, New Delhi – 110017		Nature of Sample	Stack
	Mew Detail - 1	10017	Sampling Instrument	Stack Monitoring Kit
Sampling (	Done By	Mr. Kartik	Date of Sampling	16/09/2022
Analysis St		18/09/2022		Isokinetic Sampling.
Analysis Completion On			Sampling Method	IS:11255,PART-1,2,3
		21/09/2022	Sample Received Date	18/09/2022

Sr. No.	Particulars	Details	Unit
W.	Name Of Emission	D.G. Sel 5	-
2	Rafed Capacity	2000	KVA
3	Date of Manufacturing	09/2007	Month /Yea
4	Make	Cummins	17
5	Engine Sr. No.	33161107	ia.
6	Name of the Plant/Section	DG Room	
7	Normal Operating schedule of	As & When Required	
8	Capacity on Sampling Day	1200	kW
g:	Stack Identification	Stack attached to D.G. Set No. 5	
10:	Material of Stack	Metal	
11	Stack Height from G.L.	34	Mfr.
12	Diameter of Stack	45	cm
13	Type of Stock	Round	540.
14	Fuel Type	H.S.D.	-
15	Fuel Consumption	270	Liter/Hr.
16	Flue Gas Temperature	269	*C
17	Velocity	19.6	m/s
18	Gas Volume	4566	Nm³/Hr.
19	Sampling Duration	30	Min.



Integrated HSEQR Consulting Engineers, Scientists & Trainers (Recognized By Ministry of Environment, Forest and Climate Change, New Delhi Under EPA 1988) (No. Q - 1508 / 32 / 2007 - CPW)

(ISO 9001, 14001 & 45001 Certified Organizations)

Report No: - GCI/V/LAB/G0137/22/SP/22-23/September-00/0566

Date: 21/09/2022

#### **ANALYSIS REPORT**

(For the Month of September- 2022)

Client Deto	zils		Sample Details	
Name	M/s. Select City walk Mall a unif of Select Intrastructure Pvt. Limited		Sample Code	GC1/22/I 20/515
Address Select Infrastructure Pvt. Ltd., Select City walk, A-3, District Centre, Saket.	Batch/Location	As per Table		
	New Delhi - 110017		Nature of Sample	Stock
	New Delni - 1	0017	Sampling Instrument	Stack Monitoring Kit
Sampling (	Done By	Mr. Kartik	Date of Sampling	16/09/2022
Analysis St	arts on	18/09/2022		Isokinetic Sampling.
			Sampling Method	IS:11255.PART-1,2,3
Analysis Completion On	21/09/2022	Sample Received Date	18/09/2022	

#### STACK MONITORING RESULTS

Sr. No.	Parameter	Units	Result	Emission Standard	Reference Method
1,	Particulate Matter (PM)	mg/nm <sup>3</sup>	16.5	75	IS 11255; Part 1
2.	NOx (as NOz)	ppmv	135.9	710	IS 11255: Part 7
3.	Carbon Monoxide	mg/nm³	36.8	150	Non Dispersive Infrared
4	NMHC (as C)	mg/Nm³	19,7	100	Gas Chromatograph— Flame Ionization Detector

Note: Generator sets commissioning Date – after 01, 07, 2005 (Emission Standards for Diesel Engines (Engine Rating more - than 0.8 MW (800 KW) were notified by the Environment (Protection) Third Amendment Rules 2002, vide G.S.R. 489 (E), dated 9thSeptember, 2002 at serial no. 96, under the Environment (Protection) Act, 1986.)



- Analysis is subject to the condition in Which the Sample is received at our Laboratory.
- Reports cannot be used as an evidence anywhere including judiciary purpose without our prior permission.
- Sample will be retained till 15 days from the date of sampling.

# Annexure – 34

Work completion certificate of Solar power system (102 KW)

## JaaS Associates

Consulting Engineers, Contractors and Solar Experts PAN: AFUPG8421J GSTIN: 07AFUPG8421J1Z1

18 October, 2022

## Work Completion Certificate

This is to inform you that as per your work order "Project0029 (Rooftop solar)", M/s Jaas Associates have successfully Installed, Tested and Commissioned the 100.44 KW, Rooftop solar at Select CityWalk Mall, Saket District Centre, New Delhi-110017

Customer Care	Select Infrastructure Private Limited			
Site Address	Select CityWalk Mall , A-3 District Center, Saket, New Delhi- 110017			
Invoice No.	JaaS/22-23/12 dated 16-09-2022			
Work-order	Project0029(Rooftop Solar) dated 13-05-2022			
Commissioned On	14, September, 2022			
Project Value	INR 63,72,800.00			

Sunny George

Jaas Associates

New Delhi

Select Infrastructure Private Limited

Vidyanand Srivastava
